

LEGEND

- Compound
- Show Homes
2, 3, 4 - October 2022
Handover - 2025
- 1 March 2023 -
Private _ 1, 5, 7, 194-195 (6 plots)
- 2 April 2023 -
Private _ 8, 189, 191, 193 (5 plots)
- 3 May 2023 -
Private _ 149-156, 188, 190 (10 plots)
- 4 June 2023 -
Private _ 157, 185-187, (4 plots)
HA _ 136-138, 160-163, 170-175 (11 plots)
- 5 July 2023 -
Private _ 180 - 184 (5 plots)
- 6 August 2023 -
Private _ 176-179, 158-159 (6 plots)
- 7 September 2023 -
Private _ 164-169 (6 plots)
- 8 October 2023 -
Private _ 135 (1 plot)
- 9 November 2023 -
No plots
- 10 December 2023 -
Private _ 133-134, 127-128 (4 plots)
HA _ 129-132 (4 plots)

- 11 January 2024 -
Private _ 145-148 (6 plots)
- 12 February 2024 -
HA _ 9-16, 9 (8 plots)
- 13 March 2024 -
HA _ 17-23 (7 plots)
- 14 April 2024 -
Private _ 24-25 (2 plots)
- 15 May 2024 -
Private _ 34 - 37 (4 plots)
- 16 June 2024 -
Private _ 38-42 (5 plots)
- 17 July 2024 -
Private _ 43 - 47 (5 plots)
- 18 August 2024 -
HA _ 48 - 54 (7 plots)
- 19 September 2024 -
Private _ 30-33 (4 plots)
- 20 October 2024 -
Private _ 55-59 (5 plots)
- 21 November 2024 -
Private _ 66-71 (6 plots)
- 22 December 2024 -
Private _ 61-65 (5 plots)

- 23 January 2025 -
Private _ 72-75 (4 plots)
- 24 February 2025 -
Private _ 105-108 (4 plots)
- 25 March 2025 -
HA _ 101-104 (4 plots)
- 26 April 2025 -
Private _ 78-79 (2 plots)
HA _ 76-77 (2 plots)
- 27 May 2025 -
Private _ 97-100 (4 plots)
- 28 June 2025 -
Private _ 80-83 (4 plots)
- 29 July 2025 -
Private _ 84-87 (4 plots)
- 30 August 2025 -
Private _ 93-96 (4 plots)
- 31 September 2025 -
Private _ 92 (1 plot)
HA _ 88-91 (4 plots)
- 32 October 2025 -
Private _ 109-110 (2 plots)
- 33 November 2025 -
Private _ 11-113 (3 plots)
- 34 December 2025 -
Private _ 28-29, 60 (3 plots)



- 35 January 2026 -
Private _ 114-116 (3 plots)
- 36 February 2026 -
Private _ 26-27 (2 plots)
- 37 March 2026 -
Private _ 117 - 120 (4 plots)
- 38 April 2026 -
Private _ 121 - 126 (6 plots)
- 39 May 2026 -
Private _ 139 - 143 (5 plots)
- Completed

KEY:

- Road Installed
- Road In Process
- Road Not Installed

PEBBLE WALK

Appendix B: Site Traffic Management and Road Phasing Plan - March 2023

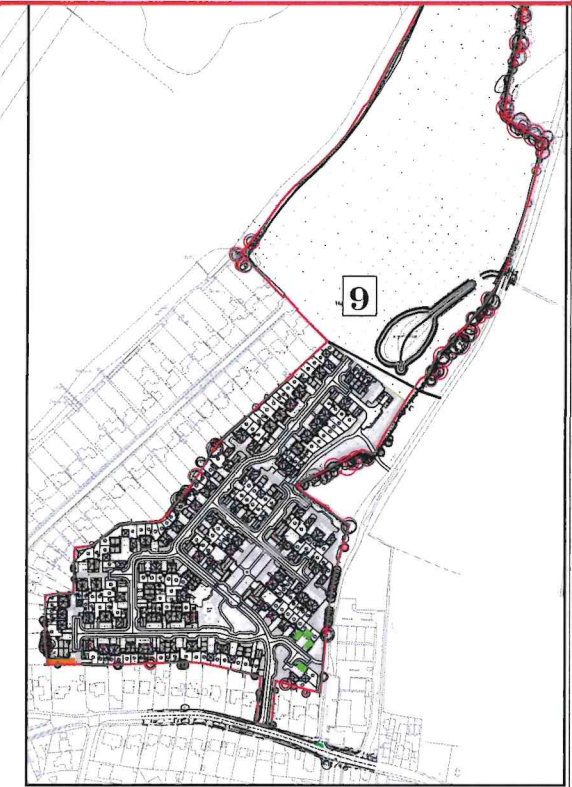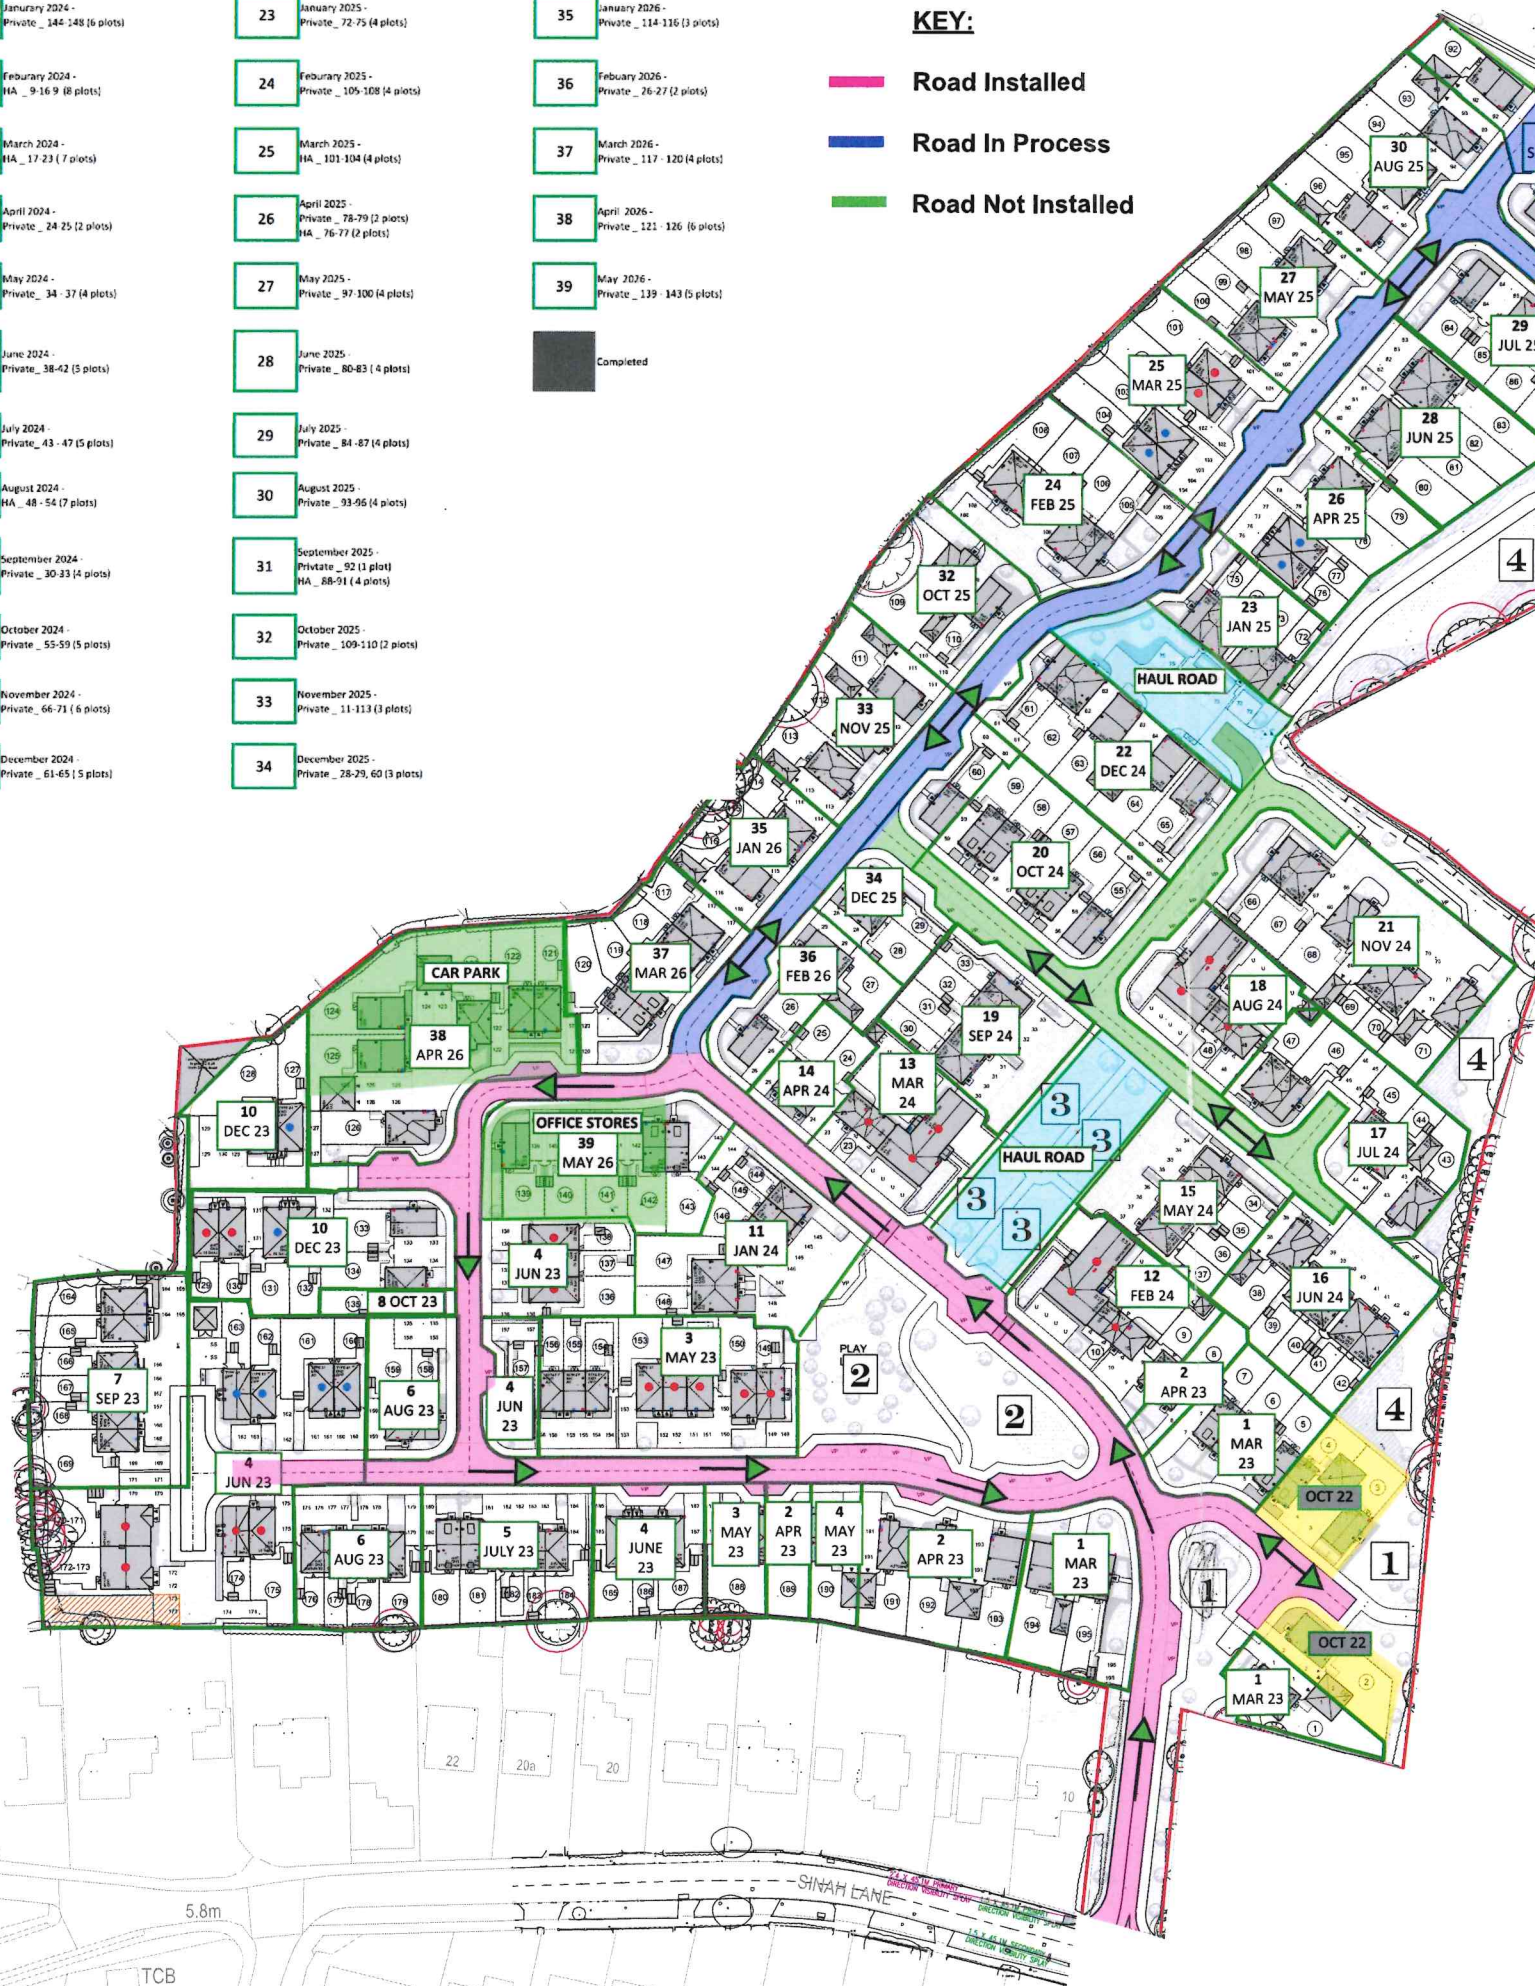

OVERALL SITE LAYOUT - n.t.s
