



Construction Environmental Management Plan (CEMP)

Masterplan Phase 1, Langstone
Park, Havant

October 2023

Construction Environmental Management Plan (CEMP)

Masterplan Phase 1, Langstone Park, Havant

12/10/2023

PRC Group
12 Warren Yard,
Warren Park,
Milton Keynes,
MK12 5NW

Document Control:

Project no.	Project
10538	Langstone Park, Havant

Version:	Written by:	Checked by:	Authorised by:	Date:
V1	Eleanor Curran	Paul Carter	Richard Schofield	1 st September 2023
V2	Eleanor Curran	Paul Carter	Richard Schofield	21 st September 2023
V3	Eleanor Curran	Paul Carter	Richard Schofield	12 th October 2023

This report has been prepared for the exclusive use of the commissioning party and may not be reproduced without prior written permission from Phlorum Limited.

All work has been carried out within the terms of the brief using all reasonable skill, care and diligence.

No liability is accepted by Phlorum for the accuracy of data or opinions provided by others in the preparation of this report, or for any use of this report other than for the purpose for which it was produced.

Phlorum Limited

Southern Office: Unit 12, Hunns Mere Way, Brighton, BN2 6AH

T: 01273 307 167 E: info@phlorum.com W: www.phlorum.com

Contents

1.	Introduction.....	1
2.	Purpose of CEMP	5
3.	Site Operations.....	7
4.	Biodiversity	9
5.	Noise, Visual and Vibrational Impacts	13
6.	Visual Screening for SPA birds	15
7.	Storage of Construction Materials, Chemicals and Equipment	16
8.	Dust Suppression	19
9.	Chemical and Fuel Run-off into Watercourses...	21
10.	Waste	23

Appendices

Appendix A – Risk Assessment - Ecology

Appendix B – Building B6000 Demolition Figure

Appendix C – Timetable of Ecological Works

1. Introduction

Background

- 1.1 Phlorum Limited was commissioned by PRC Group to compile a Construction Ecological Management Plan (CEMP) in relation to Masterplan Phase 1 which involves the demolition of building B6000 at Langstone Park, 2B Langstone Road, Havant, PO9 1SA here on referred to as 'the site'.
- 1.2 The National Grid Reference for the centre of building B6000 is SU 71341 05682. The survey area (building B6000) extends over approximately 1.1 hectares (ha). Langstone Park as a whole extends over 16 ha. Langstone Park lies directly below the A27 and Havant Bypass and is situated within the village of Langstone. Langstone is a part of the Borough of Havant, Portsmouth. 700m to the south is Southmoor Lake which feeds directly to the English Channel.
- 1.3 This document defines the range of general and specific measures to which the Main Client and its contractors shall adhere during the works, to comply with the Local Planning Authority's requirements. Condition 24 requires that a CEMP to be prepared for each phase of the development. As stated above Masterplan Phase 1 involves the demolition of building B6000.
- 1.4 Phlorum Ltd (Phlorum), as specialist environmental consultants experienced in the management of major construction projects, has been appointed by PRC Group to develop a CEMP which will be submitted to all contractors involved in the project. Compliance with the CEMP will be a mandatory contractual requirement under the provision of Condition 24 of the planning permission.

Proposed Development

- 1.5 It is understood that phase 1 of the proposed development involves the demolition of building B6000 to form a development platform. The materials from the demolition of B6000 will be stored on the B6000 development plot to be repurposed during the construction of a building adjacent to B6000 in phase 2 of the development. The B6000 development plot will be grassed over before the construction of a building on the B6000 development plot begins in phase 3 of the development.

Planning

- 1.6 Planning permission has been granted, subject to various conditions, which include the following ecological conditions:
 -  Condition 12: a detailed Ecological Mitigation, Compensation and Enhancement Strategy is required for each phase of development;

- Condition 24: a Construction Environmental Management Plan (CEMP) is required for each phase of development; and
 - Condition 33: details of the Ecological Mitigation, Compensation and Enhancement Strategy requirements secured under Condition 12 and how they relate to the relevant phase of development are required.
- 1.7 This Construction Environmental Management Plan (CEMP) has been produced to address the requirements of Condition 24.
- 1.8 Condition 24 states the following:

“Prior to the commencement of development in each phase (including demolition) a Construction Environmental Management Plan (CEMP) shall be submitted to and approved in writing by the Local Planning Authority for that phase. The CEMP shall include, but not be limited to, the following:

- *In relation to the impact on the strategic road network and environmental impacts*
- *Construction traffic routes and their management and control, parking and turning provision to be made on site, measures to prevent mud being deposited on the highway, adequate provision for addressing any abnormal wear and tear to the highway, and a programme for construction.*
- *Construction Traffic Management Plan (to include the co-ordination of deliveries and plant and materials and the disposing of waste resulting from demolition and/or construction so as to avoid undue interference with the operation of the public highway, particularly during the Monday-Friday AM Peak (0800-0900) and PM Peak (1630-1800) periods);*
- *an estimate of the daily movement of the construction traffic;*
- *the hours of construction work and deliveries;*
- *area(s) for the parking of vehicles of site operatives and visitors;*
- *area(s) for the loading and unloading of plant and materials;*
- *area(s) for the storage of plant and materials used in constructing the development;*
- *details of waste management arrangements;*
- *consideration of emissions to air, water and land. Including noise & vibration, dust, general discharges and appropriate mitigation strategies;*
- *the storage of materials and construction waste, including waste recycling where possible;*

-  *Risk Assessments and Method Statements for the works; and*
-  *contact details of personnel responsible for the construction works.*
-  *In relation to minerals recovery:*
 -  *A statement providing the following:*
 -  *a method for ensuring that minerals that can be viably recovered during the development operations are recovered and put to beneficial use; and,*
 -  *a method to record the quantity of recovered mineral (re-use on site or off site) and to report this data to the Local Planning Authority in consultation with the Minerals Planning Authority.*
-  *In relation to steps and procedures that will be implemented to avoid or mitigate constructional impacts on the adjacent Chichester and Langstone Harbours SPA, Ramsar and the SPA's functional land:*
 -  *Noise/visual/vibrational impacts*
 -  *Visual screening (for SPA birds)*
 -  *Storage of construction materials/chemicals and equipment;*
 -  *Dust suppression*
 -  *Chemical and/or fuel run-off from construction into designated sites*
 -  *Waste disposal.*
-  *All measures forming part of the approved CEMP for each phase of development including demolition shall be implemented in full through the course of development operations within that phase".*

- 1.9 This CEMP details the steps and procedures that will be implemented to avoid or mitigate constructional impacts on the adjacent Chichester and Langstone Harbours SPA, Ramsar and the SPA's functional land during the demolition phase of building B6000 only. A Construction Traffic Management Plan has been produced in a separate document by Hughes and Salvidge (2023) and seeks to manage impacts on the strategic road network. This has been prepared in accordance with the Framework CTMP required under Condition 8. A plan in relation to minerals recovery is not relevant to the demolition of B6000 as the works will not be penetrating into the ground to any significant degree and so the potential for minerals recovery is limited. Further CEMPs will be required for the other phases of the development.

Previous Reports

- 1.10 This document has been developed with reference to the findings contained within the previous Preliminary Ecological Appraisal (2022) compiled by Phlorum for Langstone Park (Masterplan). The survey area extended over approximately 16 hectares (ha).

CEMP Report

- 1.11 This document has been compiled in the context of the proposals stated in this introduction and based on information made available by the client at the time. Alterations to the scheme and changes in ecological legislation may necessitate amendments to this document at a later stage.

2. Purpose of CEMP

Purpose of the CEMP

- 2.1 The purpose of this CEMP is to set out the environmental criteria under which the works in phase 1 shall be carried out, taking account of relevant environmental legislation and prevailing standards of best practice.
- 2.2 The CEMP lays out the series of objectives and measures to be applied throughout the construction period to protect the environment and limit disturbance to residents and other sensitive receptors from construction activities. However, as stated before this CEMP relates only to phase 1 of the development which is the demolition of building B6000.
- 2.3 This CEMP sets out:
-  the general ecological principles to be applied during the demolition of building B6000 and the context within which mitigation measures will operate and be developed **[Section 4]**;
 -  the general environmental requirements that need to be considered and adopted during the demolition of building B6000 **[Sections 3 to 10]**; and
 -  steps and procedures that will be implemented to avoid or mitigate constructional impacts on the adjacent Chichester and Langstone Harbours SPA, Ramsar and the SPA's functional land:
 - Noise/visual/vibrational impacts **[Section 5]**;
 - Visual screening (for SPA birds) **[Section 6]**;
 - Storage of construction materials/chemicals and equipment **[Section 7]**;
 - Dust suppression **[Section 8]**;
 - Chemical and/or fuel run-off from construction into designated sites **[Section 9]**;
 - Waste disposal **[Section 10]**
- 2.4 The CEMP will form part of the environmental management measures to be implemented by the contractors. A review system will be developed to ensure that commitments entered into with the relevant local and statutory authorities are complied with. Where required, regular monitoring of environmental effects will be carried out by the contractors, or their consultants, in accordance with the requirements set out in the CEMP. The results of such monitoring will be audited by the Main Client and performance regularly reviewed with the contractors and the relevant authorities. This process will not remove any enforcement rights of local or statutory authorities but will help ensure potential problems are recognised and dealt with on a proactive basis.

- 2.5 The CEMP will be monitored by the contractor in conjunction with the Main Client as required. The CEMP will be revised for the various phases of the project, as required under Condition 24.

Relevant Legislation

- 2.6 The contractors will be required to comply with all relevant environmental legislation and Best Practice guidance during their work.
- 2.7 Protected species, including, species of reptiles and amphibians, all UK bats, the hazel dormouse dormice, otter, water voles and nesting birds are protected under the Wildlife and Countryside Act 1981 (as amended). Some rare bird species also receive protection under Schedule 1 of the Act. European protected species also receive protection under the Conservation of Habitats and Species Regulations 2010 (as amended). Badgers are afforded protection under the Protection of Badgers Act 1992.

Structure and Responsibility

- 2.8 The contractor shall identify the management structure responsible for implementing the CEMP. The CEMP will provide an overall management structure for ensuring and demonstrating compliance with contractor's environmental commitments, policies and objectives. This will include a programme of monitoring and auditing.
- 2.9 On tendering for the contract, the contractors shall nominate a suitably experienced manager to take responsibility for all issues associated with the environment. This shall include environmental management and compliance with all appropriate legislation and regulations and the development, implementation, monitoring, audit and updating of the CEMP.

Training

- 2.10 The contractor shall be responsible for identifying the training needs of staff to ensure that all personnel whose work may cause an impact on the environment receive appropriate environmental training. Training and awareness should include:
-  briefing staff on the role of the CEMP;
 -  provision of environmental elements in site induction talks; and
 -  giving Toolbox Talks on specific issues such as noise prevention, spillage prevention, and ecological protection etc.
- 2.11 All operatives on site will have appropriate Construction Industry Council Scheme (CSCS) or equivalent cards.

3. Site Operations

Worksite Layout and Appearance

3.1 The contractors shall take account of the following:

-  where the site is not naturally protected by existing fencing, or other barriers, temporary hoardings or fences may need to be erected to maintain public safety, prevent visual intrusion and if necessary, provide noise shielding;
-  the main client may require that hoardings include publicity information about the progress of the works, where appropriate;
-  it is understood that Condition 36 requires details of proposed lighting for each phase of development. It is proposed that there will be no lighting for the demolition of B6000 and all work will be carried out during daylight hours. However, there is already existing lighting present in the wider area of Langstone Park, including security lighting. In the event that lighting is used for security and safety, it will be of a standard and arrangement acceptable to the reasonable requirements of the LPA, so as to prevent interference with local residents, local businesses, or sensitive wildlife areas. If lighting for night work is required, some impact from lights may be unavoidable. In these instances, lights should be screened, where possible, and directed downwards and away from properties;
-  security measures should be implemented by the contractors to prevent unauthorised entry to, or exit from, the site; and
-  due to the space on the site and the sensitivity of the nearby Chichester and Langstone Harbour Ramsar and Special Protection Area (SPA), the contractors should ensure that no accommodation areas are provided for workers on the site.

Working Hours

- 3.2 The proposed working hours for the site will be, 08:00 to 18:00 hours, Mondays to Fridays and 08:00 to 13:00 hours on Saturdays, with no work on Sundays or Bank Holidays.
- 3.3 Whilst most work in phase 1 is likely to be possible during core working hours. It is possible that the special delivery of oversized plant and equipment (e.g. cranes), which may be required outside core hours, to ensure a limited impact as possible on the surrounding highways.

- 3.4 Occupiers of nearby residential properties will be informed in advance of the works taking place and their duration. In the case of work required in response to an emergency, the local authority and local residents will be advised as soon as is reasonably practicable that the works are taking place and their likely duration.

Good Housekeeping

- 3.5 Under the terms of the contract the contractors will follow a "good housekeeping" policy at all times. This shall include but not necessarily be limited to:
-  considerate site behaviour of contractor staff;
 -  prohibition of open fires;
 -  appropriate provisions for dust control and road cleanliness;
 -  the cleansing of wheel washing facilities, as necessary;
 -  frequent inspection of hoardings, their repair and re-painting, as necessary;
 -  provision and maintenance of toilet and other welfare facilities;
 -  the removal of food waste;
 -  removal of rubbish at frequent intervals, leaving the site clean and tidy;
 -  the prevention of vermin and other infestations; and
 -  site lighting should not cause undue intrusion to residential properties.
- 3.6 The project will be carried out in compliance with the Considerate Constructors Scheme, or similar standard.
- 3.7 Work site inspections will be carried out by nominated representatives from the contractors and in addition, regular inspections will be carried out by the main client or its consultants. The main client will audit the implementation of the contractors works in accordance with the CEMP and all safety procedures.
- 3.8 The site manager will be responsible for carrying out daily inspections of any ecological barriers, fences, signs and ecological areas, to ensure that no repair work is required. Plus the daily site checks will also ensure that the workers on site have not moved these protective fence/barriers, signs or impacted on ecological areas.

4. Biodiversity

Objective

- 4.1 The contractors shall comply with the relevant statutory provisions in respect of the protection of areas of nature conservation interest and of protected species and will control and limit, as far as reasonably practicable, any disturbance to such areas and such species.
- 4.2 Where species are protected by specific legislation, the contractors shall follow approved guidance to comply with those requirements and allow sufficient time for any licences or consents to be obtained.
- 4.3 The masterplan site comprises of buildings, hardstanding, amenity grassland, broad-leaved semi-natural woodland, introduced shrub, scattered trees, standalone trees, ruderal vegetation and running water and a dry ditch. However, around building B6000 there is mainly hardstanding, amenity grassland and neighbouring onsite buildings. There are trees including lime (T64), pear (T65, T66, T67 and T68), Norway maple (T70) and Indian bean (T69) trees to the east, south and west of the building. The Building B6000 Demolition Figure (Appendix B) shows that in phase 1 the building B6000 is being demolished and an area of hardstanding and external structures are being removed, alongside the removal of the trees adjacent to B6000.
- 4.4 During the PEA (2022), it was found that the Langstone Park masterplan offered low potential for roosting bats, moderate potential for breeding birds, low potential for foraging badgers, low potential for hazel dormice, low potential for reptiles, moderate potential for breeding, commuting and foraging water voles, moderate potential for breeding and commuting otters, high potential for stag beetles, and high potential for hedgehogs. During the PEA survey, specimens of cotoneaster were seen. Five species of cotoneaster are listed as non-native invasive species under Schedule 9 Part II of the Wildlife and Countryside Act (WCA) (1981 amended). Buddleia were also seen which is not listed under Schedule 9 Part II of the WCA but appears on the Non Native Species Secretariat (NNSS, 2019).
- 4.5 However, around building B6000 potential populations of badger, dormice, water voles, otters, stag beetles and hedgehogs will not be affected by the demolition works. Furthermore, at the time of the PEA, building B6000 did not offer potential for roosting bats. As a result, currently the main protected species that could be impacted by the demolition of building B6000 are nesting birds.

Risk Assessment

- 4.6 A risk assessment has been carried out of the potentially environmentally damaging activities on site. These include the following:



Demolition;

-  Potential impact on nesting birds;
-  Invasive plant species;
-  Dust /silt pollution; and
-  Potential pollution incident of the ground.

4.7 A risk assessment for the ecological issues is provided in Appendix A.

Control Measures

Ecological Receptor Location

4.8 An ecological receptor location, will be maintained on site, away from the works area at all times, in case any protected species are discovered during the works. This receptor location will be outside the footprint of the works area but within the site boundary. The receptor location will be an area which will not be disturbed by the future works on site. The area of scattered trees and broad-leaved semi-natural woodland to the southeast of B6000 is being retained so has been identified as a suitable ecological receptor location.

Demolition Works

4.9 The building B6000 is to be demolished during phase 1 of the development. An ecological watching brief is not required for this process but a suitably qualified ecologist will perform a walkover of the site before works commence. The ecologist will give a toolbox talk to ensure all construction staff on site are aware of the potential protected species on site. If any protected species are found onsite during the demolition and construction phase all works will cease, and a suitably qualified ecologist should be contacted immediately.

4.10 Appendix B provides a figure showing the location of building B6000.

Vegetation Clearance

4.11 The trees adjacent to B6000 are being removed. An ecological watching brief is not required for this process but a suitably qualified ecologist will perform a walkover of the site before works commence. The ecologist will give a toolbox talk to ensure all construction staff on site are aware of the potential protected species on site. If any protected species are found onsite during the demolition and construction phase all works will cease, and a suitably qualified ecologist should be contacted immediately.

Tree Protection

- 4.12 All trees adjacent to B6000 are being removed prior to the demolition of B6000. There is an area of scattered trees and broad-leaved semi-natural woodland 50m to the southeast of B6000 which are being retained. However, the demolition works will be contained within the central part of the site and access to the compound will be from the west. Therefore, the root protection areas of retained trees will not be affected by disturbance, contamination and compaction during the proposed works.
- 4.13 Tree protection fencing and temporary ground protection are not required for the demolition of B6000.

Light

- 4.14 It is understood that Condition 36 requires details of proposed lighting for each phase of development. It is proposed that there will be no lighting for the demolition of B6000 and all work will be carried out during daylight hours. However, there is already existing lighting present in the wider area of Langstone Park, including security lighting. In the event that lighting is used for security reasons at night, then it must be reduced as much as possible to ensure no, or limited, impact on wildlife, such as bats. This will involve ensuring that:
-  No lights are directed at any boundary features such as trees;
 -  Shields/hood are used on lights to reduce light spill and glare; and
 -  Lights are turned off when not needed, and so timers and/or sensors are used to controls the lights where possible.

Nesting Birds

- 4.15 A suitably qualified ecologist will check the site for active nests and signs of bird breeding activity before demolition begins. This will include ground nesting birds. If any nests are found then a buffer area will be created around the nest, and left until the birds have fledged. The buffer area should be fenced off and appropriate warning signs attached so staff know why it is fenced off.

Invasive Plant Species

- 4.16 The contractors will not knowingly introduce or cause to grow in the wild, species specified in Schedule 9 Part II of the Wildlife and Countryside Act 1981 (as amended).
- 4.17 During the PEA survey, no invasive plant species were seen in the B6000 area. If any invasive species are discovered, the contractors will have to ensure that all staff are informed of their presence and the appropriate controls are kept in place. Any work carried out in invasive plant areas should be supervised by a suitably qualified invasive plant specialist.
- 4.18 Appendix B provides a figure showing the location of B6000.

Timing of Sensitive Works

- 4.19 Any clearance of sensitive ecological habitats will need to be supervised by a suitably qualified ecologist. The building B6000 has the potential to be used by breeding birds such as gulls. Likewise, the trees adjacent to B6000 that are being removed have the potential to support breeding birds. The trees that have been identified as being removed do not have any potential features to support bats. An ecological watching brief is not required for the demolition of B6000 or removal of the identified onsite trees but a suitably qualified ecologist will perform a walkover of the site before works commence. The ecologist will give a toolbox talk to ensure all construction staff on site are aware of the potential protected species on site. If any protected species are found onsite during the demolition and construction phase all works will cease, and a suitably qualified ecologist should be contacted immediately.
- 4.20 Appendix C provides a timetable for the ecological works.

Protection of Habitats – Biodiversity Protection Zones

- 4.21 The principal contractor will be responsible for ensuring that the areas of vegetation outside the B6000 development site are protected during the demolition phase. This will create Biodiversity protection zones which will be protected during the works. This includes the area of scattered trees and broad-leaved semi-natural woodland to the southeast of B6000 that is being retained so has been identified as a suitable ecological receptor location. The use of protective fences and exclusion barriers are not required for this area. However, contractors will need to be informed that the biodiversity protection zone is protected and must not be damaged.

5. Noise, Visual and Vibrational Impacts

Objective

- 5.1 The contractors will control and limit noise and vibration levels during the demolition phase, so far as is reasonably practicable, so that residential properties and all other sensitive receptors including the nearby Chichester and Langstone Harbour Ramsar and Special Protection Area (SPA) are protected from excessive noise and vibration levels arising from the works. Visual impacts of the development on the surrounding area will also be minimised where possible. The contractors will be required to demonstrate that Best Practicable Means (BPM) has been applied to all activities and through the design of the developments.

Sensitive Receptors

- 5.2 The PEA desk study has shown the site to be predominantly industrial, with buildings and hardstanding. Within the wider vicinity, the area is mainly industrial and residential. To the south there is areas of large open green space, and there are woodland pockets between industrial sites and residential streets. The closest roads are the A27 to the north, Langstone Road to the east and Southmoor Lane to the west. Building B6000 is bordered by adjacent buildings in Langstone Park.

Noise and Vibration Control Measures

- 5.3 It is understood that Condition 9 states that the use of piling and large machinery are not permitted so will not be used for the demolition of B6000. The implementation of measures consistent with the recommendations contained within BS 4142:2014+A1:2019 are therefore not relevant to the development. If this changes and excessive machinery is used, measures to implement BPM may be required and may include:
-  careful selection, maintenance and location of plant, demolition methods and programming. Only plant conforming with relevant national or international noise emission standards and directives shall be used;
 -  design and use of site hoardings and other temporary screens, where practicable and necessary, to provide acoustic screening at the earliest opportunity;
 -  where practicable, appropriate choice of methods, routes and programming for the transport of demolition materials, waste and personnel by road;

-  erection of any noise barriers, should be considered if necessary during the demolition process, to provide additional protection against demolition noise;
-  monitoring and reporting of demolition noise and vibration at sensitive locations, as required. Details subject to consultation with the LPA; and
-  assessment of potentially significant noise and vibration sources, including a review of potential impacts from alternative techniques and suitable mitigation, to ensure BPM.

Visual Control Measures

- 5.4 Neighbouring buildings in Langstone Park and offsite features such as buildings, roads and vegetation provide a visual barrier between the site and nearby Chichester and Langstone Harbour Ramsar and Special Protection Area (SPA).
- 5.5 Where possible, machinery used should be below the height of nearby buildings.

6. Visual Screening for SPA birds

Objective

- 6.1 Chichester and Langstone Harbour has been designated as a Ramsar and Special Protection Area (SPA) for the internationally important populations of wintering wildfowl and wintering waders it supports. The estuarine basins comprise sand and mudflat, which are exposed at low tide. These habitats support rich assemblages of invertebrates and algae beds, which are important for colonies of breeding terns and wintering birds. Its qualifying species are:
-  breeding little tern (*Sterna albifrons*) and sandwich tern (*Sterna sandvicensis*);
 -  overwintering bar-tailed godwit (*Limosa lapponica*) and little egret (*Egretta garzetta*);
 -  migratory ringed plover (*Charadrius hiaticula*), black-tailed godwit (*Limosa limosa islandica*), dark-bellied brent goose (*Branta bernicla bernicla*), dunlin (*Calidris alpina alpina*), grey plover (*Pluvialis squatarola*), redshank (*Tringa tetanus*) and ringed plover (*Charadrius hiaticula*); and
 -  an assemblage of at least 20,000 waterfowl.
- 9.3 The PEA survey (2022) found that the site does not support any features that contribute to the ecological designations of Chichester and Langstone Harbour.

Visual Screening

- 6.2 The site is predominantly industrial, with buildings and hardstanding. Within the wider vicinity, the area is mainly industrial and residential. To the south there is areas of large open green space, and there are woodland pockets between industrial sites and residential streets. The closest roads are the A27 to the north, Langstone Road to the east and Southmoor Lane to the west. Building B6000 is bordered by adjacent buildings in Langstone Park.
- 6.3 The onsite and offsite features that are already present are deemed to be sufficient visual screening between the proposed demolition of B6000 and Chichester and Langstone Harbour where SPA birds are present.

7. Storage of Construction Materials, Chemicals and Equipment

Objective – Pollution Incidents

- 7.1 A pollution incident could occur in various ways, such as: dust blown off site on to ecological area; silt run off into adjacent water courses; surface water run-off into a surface water drain; or a fuel/chemical spillage/leak.
- 7.2 It is particularly important that no pollution incidents occur that may impact the nearby Chichester and Langstone Harbour designated site which is 0.4km south of Langstone Park.
- 7.3 As part of the implementation of the CEMP, the contractors shall provide pollution incident control measures, in conjunction with Principal Contractor and its consultants and relevant authorities, to provide a rapid response to any uncontrolled releases or pollution incidents arising from the works.
- 7.4 The pollution incident control measures will set out systems to ensure that pollution effects upon people, land, air and water are contained and minimised and clean-up procedures are developed to respond effectively once an incident is discovered. The pollution incident control measures will also contain guidance on the storage and containment of any hazardous substances.

Pollution Incident Control Plan and Emergency Contacts Procedures

- 7.5 The contractors shall prepare, maintain and provide an Emergency Contacts List and Procedures for the site, in consultation with the Principal Contractor and its consultants, the LPA, Fire Brigade, Police, Ambulance Service, relevant Statutory Authorities and affected neighbours. These Procedures shall be followed in any site emergency.
- 7.6 The procedures will contain emergency contact phone numbers and the methods for notifying the LPA and the Emergency Services for action by the contractors and the site staff. The procedures shall be agreed with the LPA, relevant statutory authorities and Emergency Services.
- 7.7 These controls will include:
 -  Ensure that no spoil heaps are located near sensitive areas, such as the surface water course/surface water drains. If this is not possible and spoil heaps are located near surface water drains, the use of drain covers are required;

-  Ensure that spoils heaps, stores of dry materials, and haul roads are regularly sprayed with water, as required;
-  Silt traps are used if any works occurring near the water bodies on site;
-  Fuel, oils and chemicals stored in bunded containers with at least 110% capacity (as primary containment).
-  Drip trays used under single container, plant or generators, must have, as a secondary containment, 110% capacity,
-  Drip trays, or other secondary containment, for multiple containers must have capacity for whichever is greatest, either 25% of the combined capacity of all the containers, or 110% capacity of the largest container.
-  Spill response kits on site; and
-  Staff trained in use of spill response kit.

Objective – Silt Runoff

- 7.8 The contractors shall take all necessary measures to avoid significant environmental effects arising from silt run off. This could be from silt entering a water course or from silt entering a surface water drain. Prior to the commencement of work, the contractors shall develop specific measures to limit silt run-off at source as part of the development of the CEMP.
- 7.9 This is particularly important due to the close proximity of the site to the Chichester and Langstone Harbour designated site which is 0.4km south of Langstone Park.

Surface Water Control Measures

- 7.10 Silt pollution can damage and kill aquatic life by smothering and suffocating. This can result in killing fish and plants due to the restriction of oxygen levels and removal of sunlight. Plus, it can also cause flooding by blocking culverts, drains, and channels. Preventing this is particularly important due to the close proximity of the site to Chichester and Langstone Harbour designated site which supports internationally important populations of birds.
- 7.11 Measures to control silt run off will include one or more of the following practices as appropriate:
-  Store fine material away from a water course or drain;
 -  cover stockpiles;
 -  install silt traps, sumps, cut off trenches, if silt run-off is likely to impact on a water course or drain;
 -  normally a double containment system will be required to control silt run-off, so if one fails the second one still works;
 -  When de-watering an excavation do not discharge directly to a water course or drain;

-  Limit any excavation close to a water course;

Monitoring

- 7.12 The contractor shall undertake regular monitoring on site to ensure that silt run-off is not impacting on a water course or surface water drain.

8. Dust Suppression

Objectives

- 8.1 The contractors shall take all necessary measures to avoid significant environmental effects arising from dust or fumes from road, or contract plant sources or any other airborne pollutants. Prior to the commencement of work, the contractors shall develop specific measures to limit dust and fume emissions at source as part of the implementation of the CEMP, such as Environmental Monitoring Procedures in accordance with Best Practicable Means (BPM).

Dust Control Measures

- 8.2 The contractors shall take all reasonably practicable measures to avoid creating a dust nuisance and shall propose measures acceptable to the LPA, prior to commencing work.
- 8.3 In the event that processes cause, or are likely to cause, the release of quantities of dust into the atmosphere, the contractors will undertake appropriate mitigation at source to minimise any emissions.
- 8.4 Measures to control the propagation of dust will include one or more of the following practices, as appropriate:
-  provide easily cleaned and properly drained hardstanding areas for vehicles entering, parking and leaving the site, with appropriate wheel washing facilities, including sumps and catchpits, which shall be kept clean by regular brushing and water spraying;
 -  site hardstanding areas will be kept free of any mud or debris deposited by site vehicles on roads or footpaths in the vicinity of the site;
 -  regularly damp down unsurfaced haul routes and verges as well as cleaning these areas where they are located close to sensitive locations and provide sealed surfacing, in order to prevent soil contamination;
 -  establish and enforce appropriate speed limits over any unmade surfaces, in order to minimise the creation of dust;
 -  control the cutting or grinding of materials on site, such that any dust created by these processes is minimised and does not migrate off the site, nor pose any significant environmental risks;
 -  vehicles loading and unloading dusty material should be screened and the material damped down;
 -  ensure that all vehicles are adequately sheeted; and
 -  store materials, as far as possible from the site boundaries and sensitive receptors taking the prevailing wind direction into account.

Monitoring

- 8.5 The contractor shall undertake dust monitoring at sensitive locations such as roads, as necessary.

9. Chemical and Fuel Run-off into Watercourses

Objective

- 9.1 The contractors will implement working methods to protect, so far as is reasonably practicable, surface and groundwaters from pollution and other adverse impacts arising from the works, including changes to water levels, flows and quality. This is particularly important due to the close proximity of the site to Chichester and Langstone Harbour designated site.

Sensitive Receptors

- 9.2 The closest ecological statutory designated area is Chichester and Langstone Harbour Ramsar and Special Protection Area (SPA) which is 0.4km south of Langstone Park. Chichester and Langstone harbours are also both designated at Sites of Special Scientific Interest (SSSI).

Hydrology & Aquatic Resources Control Measures

- 9.3 Discharges to controlled waters, whether ground or surface, will only be permitted where levels of contaminants in appropriately treated wastewater are demonstrated to be acceptable to the EA.
- 9.4 If water is discharged either to a controlled water source or a sewer, then appropriate discharge consent license will be obtained.
- 9.5 It is understood that excavation works will not be below the water table. However, if this changes, prior to any excavations works below the water table, including any site de-watering, the contractors will inform the EA of the works to be carried out and obtain the appropriate consents and/or licences.
- 9.6 The contractors shall ensure the following: the requirements of consents for discharges to controlled waters shall be complied with, including any requirements for monitoring and reporting of results to the appropriate authority.
- 9.7 Appropriate measures will be taken to ensure that any oil interceptors and sediment settlement or other treatment facilities used if required are regularly inspected and maintained and that a full record is kept of inspections, maintenance works and measures taken to sustain equipment performance; and applications for Trade Effluent Consents shall be made to the relevant water company for any discharge into a sewer.

- 9.8 The contractors will make provisions for the control of hazardous substances, including oil drums/fuel stores or containers on site, in accordance with COSHH regulations. Such items are to be properly banded so that in the event of spillage or leakage, no oil or other contaminants are allowed to reach water courses or groundwaters, including aquifers.

10. Waste

Objective

- 10.1 The contractors will be required to carry out the works in such a way that, as far as is reasonably practicable, the amount of waste to be disposed of is minimised and that any waste arising from the sites is properly classified and dealt with in accordance with the appropriate legislation.

Waste Control Measures

- 10.2 As part of the implementation of the CEMP, the contractors will identify the: waste categories; waste quantities; opportunities for recycling and/ or reuse; disposal routes; and licensing requirements, for all waste arising from the works. An audit programme will be undertaken by the contractors to demonstrate that any waste removed is received at an appropriately licensed waste facility.
- 10.3 It is understood that the materials from the demolition of B6000 will be stored on the B6000 development plot and then repurposed during the construction of a building adjacent to B6000 in phase 2 of the development.
- 10.4 The contractors will comply with the appropriate guidance notes and statutory procedures in the identification, handling, storage, recovery and disposal of waste.
- 10.5 Where possible all waste will be reduced, reused and recycled prior to landfilling. All hazardous waste will be segregated. Site office waste would be collected separately to maximise the opportunities of recycling.
- 10.6 All waste removed from site will have an appropriate filled out waste transfer note, and/or consignment note. These notes will be kept as a minimum for two to three years respectively.

Waste Storage

- 10.7 Before being repurposed in phase 2 of the development, the materials from the demolition of B6000 will be stored on the B6000 development plot rather than the phase 2 development plot in order to reduce any impacts on Chichester and Langstone Harbour because B6000 is further from the designated site.
- 10.8 The site office waste and site office recycling waste will be located in/ or next to the site compound.
- 10.9 The general site waste will be stored in dedicated storage areas close to the site compound. This will include dedicated hazardous waste storage containers/areas.

Monitoring

- 10.10 As part of the implementation of the CEMP, the contractor shall produce a procedure to review the environmental capabilities of sub-contractors, including waste carriers and disposal sites and ensure that they are regularly audited.
- 10.11 Checks will also be carried out to ensure that there are appropriate, and filled out, waste transfer notes and consignment notes are being kept.

Appendices

Appendix A

Risk Assessment

RISK ASSESSMENT: Biodiversity Method Statement

Job Number: 10538

Job Title: Langstone Technology Park, B6000 demolition



Activity or work to be undertaken	Description of working environment
Phase 1 of the development: demolition of building B6000.	Demolition of the site.

People at risk	Phlorum workers including temporary workers, plus the main contractor workers
----------------	---

Hazard	Cause and potential consequence	Risk rating (RR) before control			HC E S EC AC PPE	Control measures	Risk rating (RR) after control		
		S	L	Initial RR			S	L	Final RR
Demolition	Demolition work may cause harm to wildlife.	5	5	25	EC AC PPE	A suitably qualified ecologist will perform a walkover of the site before works commence. The ecologist will give a toolbox talk to ensure all construction staff on site are aware of the potential protected species on site. If any protected species are found onsite during the demolition phase all works will cease, and a suitably qualified ecologist should be contacted immediately.	3	3	9
Failure of ensuring legal compliance	Working resulting in legal offence and potential prosecution as a result of impact on protected ecological habitat or species.	5	5	25	AC	Certain ecological habitats and species are protected under UK legislation. Some habitats/ species are protected under International law. Ensure all works complies with the appropriate legislation. Ensure ecological surveys are carried out prior to any works. Ensure that any works that impacts on protected habitats or species has the appropriate licences/approval, and the works are supervised by an ecologist, as required.	3	3	9
Work near nesting birds	Kill, injury, or take any wild bird, or eggs, or destroy any wild bird nest. Additional protection for a Schedule 1 listed bird (under the Wildlife and Countryside Act 1981).	5	4	20	AC	If nests are found then an exclusion zone must be secured around them. This zone must remain in place until the young have fledged.	4	3	12
Work near invasive plants	Spread of invasive plants. Certain non-native invasive plants are listed in Schedule 9 of the Wildlife and Countryside Act 1981, where it is illegal to plant or otherwise allow them to grow in the wild, which also means it illegal to allow them to grow across a site boundary.	4	4	16	AC	If any invasive plant species are identified on site during demolition, they will need to be appropriately managed: Ensure that an invasive plants expert (member of the Property Care Association Invasive Weed Control Group PCA IWCG) is used to supervise the control, and or treatment of the invasive plant. A herbicide spraying program could take several years before the plant's growth is controlled. If the invasive plant is left on site then it needs to be fenced off to prevent unauthorised access into the area which could result in its spread across the site, or even off site.	3	3	9
Work near trees	Tree Preservation order (TPO) can be applied to any trees and makes it an offence to cut down, top, lop, uproot or wilfully damage the tree. BS 5837 provide guidance on trees and includes root protection areas (RPA).	4	4	16	EC	No work in the demolition of B6000 phase of the development should occur near retained trees on site. If this changes: Ensure that protective fences are installed around the root protection area of all trees retained on site. Signage will also need to be installed on the fences warning workers what the area is. If any works are required in the fence of areas then approval will need from the local tree officer. Ensure no plant or materials are stored within the RPA of trees.	3	3	9
Pandemics	Spreading or contracting a pandemic, resulting in illness, time in hospital, and/or death	5	3	15	AC	Follow Government guidance, and provide this guidance to staff. This may include appropriate welfare facilities, with soap/sanitiser. At times this may result in keeping appropriate distance away other people, such as 2m apart. Employees should cough or sneeze into their elbow, or use a tissue and then bin the tissue. This will reduce the spread of many illnesses including common coughs and colds, as well as some more serious pandemics.	4	3	12

Fuel, oil or chemical spillage	Fuel, oil or chemical spillage resulting in contamination of an ecological habitat and/or species	2	5	10	EC	Without appropriate mitigation, spillages would pose a risk to the nearby SPA. Ensure all fuel/chemicals are stored in bunded area (110% capacity). Ensure that there is a spill response kit on site and staff trained in how to use it. Ensure spillage and used spill kit is removed off site as hazardous waste. Use drip trays under plant to reduce a pollution incident. Store fine material, such as soil, sand, away from any water courses.	2	3	6
Insect bites (e.g. wasps, bees, and hornets) and bites from other animals (e.g. bats, and snakes).	Site works may results in wasps nests being disturbed and stinging operatives. Scratches and bites from bats could result in salmonella and or malaria.	5	2	10	AC	Ensure that all workers have informed the top management if they are allergic to insects stings. If wasps, hornets, bees nests are known, or discovered in an area, then do not work in the area until the nest is removed. Workers that are allergic to insects bites should always carry with them a suitable treatment system. Ensure gloves are worn if bats need to be handled. Only qualified and licensed workers to handle bats. Ensure that that malaria jabs are taken by all workers likely to handle bats.	3	1	3
Cuts and stings from vegetation, such as nettles, brambles and giant hogweed.	Surveying sites can result in walking through dense vegetation which could result in nettles stings, or cuts from brambles and thorns..	2	5	10	PPE	Ensure that workers wear long trousers and sleeves when surveying sites. Where possible cut paths through vegetation prior to walking through. Clean any cuts with clean water. Wear gloves, where necessary.	2	3	6
General vegetation clearance	Destruction of general habitat on site.	3	3	9	AC	Clearance work to occur out of between March and September, inclusive, which is outside their less active period. Ensure an ecologist carries out a walkover of the site prior to the removal of trees.	3	2	6
Use of artificial lights	Lights can have an impact on wildlife, particularly bats	3	3	9	EC	It is understood that no lighting is being used for the demolition of B6000 and all work is being carried out in daylight hours.	1	1	1
Dust and silt	Dust and particles could result in poor eye sight, and breathing problems. Dust also cover plants reducing their potential to photosynthesise. Silt run of can impact on water courses impacting plants and animals.	3	2	6	PPE. EC	Ensure appropriate PPE is used as required when conditions are dusty. Use water spray on hauled roads and spoil heaps. Keep spoil heaps away from sensitive ecological areas. Ensure waste lorries are sheeted. Ensure speed limit on site is maintained.	3	1	3
Excavating trenches	Trips and falls into uncovered trenches. Wildlife can fall in and get trapped in trenches.	3	3	9	EC AC PPE	Ensure workers are informed about the presence of trenches. Cover or fence off trenches as required. Ensure appropriate PPE is used as required. Ensure that excavations are covered at night or a ramp installed to allow wildlife to escape such as badgers, otters or other small mammals	2	1	2
Noise	Workers may experience noisy environments while working onsite. Noise can also cause disturbance to wildlife.	3	2	6	PPE	Ear plugs are provided to all workers for work onsite.	2	1	2


Further information

Risk Matrix Table 1. method statement.

	Name:	Position	Date
Prepared by:	Eleanor Curran	Environmental Consultant	19/09/2023
Checked by:	Paul Carter	Principal Environmental Consultant	19/09/2023

Appendix B

Building B6000 Demolition Figure

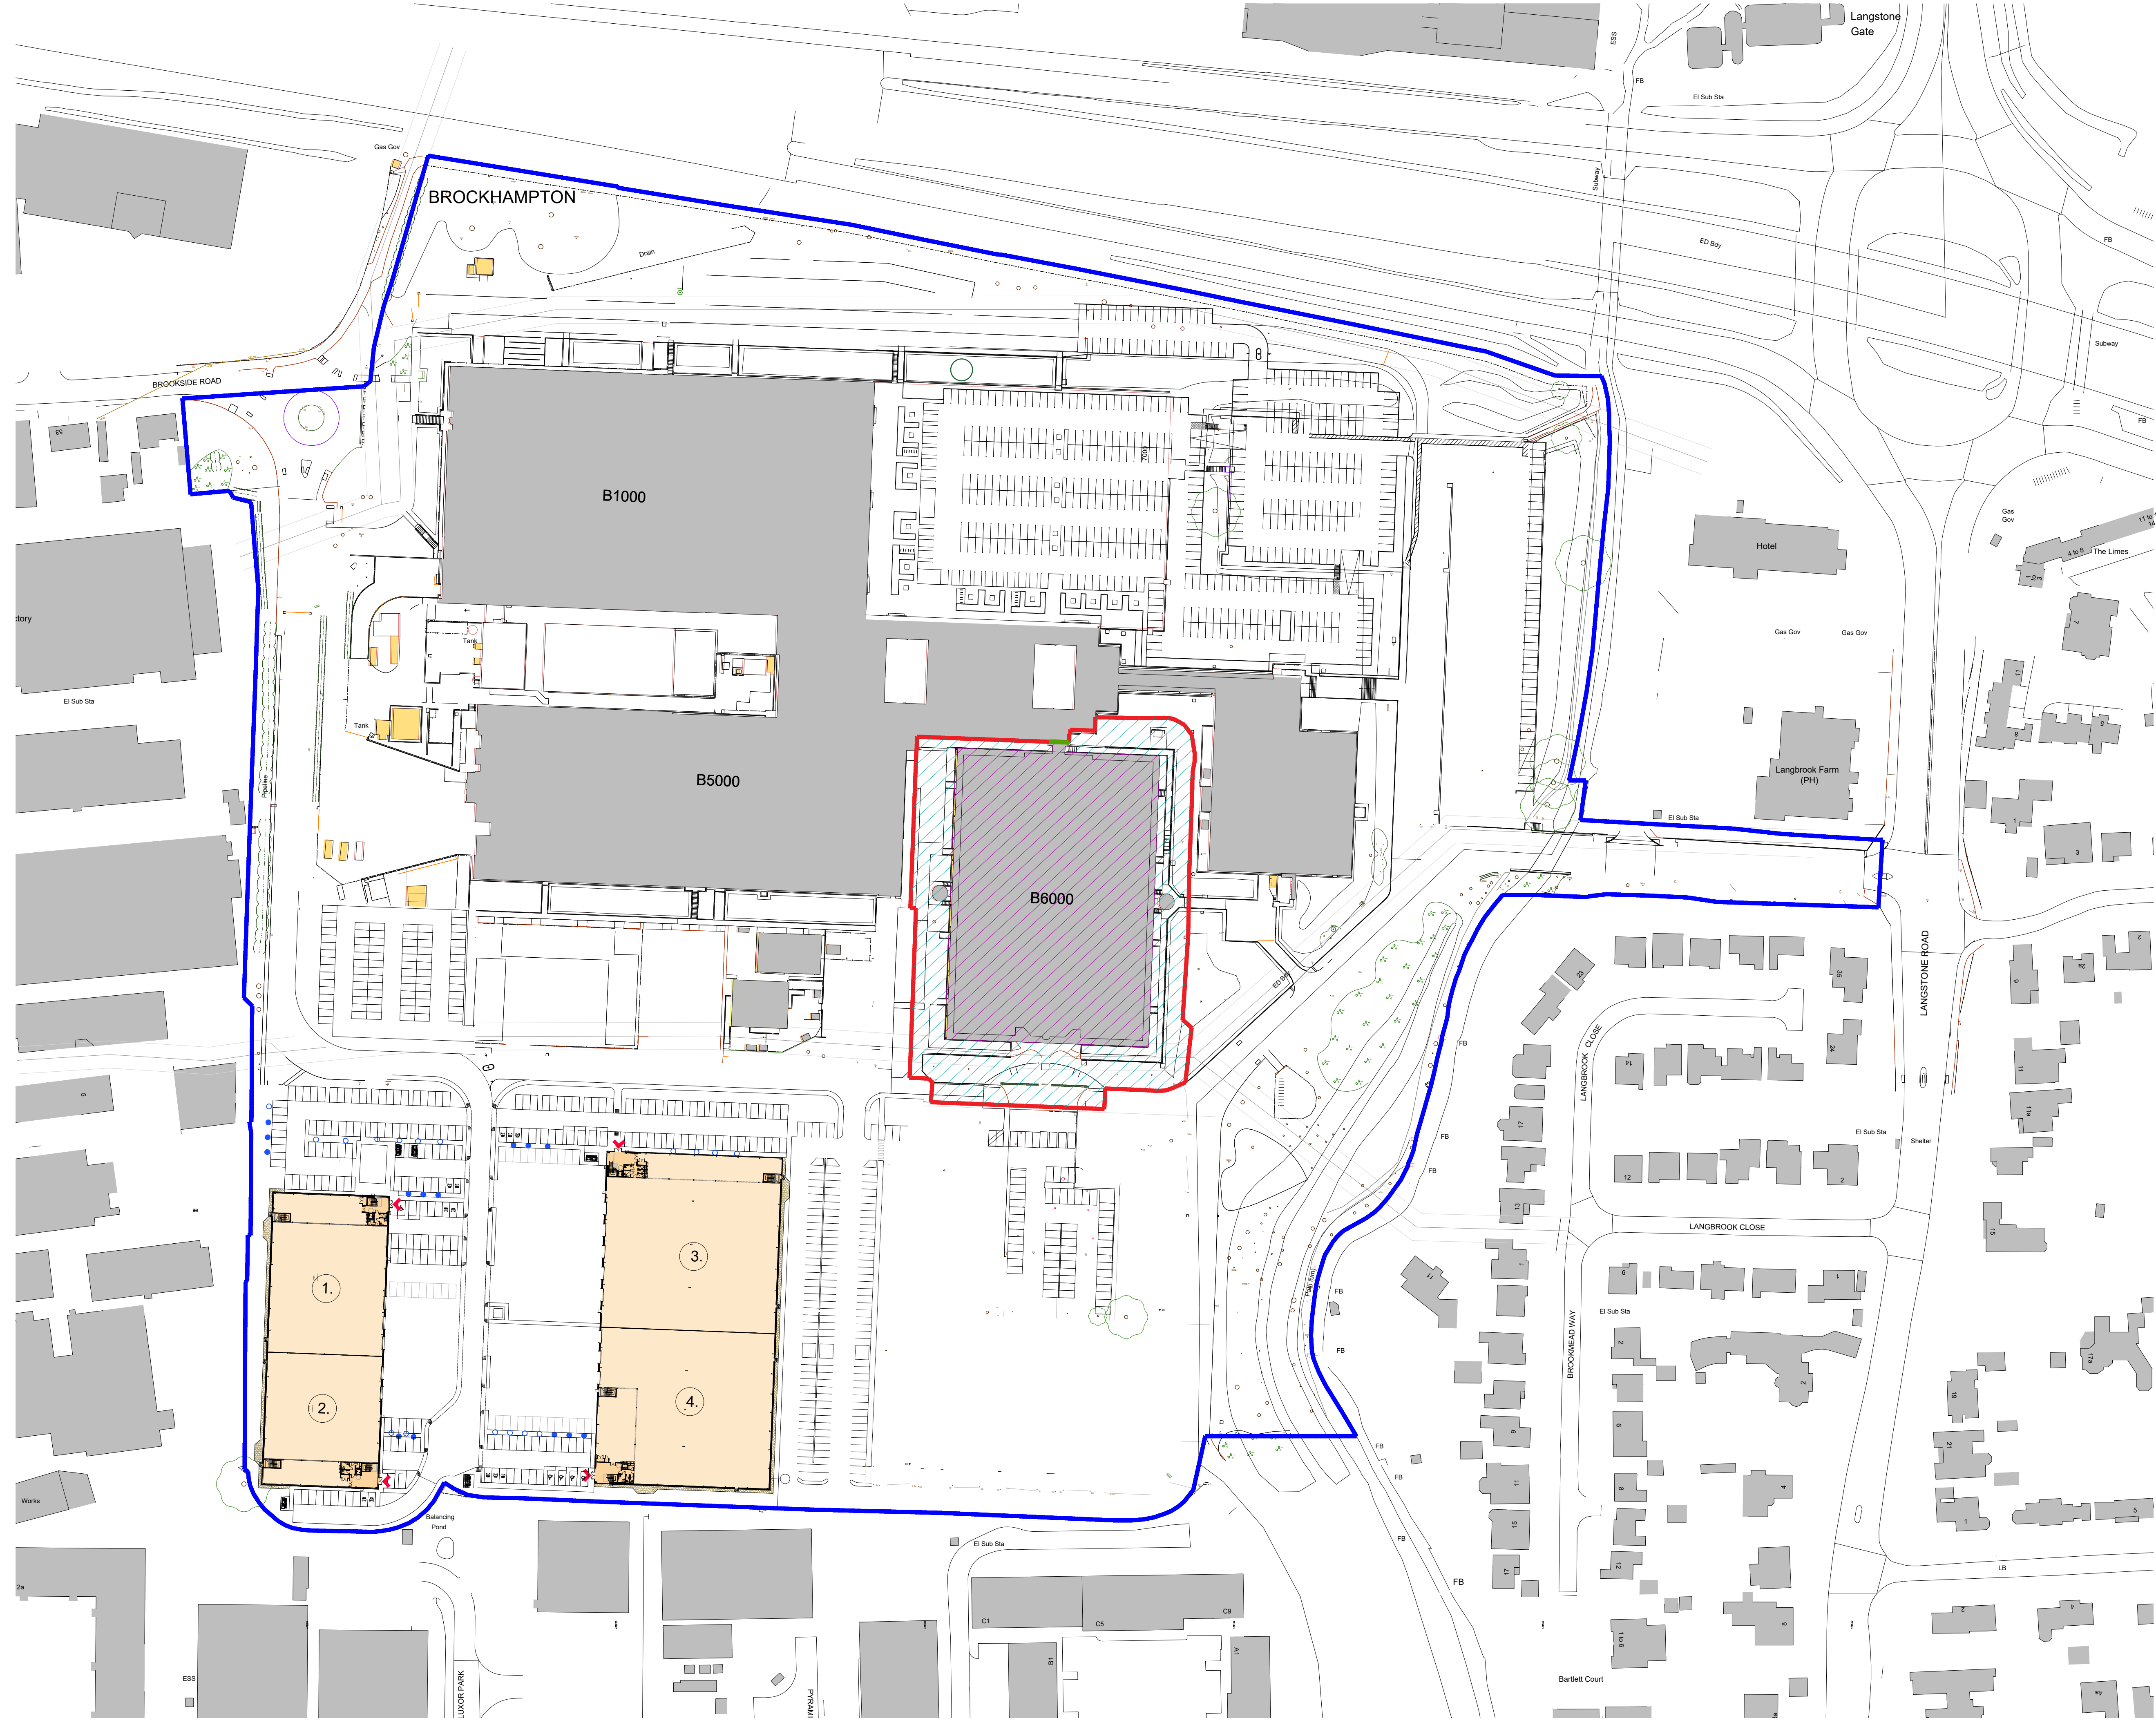

Figured dimensions only are to be used. All dimensions to be checked onsite. Differences between drawings and between drawings and specification or bills of quantities to be reported to the PRC Group.

The copyright of the drawings and designs contained therein remains vested in the PRC Group.

Revisions: Drawn/Chkd: Date:

KEY:

- DEMOLITION SITE AREA
- B6000 STRUTURCE TO BE DEMOLISHED TO UNDERSIDE OF SLAB
- HARD SURFACING & EXTERNAL STRUCTURES TO BE REMOVED
- OPENING TO EXISTING B4000 TO MADE WATERTIGHT AND SAFE TO MATCH EXISTING

N

Client:
XLB PROPERTY &
HAVANT S.a.r.l. (Luxembourg)

Project:
LANGSTONE PARK
HAVANT

Drawing Title:
B6000 DEMOLITION PLAN

12 Warren Yard,
Warren Park,
Milton Keynes,
MK12 5HW
01908 305 246
info@prc-group.com
www.prc-group.com

PRC

Architecture
Planning
Master Planning
Urban Design
Interiors
Landscape

Offices
Woking
London
Milton Keynes
Warsaw

Scale @ A1: 1:1000
Checked by: ME
Date: JUNE 23
Job No: 11392
Stage: PL 017
Rev: *

Issue Status:
Construction ☐ Preliminary ☐
Information ☐ Approval ☐
Tender ☐

Scale 1:1000

0 10 20 30 40 50 100m

PRC Architecture & Planning

Appendix C

Timetable of Ecological Work

Timetable of Works

Activity	Timing	Comments	Person Responsible
Demolition of buildings	Any time when required	A suitably qualified ecologist will need to carry out a site walkover and give a toolbox talk before work commences. A receptor area should be established at this stage.	Principal contractor/ site manager (with advice from project ecologist)
Site inspections to ensure ecological controls/barriers /receptors are not damage/disturbed	Everyday during the demolition and construction phase	If there are issues then the project ecologist can provide advice	Principal contractor/ site manager



Phlorum Limited

Head Office & Registered Office:

Unit 12
Hunns Mere Way
Woodingdean
Brighton
East Sussex
BN2 6AH
T: 01273 307 167

Northern Office:

Ground Floor
Adamson House
Towers Business Park
Wilmslow Road
Didsbury
Manchester
M20 2YY
T: 0161 955 4250

Western Office:

One Caspian Point
Pierhead Street
Cardiff Bay
Cardiff
CF10 4DQ
T: 029 2092 0820

info@phlorum.com
www.phlorum.com

Registered in England & Wales. Reg No. 4967256
