

HEALTH AND SAFETY PLAN



CLIENT: XLB Projects

PROJECT: Langstone Technology Park, Building 1000

DOCUMENT REFERENCE: HSP528-20

ISSUE NO: 1

ANTICIPATED START DATE: Feb 2021

DURATION: 12 weeks

THIS ISSUE

	PRINT NAME	SIGNATURE	POSITION	DATE
AUTHOR	DAN BYNG		Project Manager	JAN 2021
CHECKED BY:	Tony Jack		SHEQ Manager	JAN 2021
ACCEPTED BY:				



HEAD OFFICE

11 Flathouse Road, Portsmouth
Hampshire PO1 4QS

Tel 02392 753733

Fax 02392 755189

HEATHROW OFFICE

Room 107-111, Epsom Square
Eastern Business Park TW6 2BJ

Tel 02392 753733

Fax 02392 755189

www.hughesandsalvidge.co.uk

Ref No. HSP528-20 Langstone Tec



ISSUE HISTORY			
ISSUE NUMBER:	ISSUE DATE	AUTHOR	AMENDMENTS
1	JAN 2021	DAN BYNG	N/A

All revisions to the health and safety plan will be recorded on this page.

The author of the amendment(s), or other authorised person, must explain the details of the amendment (s) to the Site Manager/Site Supervisor. The author must ensure that the Site Manager/Site Supervisor signs off the amendment to confirm that he has received and understood it, and that the Site Manager/Site Supervisor returns the signed off front page so that the author can file it in the project office file.

The Site Manager/Site Supervisor must sign off and return the copy of this Amendment page, as explained above, and carefully insert this page and the amendments into the project site file. He must also clearly line through the existing pages to indicate they have been superseded.

Contents

SECTION 1 – PROJECT INFORMATION	5
1.1 - PROJECT LOCATION	5
1.2 – OUTLINE SCOPE OF WORKS	5
1.3 – DURATION OF WORKS	5
1.4 – SITE RESTRICTIONS	6
1.5 – REFERENCED DOCUMENTATION	6
1.6 – PROJECT CDM OBJECTIVES	9
1.7 - HEALTH AND SAFETY FILE.....	5
SECTION 2 - ORGANISATION	10
2.1 – PARTIES AND CONSULTANTS	10
SECTION 3 – SITE SETUP AND WELFARE FACILITIES.....	11
3.1 – WELFARE FACILITIES	11
3.2 - FIRST AID	12
3.3 - WATER SUPPLY	12
3.4 – SITE LAYOUT PLAN	13
SECTION 4 – SITE RULES	14
SECTION 5 – PERSONAL PROTECTIVE EQUIPMENT	15
5.1 – HUGHES & SALVIDGE EMPLOYEES.....	15
5.2 – VISITORS	15
SECTION 6 - UTILITIES	16
6.1 – GENERAL	16
6.2 - PROTECTION TO PLANT	16
SECTION 7 – ASBESTOS	17
7.1 – ASBESTOS SURVEY	17
7.2 – HSE NOTIFICATION	17
7.3 – LICENSED ASBESTOS REMOVAL	17
7.4 – NON-LICENSED ASBESTOS REMOVAL	17
7.5 - FURTHER ASBESTOS IDENTIFICATION	17
SECTION 8 – TEMPORARY WORKS	17
SECTION 9 – SITE PERMITS.....	19
SECTION 10 – TRAFFIC MANAGEMENT	20
10.1 – AIMS.....	20
10.2 - VEHICULAR ACCESS & EGRESS.....	20
10.3 - DELIVERIES.....	20
10.4 - SITE SPEED	20
10.5 - VEHICLE CLEANING	20
10.6 - ROAD CLEANING.....	20
10.7 - REVERSING ALARMS	20
10.8 - DEDICATED VEHICLES	20

10.9 - VEHICLE QUANTITIES.....	20
10.10 - SITE TRAFFIC RULES.....	21
10.11 – TRAFFIC MANAGEMENT PLAN.....	22
SECTION 11 – EMERGENCY PROCEDURES	23
11.1 - FIRE INCIDENTS.....	23
11.2 - INJURY INCIDENTS	23
11.3 SPILLAGES	23
SECTION 12 – ENVIRONMENTAL CONTROLS	25
12.1 – GENERAL	25
12.2 – WASTE MANAGEMENT RECYCLING AND DISPOSAL	25
12.3 – NOISE & VIBRATION.....	26
12.4 – DUST	26
12.5 – FUEL	26
12.6 – DRAINAGE & CONTROL OF RUN OFF	26
12.7 – STOCKPILES.....	26
SECTION 13 – SITE SECURITY.....	27
13.1 - SECURITY	27
13.2 - VISITORS	27
SECTION 14 – PERSONNEL RESPONSIBILITIES.....	28
14.1 – PROJECT MANAGER.....	28
14.2 – SHEQ MANAGER	28
14.3 – SITE MANAGER/SITE SUPERVISOR.....	28
14.4 – SITE OPERATIVES	29
14.5 – TEMPORARY WORKS COORDINATOR (TWC)	29
14.6 – TEMPORARY WORKS SUPERVISOR	30
SECTION 15 - TRAINING	31
15.1 – GENERAL	31
15.2 – SITE INDUCTION TRAINING.....	31
15.3 – METHOD STATEMENT BRIEFING.....	31
15.4 – TOOL BOX TALKS.....	32
SECTION 16 - COMMUNICATION	34
16.1 – GENERAL	34
16.2 – PROGRESS MEETINGS	34
16.3 – BETWEEN HUGHES & SALVIDGE AND THE CLIENT’S REP/PRINCIPAL DESIGNER	34
16.4 – BETWEEN HUGHES & SALVIDGE AND SUBCONTRACTORS	34
16.5 – VISITS BY THE HEALTH & SAFETY EXECUTIVE	35
16.6 – OCCUPIED ADJOINING PREMISES	35

SECTION 1 – PROJECT INFORMATION

1.1 - PROJECT LOCATION

Hughes & Salvidge have been appointed the role of Principal Contractor for demolition works at Langstone Technology Park, Building 1000, Havant, Hampshire, PO9 1SA



1.2 – OUTLINE SCOPE OF WORKS

- Agree licences and approvals with local authority.
- Approval of health and safety documentation such as TMP, HSP and RAMS
- Enabling works for trialling, trial pits etc...
- Erect secure perimeter fencing to the site, this will be in the form of Heras fencing with appropriate signage affixed
- Termination, diversion and re-routing of services so as to make safe the demolition area
- Condition survey to existing footpaths and roads
- Removal of all asbestos found within the R&D report
- Installation of temporary weatherproofing where separation is to be formed
- Soft strip to all 3 bays
- Separation along agreed cut line of bay 2 - 3
- Demolition of bays 1 and 2

1.3 – DURATION OF WORKS

12 weeks

Commence February 2021

1.4 – SITE RESTRICTIONS

- Asbestos containing materials have been identified from the asbestos surveys produced by therefore all asbestos works will be completed prior to any structural demolition.
- The area of works are within a 'live' occupied work camp with precision works being undertaken within neighbouring properties. All works are to be planned and carried out in such a way as to not impact any of the neighbouring properties
- The main A27 road site to the north of the building to be demolition so tight duct control during demolition will be deployed
- Shared access / egress roads around the works camp will be used, so strict adherence to the traffic management plan (TMP) will be required

1.5 – REFERENCED DOCUMENTATION

Ref.	Document Ref.	Title	Revision	Date	
Volume 1 - ERs					
	200703	Langstone Bldg 1000 Prelims	-	03/07/2020	
VOLUME 1 - APPENDICES					
1.00 Schedule of Amendments to JCT Intermediate with Contractor Design 2016 (Greenberg Traurig)					
1.01	579582269_v 1_LTP	B1000 - JCT ICD 2016 - Schedule of Amondments	v1	11/06/2020	Appendix A
2.00 List of Tender Documents					
2.01	AS THIS DOCUMENT				Appendix B
3.00 Site Surveys (Clancy)					
3.01	CPR/KDDPL/SR141	Knight & Day Drainago & Plumbing Ltd - CCTV Drainago survey SR141	000	5 June 2020	Appendix C
3.02	SB4986-MBS	SurveyBase - basement floor plan survey	-	09/06/2020	Appendix C
3.03	10/1425/001	Clancy - 10-1425-003 Letter Report	000	June 2020	Appendix C
4.00 Work schedules Pricing Document / Contract Sum Analysis (Stace LLP)					
4.01	2021/0123	200707 Langstone Bldg 1000 - Section 3 Work Schedules	-	07/07/2020	Appendix D
5.00 Key Payments Dates Schedule (Stace LLP)					
5.01	2021/0123	200706 (H7.1.2) JCT 2016 Schedule of Key Payment Dates	-	06/07/2020	Appendix E
6.00 Building Control information (Buckley Lewis)					
6.01	Not applicable - see AWW documentation				Appendix F
7.00 Planning					
7.01	Planning ref APP/19/00703	Langstone Technology Park Draft Conditions Top	no rev	undated	Appendix G
8.00 Design Responsibility Matrix (Hollis)					
8.01	No ref	Building 1000 - Schedule of Design Responsibilities_DRAFT	-	06/07/2020	Appendix H
9.00 Pre-Construction Information (Gleeds)					
9.01	BLHS0741 B1000-4000 PCI v2	Building 1000 & 4000 Demolition & Strip out Pre-Construction Information	v2	03/07/2020	Appendix J

Ref.	Document Ref.	Title	Revision	Date	
VOLUME 1 - APPENDICES					
10.00 Site Rules					
10.01	No ref	Site Rules for Contractors	no rev	undated	Appendix K

11.00 Breeam (Cudd Bentley)					
11.01	5548-CBC-RGV-SP-Z-003-P01	Demolition Contractor Breeam Requirements	1	10/06/2020	Appendix L
12.00 Asbestos					
12.01	J188599	Demolition Asbestos survey Bay 3 of B1000	-	15/06/2020	Appendix M
12.02	J188600	Demolition Asbestos survey Bay 1&2 of B1000	-	15/06/2020	Appendix M

Ref.	Document Ref.	Title	Revision	Date
------	---------------	-------	----------	------

VOLUME 2 - DRAWINGS

13.00 Architectural Information (AWW)				
13.01	4046A-1001	Site Location Plan - Option 01	A	
13.02	4046A-1002	Site Plan - Option 01	A	
13.03	4046A-1005	Site Location Plan - Option 02	A	
13.04	4046A-1006	Site Plan - Option 02	A	
13.05	4046A-1010	Site Logistics plan Option 01	A	
13.06	4046A-1015	Site Logistics plan Option 02	A	
13.07	4046A-1101	Existing ground floor plan option 01	A	
13.08	4046A-1102	Existing roof plan option 01	A	
13.09	4046A-1105	Existing basement plan option 02	A	
13.10	4046A-1106	Existing Ground Floor Plan - Option 02	A	
13.11	4046A-1107	Existing ground floor plan option 02	A	
13.12	4046A-1130	Existing North elevation	A	
13.13	4046A-1131	Existing East & West elevation option 01	A	
13.14	4046A-1132	Existing South elevation option 01	A	
13.15	4046A-1135	Existing North elevation option 02	A	
13.16	4046A-1136	Existing East & West elevation option 02	A	
13.17	4046A-1137	Existing South elevation option 02	A	
13.18	4046A-1200	Basement Strip Out Floor Plan - Option 02	C	
13.19	4046A-1201	Ground floor strip out plan option 01	B	
13.20	4046A-1202	Roof demolition plan option 01	C	
13.21	4046A-1205	Ground Floor Strip Out Plan - Option 02	C	
13.22	4046A-1206	Roof Demolition Plan - Option 02	B	
13.23	4046A-1211	Basement Strip Out Plan - Bay 01 Option 02	B	
13.24	4046A-1212	Basement Strip Out Plan - Bay 02 Option 02	B	
13.25	4046A-1213	Basement Strip Out Plan - Bay 03 Option 02	C	
13.26	4046A-1221	GF strip Out Plan- Bay 01 - Option 01	B	
13.27	4046A-1222	GF Strip Out Plan- Bay 02 - Option 01	B	
13.28	4046A-1223	GF Strip Out Plan- Bay 03 - Option 01	B	
13.29	4046A-1225	GF strip Out Plan- Bay 01 - Option 02	C	
13.30	4046A-1226	GF Strip Out Plan- Bay 02 - Option 02	C	
13.31	4046A-1227	GF Strip Out Plan- Bay 03 - Option 02	C	
13.32	4046A-1230	Demolition Elevations North - Option 01	B	
13.33	4046A-1231	Demolition Elevations East and West - Option 01	B	
13.34	4046A-1232	Demolition Elevations South - Option 01	B	
13.35	4046A-1235	Demolition Elevations North - Option 02	B	
13.36	4046A-1236	Demolition Elevations East and West - Option 02	B	
13.37	4046A-1237	Demolition Elevations South - Option 02	B	

Ref.	Document Ref.	Title	Revision	Date
13.38	4046A-1238	Building 1000 _ 4000 North Elevations - Opt 02 Post Demo	B	
13.39	4046A-1239	Building 1000 _ 4000 East Elevation - Opt 02 Post Demo	C	
13.40	4046A-1240	Typical Sections Building 1000 - Option 01	B	
13.41	4046A-1245	Typical Sections Building 1000 - Option 02	B	
13.42	4046A-1250	Typical Section Building 4000 - Option 01	B	
13.43	4046A-1255	Typical Sections Building 4000 - Option 02	C	
13.44	4046A-1256	Typical Sections Building 4000 - Option 02	C	
13.45	4046A-1260	Ground Floor Strip Out Completed - Option 01	C	
13.46	4046A-1265	Ground Floor Strip Out Completed - Option 02	C	
13.47	4046A-6000	Typical Demolition_Temporary Works Details - B1000 Grid 33W	A	
13.48	4046A-6001	Typical Demolition Slab Edge Detail - B1000	B	
13.49	4046A-6010	Typical Demolition_Temporary Works Details - B4000 Grid 15S	C	
13.50	4046A-B-5 (option 1)	B1000+4000 - Outline specification - scope of works - OPTION 1	Issue 3 (rev C)	
13.51	4046A-B-5 (option 2)	B1000+4000 - Outline specification - scope of works - OPTION 2	Issue 3 (rev B)	

14.00 Structural & Civils Information (Clancy)

Option 1				
14.01	S-LS-GA-00-1150	B1000 Ground floor strip out plan	T2	
14.02	S-LS-GA-RF-1151	B1000 Roof demolition plan	T2	
14.03	S-LS-SEC-SL-1200	Typical sections - B1000 & B4000	T2	
14.04	S-LS-DET-SL-1301	Typical details - B1000 & B4001 - sheet 1	T2	
14.05	S-LS-DET-SL-1302	Typical details - B1000 & B4001 - sheet 2	T2	
14.06	S-LS-GN-SL-1000	Structural specification	T2	
14.07	C-LS-GA-DRN-400400	Drainage general arrangement	T2	
14.08	C-LS-GA-DRN-400410	Drainage details	T1	
Option 2				
14.09	S-LS-GA-B1-2149	B1000 Basement floor strip out plan	T2	
14.10	S-LS-GA-00-2150	B1000 Ground floor strip out plan	T2	
14.11	S-LS-GA-RF-2151	B1000 Roof demolition plan	T2	
14.12	S-LS-SEC-SL-2200	Typical sections - B1000 & B4000	T2	
14.13	S-LS-DET-SL-2301	Typical details - B1000 - sheet 1	T2	
14.14	S-LS-DET-SL-2302	Typical details - B1000 - sheet 2	T2	
14.15	S-LS-GN-SL-1000	Structural specification	T2	
14.16	C-LS-GA-DRN-400500	Drainage general arrangement	T2	

Ref.	Document Ref.	Title	Revision	Date
15.00 Mechanical and Electrical Information (Cudd Bentley)				
15.01	5702-CBC-00-00-DR-M-50001	Bay 1 - Mechanical Services Strip Out and Enabling Works Layout (Option 1)	T01	
15.02	5702-CBC-00-00-DR-M-50002	Bay 2 - Mechanical Services Strip Out and Enabling Works Layout (Option 1)	T02	
15.03	5702-CBC-00-00-DR-M-50003	Detail sheet (Option 1)	T02	
15.04	5702-CBC-00-00-DR-M-50004	Bay 1 - Mechanical Services Strip Out and Enabling Works Layout (Option 2)	T01	
15.05	5702-CBC-00-00-DR-M-50005	Bay 2 - Mechanical Services Strip Out and Enabling Works Layout (Option 2)	T02	
15.06	5702-CBC-00-00-DR-M-50006	Bay 3 - Mechanical Services Strip Out and Enabling Works Layout (Option 2)	T02	
15.07	5702-CBC-00-00-DR-M-50007	Detail sheet (Option 2)	T01	
15.08	5702-CBC-00-00-DR-M-50008	Basement level - Mechanical services strip out and enabling works layout (Option 2)	T01	
15.09	5702-CBC-00-00-DR-M-50009	Detail sheet (Option 1 & 2)	T02	
15.10	5702-CBC-00-00-DR-E-60001	Bay 1 - Electrical services strip out and enabling works layout (Option 1)	T01	
15.11	5702-CBC-00-00-DR-E-60002	Bay 2 - Electrical services strip out and enabling works layout (Option 1)	T02	
15.12	5702-CBC-00-00-DR-E-60003	Bay 3 - Electrical services strip out and enabling works layout (Option 1)	T02	
15.13	5702-CBC-00-00-DR-E-60004	Roof level - Electrical services strip out and enabling works layout (Option 1)	T02	
15.14	5702-CBC-00-00-DR-E-60005	Bay 1 - Electrical services strip out and enabling works layout (Option 2)	T01	
15.15	5702-CBC-00-00-DR-E-60006	Bay 2 - Electrical services strip out and enabling works layout (Option 2)	T01	
15.16	5702-CBC-00-00-DR-E-60007	Bay 3 - Electrical services strip out and enabling works layout (Option 2)	T02	
15.17	5702-CBC-00-00-DR-E-60008	Roof level - Electrical services strip out and enabling works layout (Option 2)	T02	
15.18	5702-CBC-00-00-DR-E-60009	Basement level - Electrical Services Strip out and enabling works layout (Option 2)	T01	
15.19	5702-CBC-00-00-DR-E-60010	Detail sheet 1 of 2	T01	
15.20	5702-CBC-00-00-DR-E-60011	Detail sheet 2 of 3	T01	
15.21	5702-CBC-GRG-SP-M-001	Mechanical Services Strip Out and Enabling Works Specification	T02	
15.22	5702-CBC-NW-SP-E-001	Electrical Services Strip Out and Enabling Works Specification	T02	
15.23	5702-CBC-RGV-SP-Z-001-P01	Demolition contractor Breeam requirements	P01	

1.6 – PROJECT CDM OBJECTIVES

- No adverse impact on the environment caused by project works
- No adverse health effects caused by project works
- No Near Misses regarding Work at Height
- No Near Misses regarding Hot Works

1.7 – HEALTH AND SAFETY FILE

On completion of the contract a health and safety file will be compiled and will include the following subject to client requirements.

- Waste Transfer Notes
- Waste Consignment notes for Hazardous Wastes
- Air Clearance Certificates for licensed asbestos removal works
- Site plan with photographs of completed works and marked with any potential hazards.

SECTION 2 - ORGANISATION

2.1 – PARTIES AND CONSULTANTS

CLIENT

XLB Projects
Silver House
31-35 Beak Street
London
W1F 9DP

Tel:

Email: paul@xlbproperty.com

Contact: Paul Whelan

PRINCIPAL DESIGNER/CLIENT'S REPRESENTATIVE

Baynham Meikle
8 Meadow Road
Edgebaston
Birmingham
B17 8BU

Tel:

Email: glan.cashmore@bm-p.co.uk

Contact: Glen Cashmore

DEMOLITION CONTRACTOR

Hughes & Salvidge Ltd (Head Office)
11 Flathouse Road
Flathouse Quay
Portsmouth
PO1 4QS

Tel: 023 9275 3733

Email: enquiries@hughesandsalvidge.co.uk

Website: www.hughesandsalvidge.co.uk

MANAGING DIRECTOR

Martyn Burnett

Mobile: 07860 136361

Email: martyn.burnett@hughesandsalvidge.co.uk

TECHNICAL DIRECTOR

Ian Martin

Mobile: 07768 350877

Email: ian.martin@hughesandsalvidge.co.uk

HEALTH & SAFETY ADVISER

Tony Jack

Mobile: 07867 455107

Email: tony.jack@hughesandsalvidge.co.uk

PROJECT MANAGER

DAN BYNG

Mobile: 07889 087614

Email: danny.byng@hughesandsalvidge.co.uk

SITE MANAGER

Charlie Cawte

Mobile: 07798 554045

Email: charlie.cawte@hughesandsalvidge.co.uk

EMERGENCY CONTACT:

In the event of an emergency or an out of hour's issue, please call the following mobile number:

Charlie Cawte – Mobile: 07798 554045 or DAN BYNG - Mobile: 07889 087614

SECTION 3 – SITE SETUP AND WELFARE FACILITIES

3.1 – WELFARE FACILITIES

Facilities will be provided by Hughes & Salvidge, located at agreed location. These facilities are fitted with a temporary power supply and will include:

- Site Office
- Mess Room with facilities for hot water and heating food
- Drying Room
- WC with warm water and soap
- Appropriate fire-fighting equipment within the offices

The Site Manager/Site Supervisor will appoint an operative to carry out the cleaning of the site facilities on a daily basis and replenish with supplies as necessary. Within the Mess Room there will be a project notice board. General Health & Safety and environment information will be displayed on this board. In particular, the following items will be displayed:

- F10
- General Site Rules
- Emergency Rules
- Map to Local Accident & Emergency Hospital
- Identity of First Aider on site
- Location of First Aid supplies
- HSE Law Poster
- Health & Safety Policy Statement
- Environment Policy Statement
- Quality Policy Statement
- Insurance
- Section 81 Demolition Counter Notice
- Latest COVID posters, Risk Assessments, Sanitising equipment

3.2 - FIRST AID

Adequate first aid supplies are always available on site. The location of these will be identified within site facilities.


The nominated First Aider on this project is Charlie Cawte, details will also be displayed within site facilities.

3.3 - WATER SUPPLY

On site Wash Out Hydrant or Fire Hydrant will be utilised. Hughes and Salvidge to provide standpipe, key and all hoses, nozzles etc. Standpipe to be fitted with double check valve to BS6282.

Where possible the Client will supply water point with enough pressure within the site boundary.

3.4 – SITE LAYOUT PLAN

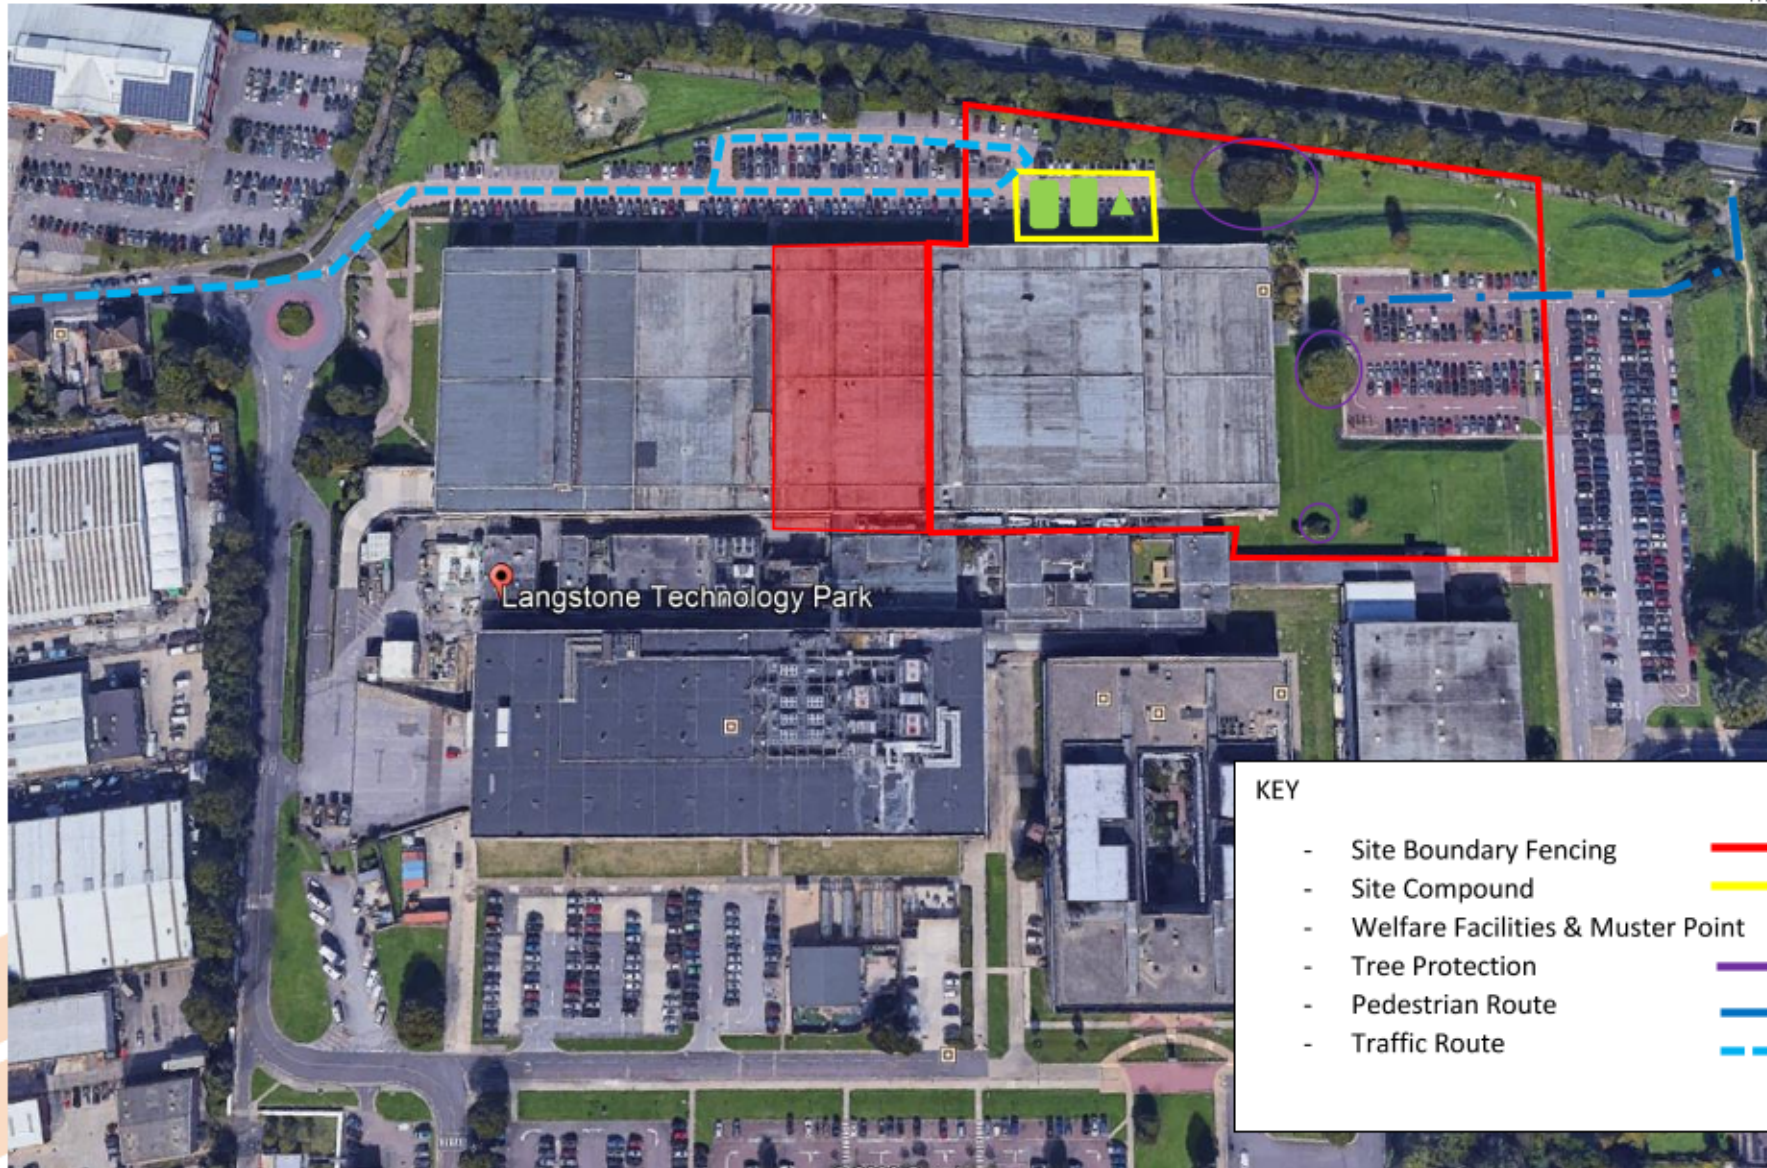

SECTION 4 – SITE RULES



Site Rules

GENERAL

1. Mobile phones/Bluetooth devices should not be used on site and do not answer mobile phones when operating plant or machinery. If there is a requirement to use a mobile phone move to the designated safe area.
2. Valuables and personal property are brought to site at the owner's risk.
3. Alcohol/drugs must not be brought onto site. Employees must not attend work if under the effect of any drugs or alcohol (they will be refused entry to site). Any drugs that may affect an employee's performance should be advised to Management. All employees are issued with the Company Drug Policy (contained in Employees' Handbook) which gives full guidance, be aware of random alcohol and drug testing by clients & Hughes and Salvidge SHEQ team.
4. Work areas are to be kept clear and tidy to allow safe access and egress. Everyone is responsible for picking up and moving trip hazards.
5. The work site, excavations, pits, voids, etc. shall be guarded and signed at all times where necessary.

PPE & CLOTHING

6. The following PPE is compulsory on all Hughes and Salvidge sites unless a specific risk assessment has deemed other PPE must be worn.
 - High-Viz Vest or Coat
 - Safety Footwear (S3 Minimum standard)
 - Safety Helmet
 - Safety Glasses (See risk assessment for specialist works i.e. Burning)
 - Suitable Gloves for task

PLANT & EQUIPMENT

7. All guards and safety devices, e.g. Emergency stop buttons; must be in place and working correctly.
8. Daily checks and records to be carried out
9. All electrical plant & equipment must be 110V (with certain limited exceptions, e.g. Dust Boss, DCU)
10. Speed limit must be adhered to within the site.

WELFARE

11. Complaints from the public shall be dealt with in a courteous manner and referred to the Site Manager, Site Supervisor or Management as appropriate.
12. For health & hygiene reasons, eating and drinking are not permitted outside of the welfare area and it is essential that employees wash their hands before handling food.
13. Swearing, horseplay and practical jokes are not acceptable. Members of the public must not be subjected to wolf whistles or other inappropriate behaviour or language.

IF IN DOUBT – ASK

SECTION 5 – PERSONAL PROTECTIVE EQUIPMENT

5.1 – HUGHES & SALVIDGE EMPLOYEES

All operatives involved with the project will be issued with all appropriate Personal Protective Equipment FOC. The Site Manager/Site Supervisor is responsible for ensuring the site has adequate PPE supplies. PPE Register is to be kept on site to record issue.

MANDATORY PPE

The following is the minimum mandatory PPE for all employees and visitors to site:

- Safety boots - minimum S3 and lace up
- Safety helmet
- Gloves (type according to task)
- Hi-Vis waistcoat
- Safety glasses

NB: Machine Operators do not have to wear items 2-5, whilst in their cabs.

TASK SPECIFIC PPE

Additional PPE/RPE will also be required for certain tasks. Task Method Statements and Risk Assessments will state what, if any, additional PPE/RPE is required for each task.

HOT CUT BURNING OPERATIONS PPE

The following PPE will be worn for hot cut burning operations:

1. Safety boots
2. Safety helmet fitted with green drop down Visor
3. Leather gauntlets
4. Leather jacket with button up neck and full sleeves
5. Heat resistant hood
6. Half face masks, fitted with ABE1 fitter (if burning painted or galvanised metal)

NB: For a low risk, one-off cut, the Site Supervisor/Manager may agree to items 5-7 not being used.

5.2 – VISITORS

Dedicated PPE, for use only by visitors, will be kept at the office

1. Safety boots
2. Safety helmet
3. Gloves
4. Hi-Vis waistcoat
5. Safety glasses

SECTION 6 - UTILITIES

6.1 – GENERAL

Hughes & Salvidge to arrange isolation of the incoming utility services to all structures being demolished.

Written confirmation from appropriate utility provider is required to confirm isolations are complete and illustrate all the details of isolations and any known services that are in the vicinity of the areas being demolished.

However, from experience, these are often difficult to attain. If the Site Management have any uncertainty as to the status of services to the site then third M&E service subcontract engineers will be employed to prove the status, and provide certificates.

Further discussions will take place throughout the contract between all parties, regarding any services that are required to be left intact, diverted or subsequently removed.

6.2 - PROTECTION TO PLANT

Where it is identified that “live” plant exists beneath slabs adjacent to assets being demolished, steel plates to be laid out.

Plant to be identified to personnel via Tool Box Talk.

SECTION 7 – ASBESTOS

7.1 – ASBESTOS SURVEY

A Refurbishment & Demolition Asbestos Survey has been carried out by Envirochem prior to the demolition works commencing.

7.2 – HSE NOTIFICATION

The Refurbishment & Demolition Asbestos Survey has identified both licensed and non-licensed asbestos containing materials. Both FODASB5 and ASBNNLW1 notification forms will be submitted to the HSE, respectively.

The Refurbishment & Demolition Asbestos Survey has identified licensed asbestos containing materials only. FODASB5 notification form will be submitted to the HSE.

The Refurbishment & Demolition Asbestos Survey has identified non-licensed asbestos containing materials only. ASBNNLW1 notification form will be submitted to the HSE.

7.3 – LICENSED ASBESTOS REMOVAL

Licensed asbestos removal will be performed by Hughes & Salvidge's preferred licensed asbestos removal contractor:

R H Insulation Services Ltd
Unit D7 Segensworth Business Centre
Segensworth Road
Fareham
Hampshire
PO15 5RQ

7.4 – NON-LICENSED ASBESTOS REMOVAL

Non-licensed asbestos removal will be performed by Hughes & Salvidge.

7.5 - FURTHER ASBESTOS IDENTIFICATION

During the works there is a risk that further asbestos materials, previously unknown of, may be discovered.

On discovery of suspected material, operatives will advise the Site Manager/Site Supervisor immediately who will in turn contact Head Office so that samples of the suspect material can be taken and sent for analysis.

Head Office to ensure Client is fully aware at all stages of suspected discovery and subsequent resultant analysis. All site operatives will have undergone Asbestos Awareness Training.

SECTION 8 – TEMPORARY WORKS

Different forms of Temporary Works (TW) may be required in order to safely and effectively deliver this project. The Project Manager assumes the role of Temporary Works Coordinator (TWC); and is responsible for confirming necessary TW, production of TW register, ensuring appropriate levels of independence of design checking, and issuance of all Permitry for installation, alteration, and removal of TW. The TWC may delegate the duty of issuance of Permitry to the Temporary Works Supervisor (TWS). In this instance the TWS will be the Site Manager.

TWC: Dan Byng

TWS: Charlie Cawte

The responsibilities of these individuals are fully detailed in Section 14 of this document.

It is imperative that all TW are given a category of risk. This category of risk will determine the level of independence of the checker of the relevant design.

Below is an extract from BS5957 illustrating how to determine the category of risk, and therefore level of independence of checking required:

Table 1 Categories of design check

Category	Scope	Comment	Independence of checker
0	Restricted to standard solutions only, to ensure the site conditions do not conflict with the scope or limitations of the chosen standard solution.	This applies to the use of standard solutions and not the original design, which will require both structural calculation and checking to category 1, 2 or 3, as appropriate.	Because this is a site issue, the check may be carried out by another member of the site or design team.
1	For simple designs. These may include: formwork; falsework (where top restraint is not assumed); needling and propping to brickwork openings in single storey construction.	Such designs would be undertaken using simple methods of analysis and be in accordance with the relevant standards, supplier's technical literature or other reference publications.	The check may be carried out by another member of the design team.
2	On more complex or involved designs. Designs for excavations, for foundations, for structural steelwork connections, for reinforced concrete.	Category 2 checks would include designs where a considerable degree of interpretation of loading or soils' information is required before the design of the foundation or excavation support or slope.	The check should be carried out by an individual not involved in the design and not consulted by the designer.
3	For complex or innovative designs, which result in complex sequences of moving and/or construction of either the temporary works or permanent works.	These designs include unusual designs or where significant departures from standards, novel methods of analysis or considerable exercise of engineering judgement are involved.	The check should be carried out by another organization.

Temporary Works	Category of Risk
Heras Fencing	0
Welfare Cabins (single stack)	0
Signage	0
Scaffold Tower	0
Podium Step	0
MEWP	0
Hoarding	2
Scaffold (Basic)	2

Permits are required to be issued for all category 1-3 designs.

SECTION 9 – SITE PERMITS

The following Site Permits are required to be issued by Site Manager/Supervisor:

- Permit to Dig
- Permit to Hot Cut
- Permit to Enter Confined Space
- Permit to Work
- Permit to Install, Load, Alter, or Dismantle Temporary Works

SECTION 10 – TRAFFIC MANAGEMENT

10.1 – AIMS

The main aims of the traffic management plan are detailed below. The person in charge of traffic management on and off site will be the Site Manager/Supervisor or his nominated deputy.

1. To ensure minimal disruption of traffic flow along surrounding roads.
2. To ensure vehicles do not enter 'No-Go' areas.
3. To ensure that any mud arising from the works is not taken onto the highway.
4. To ensure the Health & Safety of site personnel along with pedestrians using footpaths adjacent to site entrance.
5. To minimise any nuisance to surrounding occupiers caused by site traffic or traffic entering or leaving site; there shall be no queuing of vehicles on any of the surrounding roads.
6. No large plant or heavy goods vehicles will be permitted on site prior to 8.00 am

10.2 - VEHICULAR ACCESS & EGRESS

Access is to be gained via Brookside Road Care to be taken by drivers when entering and leaving the site. Heavy goods vehicles will not be permitted on site before 9.00 a.m. Any arriving on site prior to this time will be refused entry. Last access will be 16.00, again any deliveries after this time will be refused

10.3 - DELIVERIES

Deliveries of plant and equipment along with fuel, waste and scrap collection will be planned in advance by the Site Manager/Site Supervisor. When delivery vehicles arrive on site they will report to office, sign in, be given the site rules for traffic and then directed to their delivery location (copy of site rules attached). Vehicles will be parked inside the site whilst signing in.

10.4 - SITE SPEED

The maximum speed limit on site is 10mph. Any drivers breaking this speed limit will be banned.

10.5 - VEHICLE CLEANING

Vehicles to be checked by driver and Banksman for mud on wheels. Water supply to be on hand to wash down if required and road sweeper will be on standby should the need arise for sweeper to be deployed.

10.6 - ROAD CLEANING

The likelihood of mud on the road during demolition is low. The Site Manager/Supervisor will monitor road cleanliness and arrange road sweepers if deemed necessary.

10.7 - REVERSING ALARMS

The majority of vehicles making deliveries to site will have audible reversing alarms. In the interest of Health & Safety these will not be switched off. Banks men to be in place when required.

10.8 - DEDICATED VEHICLES

As there are only a limited number of companies that will be making deliveries and collecting waste, etc. it is the intention that where possible the same drivers will be used.

10.9 - VEHICLE QUANTITIES


Following the initial delivery of bulk plant etc. the numbers of heavy goods vehicles entering and leaving site is likely to be no more than 4 per day.

10.10 - SITE TRAFFIC RULES

- **MAXIMUM SPEED LIMIT ON SITE *STRICTLY* 10 M.P.H**
- **VEHICLES MUST STAY WITHIN DEDICATED ROUTES**
- **NO REVERSING WITHOUT A LOOKOUT**
- **DRIVER TO WEAR SAFETY HELMET, SAFETY FOOTWEAR, GLASSES, GLOVES & HIGH VISIBILITY CLOTHING WHEN OUT OF CAB**
- **PERSONNEL MUST REPORT TO SITE MANAGER/SITE SUPERVISOR BEFORE LOADING/UNLOADING**
- **ALL LOADS MUST BE SECURE BEFORE LEAVING SITE, HIEGHT OF LOADS, THIS IS ULTIMATELY THE DRIVER'S RESPONSIBILITY**
- **WHEELS TO BE CHECKED TO ENSURE NO MUD IS TAKEN ONTO ROAD**
- **NO LOAD WILL BE ALLOWED TO LEAVE SITE WITHOUT RELEVANT PAPERWORK/TICKETS BEING CORRECT AND SIGNED**

OFFENDERS WILL BE BANNED FROM SITE

10.11 – TRAFFIC MANAGEMENT PLAN

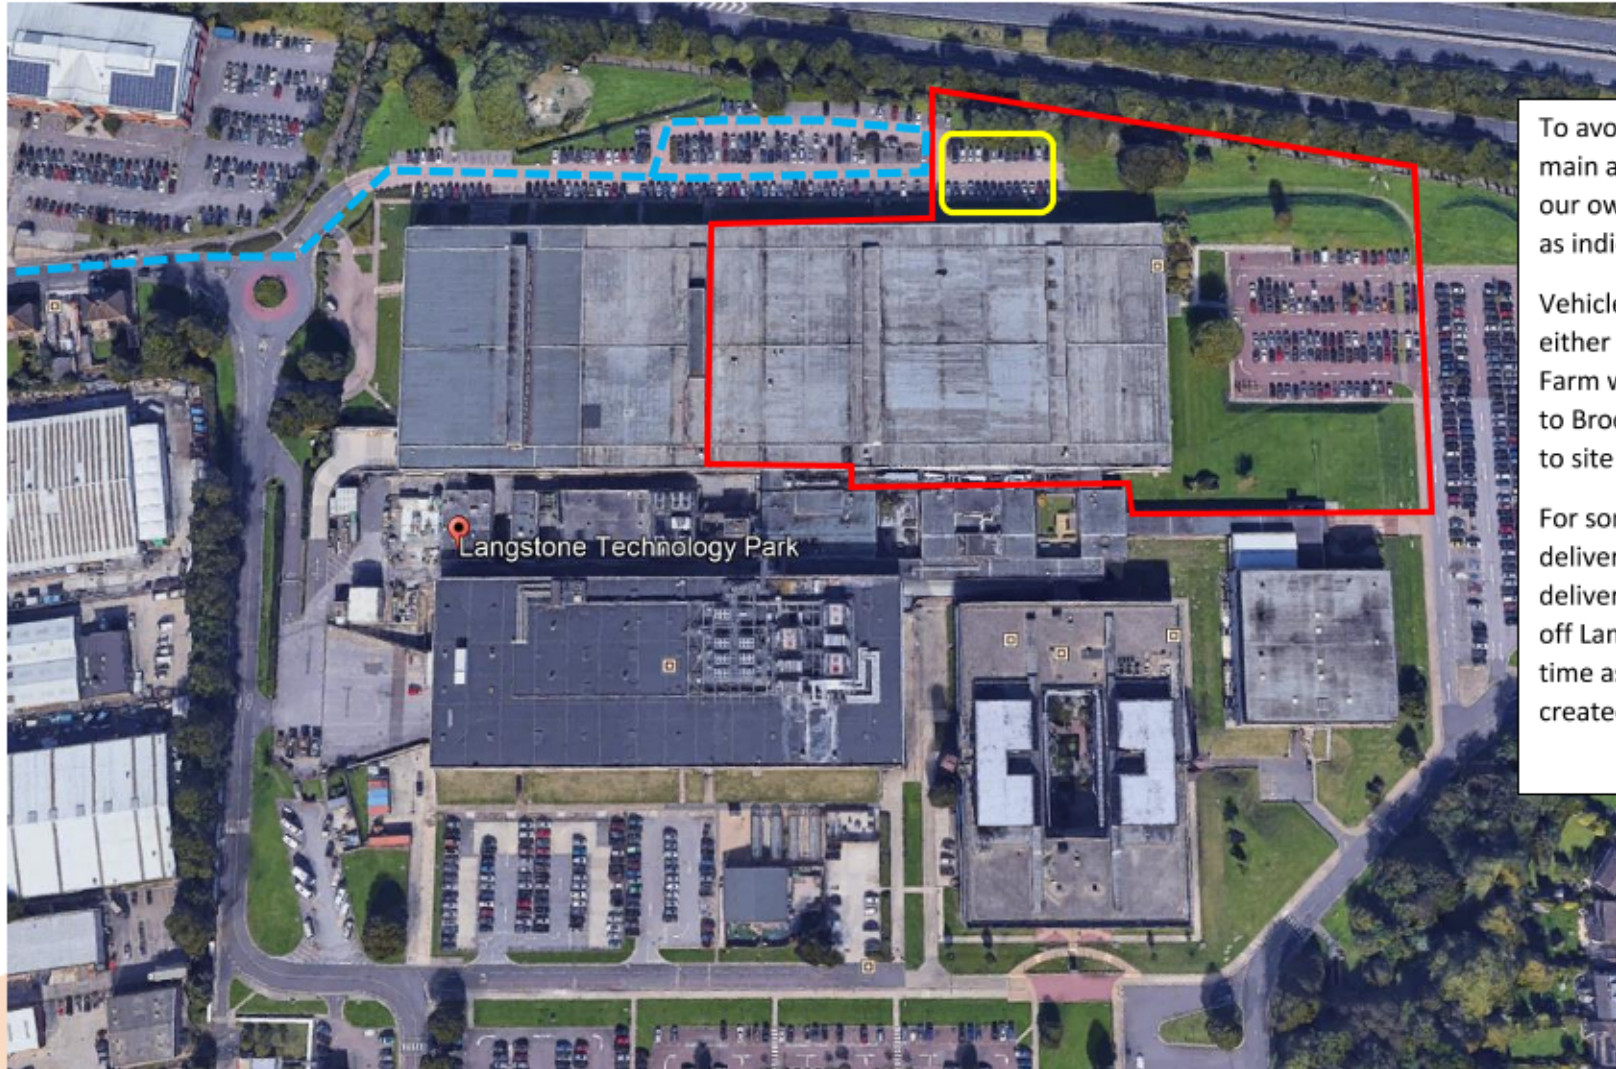

To avoid too much shared use of main access roads HSL will create our own access to and from site as indicated — — — — —

Vehicles are to access from either the A3M or A27 onto Harts Farm way which in turn leads on to Brookside Road where access to site can be gained.

For some of the larger plant deliveries, these may have to be delivered via the main entrance off Langstone Road until such time as the preferred route is created

SECTION 11 – EMERGENCY PROCEDURES

11.1 - FIRE INCIDENTS

Upon discovering a fire, which cannot be easily extinguished or hearing the site alarm, the work area is to be evacuated. Hand operated sirens will be placed at signed fire points, that are contain throughout the site, to signal that evacuation is required by its sounding. The site manager on a weekly basis will test the siren when the site is not occupied. The site office staff and the site security will be advised when testing is in progress.

Should any personnel be unaccounted for the site manager will instigate a search or await assistance, as he deems appropriate. Specific fire and rescue procedures will be developed and agreed when confined space working is required.

Upon the emergency services arriving at the site they will be escorted by site security to the appropriate Hughes and Salvidge Limited area where the site administrator and/or site manager will explain the site hazards and conditions and escort them on site where practical. In the case of an out of hours' emergency, the gatehouse personnel will appraise the emergency services personnel and attempt to contact the management of Hughes and Salvidge Limited using the telephone numbers provided to the client's project team, or as detailed at site security. The Hughes and Salvidge Limited personnel will then attend site if necessary. Principal Designer/Client to be made aware of incident within 24 hours.

11.2 - INJURY INCIDENTS

In the event of an injury requiring first aid treatment the incident must be immediately reported to the Site Manager and/or his deputy who are trained in First Aid. He/they will treat the injury as considered appropriate and if applicable, arrange for the injured person to attend hospital. The Site Manager will then make sure that the Incident Investigation Report Form is completed and sent by Email to the Company Head Office. Upon receipt the Health and Safety Manager will review all documentation relating to the injury and distribute accordingly to the Client and Principal Designer. Principal Designer/Client to be made aware of injury within 24 hours.


Should it be necessary to summon external Emergency Services to the scene of an incident, telephoning the Emergency Services on 999, giving name, location and details of the incident. Where a telephone is not available near the work area a 2-way radio will be used to contact the site manager. Access routes will be kept clear of obstruction at all times

11.3 SPILLAGES

The removal/cleaning of any spillages of materials or any trapped process residues will be overseen by the site manager.

The actions to be taken are:

- All operatives will be removed from the area and when required the area cordoned off.
- The site drains in the vicinity will be covered by sand bags or other suitable methods to prevent any spilled materials entering the site drainage system.
- The client will then be informed and an agreed course of action will be undertaken.
- For low risk spills, absorbent materials will be placed on the spill using any necessary PPE and RPE. The absorbent materials will be shovelled into bags and placed in the appropriate waste container.
- For high risk spills, a detailed actions plan will be developed with the client prior to any remediating action are undertaken

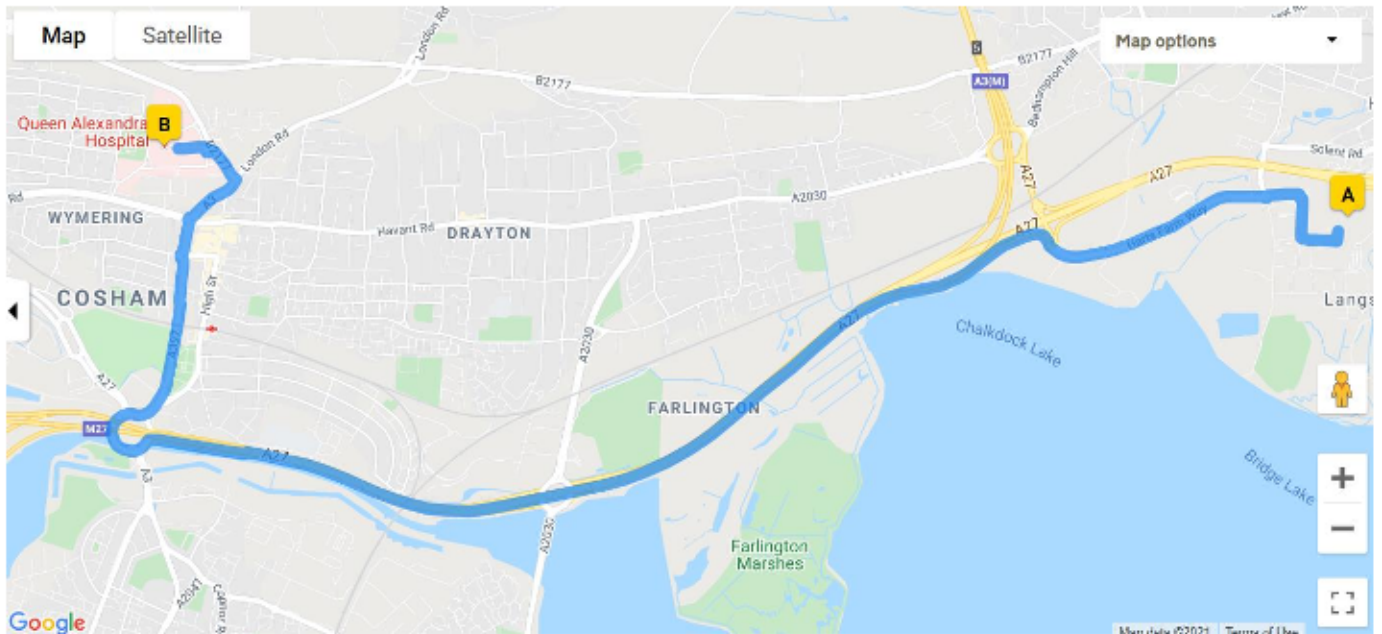

Queen Alexandra Hospital

Cosham

Portsmouth

PO6 3LY

SECTION 12 – ENVIRONMENTAL CONTROLS

12.1 – GENERAL

We want to minimise pollution and waste, as this will affect on our future health. Some materials can be harmful to the environment as well as to people. Always try to use eco-friendly materials such as water based rather than solvents and use the minimum that is required to do the job. Don't skimp as it will need to be done again. The same applies to energy; the more energy you use or waste, the more the power station or refinery will emit pollution into the atmosphere.

Some ways of reducing energy:

- Don't leave unwanted lights or equipment switched on, especially heaters
- Keep outside doors closed to retain heat, fit door closers to drying rooms
- Use thermostats and timers to control individual room temperatures
- Euro 5/6 Plant

WASTE

Some waste will be produced but this should be minimised to reduce landfill costs. There is an order of priority:

REDUCE

- Don't over order and keep stock of what you have
- Don't waste energy, switch off unwanted lights and equipment
- Use more efficient equipment – e.g. use LED lights rather than incandescent bulbs
- Only take out what you are going to use that day / shift

REPLACE / FIND AN ALTERNATIVE

- Avoid CFCs in fridges and fire extinguishers; PCBs – in transformers
- Use aerosols with alternative gases inside not CFCs
- Avoid chloride-bleached paper, use chlorine free paper

RE-USE

- Wherever possible, attempt to reuse material

REFURBISH / RENOVATE

- Try to use the best, most durable materials available for the purpose. This will mean less replacement in the future and less waste.
- Materials that cannot be re-used directly can be refurbished and re-used
- We have a weekly plant inspection log to ensure all equipment is running efficiently – not only reducing emissions but also saving time because its working properly

12.2 – WASTE MANAGEMENT RECYCLING AND DISPOSAL

All debris arising from demolition will be segregated and processed on site as part of demolition process. There will be many types of material produced and these will be dealt with as follows if applicable;

General Debris

All materials unable to be recycled such as ceiling tiles and loose debris will be loaded into 35-yard roll on/off containers and moved off site to licensed landfill facility. Each bin will be conveyed with netting to prevent dust.

Plasterboard

This will be kept separate and placed into containers specifically for this type of waste.

Timber

All timber waste will be segregated and loaded into a 35yrd roll on/off bin ready for transported to a waste transfer station for recycling.

Scrap Metals

All scrap metal will be segregated into various grades/types and loaded into scrap trailers or roll on/off containers and removed from site to licensed scrap processing plant for recycling as part of the demolition process.

Concrete / Brick / Masonry (Hard Inert Arisings)

All hard inert arisings to be crushed and left on site for re-use.

12.3 – NOISE & VIBRATION

Throughout the demolition process, noise is to be kept to a minimum; this will be achieved in various ways as detailed below.

1. Use of correct plant for specific tasks ensuring plant is fully maintained.
2. Using 'quietest' method when both demolishing structures and removing hardcore and concrete, i.e. using bucket or pulveriser rather than impact breakers.
3. Leaving part of external envelope of particular buildings intact whilst removing materials. This will be determined by structural stability of buildings as demolitions proceed.
4. Ensuring works are only carried out within agreed working hours.

12.4 – DUST

Dust may present itself as a hazard during demolition works. This will be controlled by means of dampening down using water supplies around the site. During structural demolition suppression will be via fire hoses with operatives to gain access above structure where necessary by means of MEWP to enable water to be sprayed onto the workface

12.5 – FUEL

Storage of fuel for plant will be in secure 110% bunded bowsters with no external openings/taps. Spill kits will be kept in marked up yellow containers adjacent to the bowsters to clear up any fuel spillages. Operators to report any spillages ASAP to Site Manager immediately. Foam fire extinguishers will also be available.

12.6 – DRAINAGE & CONTROL OF RUN OFF

Whilst it will be necessary to control dust with water, care has to be taken to ensure that general site dirt and dust does not enter the existing drainage system. Gullies will be protected by filter rolls and/or pads that will be checked regularly for effectiveness and replaced as appropriate. These are to be checked by the Site Manager/Site Supervisor and replaced as necessary.

12.7 – STOCKPILES

Whenever possible stockpiles of brick / concrete will be kept to a minimum. Materials will be loaded away as they arise. However, in some areas, this may not be practicable. In this instance the stockpiles will be kept dampened to avoid migration of dust.

SECTION 13 – SITE SECURITY

13.1 - SECURITY

The site fencing will be checked for security and integrity at the beginning and end of each working day.

13.2 - VISITORS

- All visitors to site will be escorted on site by Site Manager/Site Supervisor or his nominated deputy.
- Visitors will be required to sign in at the office and must wear appropriate PPE, which will be a minimum of hard hat, gloves, safety glasses, appropriate footwear and high visibility clothing. (Dedicated PPE, excluding footwear, for use only by visitors, will be kept at the office.)
- Note: If visitors do not have suitable footwear they will be restricted as to where they can walk around the site by the Site Manager/Site Supervisor.
- As visitors to site will be escorted around site at all times, a full induction is not required, instead visitors will undergo a brief site induction detailing site rules, any 'no go' areas, etc.

SECTION 14 – PERSONNEL RESPONSIBILITIES

14.1 – PROJECT MANAGER

Is responsible to the Operations Director for:

- Directing the project team under his control to implement the Safety, Health, Environment & Quality (SHEQ) Policy
- Fully understanding personal responsibilities under the HASAWA 1974 and all supporting legislation and treat the health and safety of persons under their control as a matter of the highest priority.
- Organising/monitoring the project to comply with the Safety, Health, and Environment & Quality Policy.
- Appointing qualified First Aider for the project.
- Disciplining/reporting any person who is careless in regard to their own safety or the safety of others.
- Attending regular meetings with the Client and/or their representatives as and when required.
- Co-operating in all opportunities available for safety training and assessing the individual training needs of the project personnel.
- Responsible for checking and agreeing with sub-contractors' Method Statements and passing information to the Principal Designer.
- Responsible for reviewing and updating the Health & Safety Plan as required and providing a report on progress of the works for use at progress meetings.
- Responsible for providing all relevant information for inclusion in the Health & Safety file and presenting this file to Principal Designer on completion of the works.

14.2 – SHEQ MANAGER

Is responsible to the Managing Director for:

- Carrying out Health & Safety Site Inspections and recording findings.
- All aspects of site safety training, refresher and specialist training where necessary.
- Ensuring that all operatives are trained and competent in their work process.
- Ensuring that all information affecting site Health & Safety is communicated to the work force.
- Ensuring that the Company Safety Policy is implemented at all times during the project.
- Advising on safe working procedures and monitoring to ensure compliance.
- Checking works are being carried out as laid down in the Health & Safety Plan and Method Statements.
- Reporting any person found to be careless with regard to their own safety or omissions that affect others.
- Encouraging all persons to show awareness and attention to safety matters.
- Ensuring that all registers and forms that are required be maintained on the project, kept up to date and available for inspection.

14.3 – SITE MANAGER/SITE SUPERVISOR

Is Responsible to the Project Manager for:

- Familiarising himself with the project safety requirements and implementing these as required.
- Carrying out instructions given by the Project Manager and Health & Safety Adviser.
- Keeping up to date a specific site diary, which will be issued by the office on request.
- Observing safety regulations, risk assessment and method statements at all times.
- Carrying out site inductions and briefing method statements as required and recording all such sessions.
- Delivering Tool Box Talks no less than 1 every 2 weeks and recording sessions.
- Taking the best possible care of their own health and safety, that of colleagues and operatives and anyone else whom the works may affect.
- Ensuring that safe systems of work are maintained and plant is kept in good order thus keeping the level of disruption to a minimum.
- Reporting any fault or failure of any plant or system to the Project Manager/Plant Manager to enable rapid rectification.

- Ensuring any action required as the result of a site inspection by the Health & Safety Adviser or others is rectified as a matter of priority.
- Ensuring that all personnel are aware of emergency procedures and whereabouts of First Aiders.

14.4 – SITE OPERATIVES

are responsible to the Site Manager/Site Supervisor for:

- Ensuring that all instructions given are carried out in accordance with Risk Assessments, COSHH Assessments and Method Statements.
- Ensuring that they take reasonable care of their own Health and Safety and carry out their works in such a manner that does not affect others.
- Reporting of any condition that they see that they may consider being of risk to anyone.
- Reporting any defect or loss of equipment issued in the interests of personal protection or which may result in risk to fellow operatives or others.
- Ensuring that they familiarise themselves with all site emergency procedures.
- Complying with General Site Rules, which are posted in their welfare facility and contained herein.

14.5 – TEMPORARY WORKS COORDINATOR (TWC)

The TWC should be the first point of contact between the designer and the site team for all TW matters.

The TWC should be responsible for ensuring that the organisation's procedure for the control of Temporary Works is implemented on site.

The TWC should be responsible to the organisation's Designated Individual, for ensuring the Temporary Works design is implemented in accordance with the relevant drawings and the specification.

The TWC should define and record the actual responsibilities of each TWS, where appointed (see 4.5).

The principal activities of the TWC are to:

- Co-ordinate all temporary works activities.
- Ensure a temporary works register is established and maintained.
- Ensure that the various responsibilities have been allocated and accepted.
- Ensure that a design brief is prepared with full consultation, is adequate, and is in accordance with the actual situation on site.
- Ensure that any residual risks, identified at the design stage, assumed methods of construction or loading constraints identified by the designer of the permanent works are included in the design brief.
- Ensure that a satisfactory temporary works design is carried out.
- Ensure that a design check is carried out by someone who was not involved in the original design this should include checking for:
 1. concept
 2. structural adequacy
 3. compliance with the brief
- Where appropriate, ensure that the design is made available to other interested parties, e.g. the Principal Designer or the designer of the permanent works.
- Register or record the drawings, calculations and other relevant documents relating to the final design.
- Ensure that those responsible for on-site supervision receive full details of the design, including any limitations and guidance notes associated with it and prepare a specific method statement.
- Ensure that checks are made at appropriate stages.
- Ensure that any proposed changes in materials or construction are checked against the original design and appropriate action taken.
- Ensure that any agreed changes, or corrections of faults, are correctly carried out on site.

- Ensure that during use of the temporary works all appropriate maintenance is carried out.
- Ensure all necessary Permitry is issued by the TWS.
- Ensure that a documented safe system of work is in place and implemented for the installation and dismantling of any temporary works.
- Ensure that any relevant information for the health and safety file is transmitted to the Principal Designer.
- In all cases, ensure that the TWSs are operating in accordance with the approved procedures.

The TWC appointed for this project is Dan Byng

The TWC Signature.....

14.6 – TEMPORARY WORKS SUPERVISOR

The TWS should be responsible to the TWC. The TWS should assist the TWC in the supervision and checking of the temporary works. This should include the supervision of the erection, use, maintenance and dismantling of the temporary works, as applicable. This should also include carrying out inspections of the scheme and formally recording the findings on HSF17A form, and liaising with the TWC to ensure any modifications to the scheme or differences from the envisaged conditions (use or environmental) are drawn to the attention of the designer.

The TWS has been delegated the responsibility for the issuance of site Permitry for the installation, loading, alteration, and dismantling of any temporary works.

The TWS appointed for this project is Charlie Cawte

The TWS signature

SECTION 15 - TRAINING

15.1 – GENERAL

Personnel employed on the site will have received formal training from an approved body, i.e. NDTG, CITB accreditation and will hold a valid CSCS card as a minimum. Hughes and Salvidge expect all employees to have undertaken asbestos and demolition awareness training.

A Summary Competency Training Matrix is retained on site by Site Managers/Site Supervisors, which illustrates the competency of all Hughes & Salvidge personnel.

15.2 – SITE INDUCTION TRAINING

The Site Manager/Site Supervisor will ensure that all operatives are suitably and adequately trained for the work that they do or are likely to do.

All personnel engaged on site must undergo a site-specific health & safety induction session prior to starting work on site. This will be delivered by the Site Manager/Site Supervisor.

The following must be included in the site induction:

- Project safety rules.
- The arrangements and rules regarding working in the vicinity of asbestos.
- Emergency procedures, which are to be agreed with Client/Principal Designer.
- Explanation of Method Statement/Health & Safety Environmental Plan and any implications this may have.

These items should be considered a minimum and each contractor should add any information relevant to their activities.

A record must be made on a HSF15 Form of all Site Inductions and submitted to the Project Manager giving the following details:

- Site
- Duration
- Details of Induction
- Date of induction
- Name and signature of all attendees
- Name of the inductor

All visitors to site will undergo a reduced induction from Site Manager/Site Supervisor on site. They will also sign to confirm they have received an induction, on an HSF15 Form.

15.3 – METHOD STATEMENT BRIEFING

All personnel engaged on site must undergo a Method Statement Briefing session specific to their work prior to starting work on site. This will be undertaken by the Site Manager/Site Supervisor.

An explanation of Method Statement/Health & Safety Plan and any implications this may have must be included. These items should be considered a minimum and any subcontractor should add any information relevant to their activities.

A record must be made on a HSF14 Form of all Method Briefings and submitted to the Project Manager, giving the following details:

- Site
- Duration
- Brief Details of Method

- Date of briefing
- Name and signature of all attendees
- Name of the briefer

15.4 – TOOL BOX TALKS

Tool Box Talks are to be held throughout the duration of the project. The topic of each talk will be specific and may relate to any of the following:

- Daily briefings of works that day
- Standard NDTG Tool Box Talk
- A current work activity
- A future work activity
- An adverse trend in site working practice
- A safe working procedure
- A method statement
- Any 'No Go' areas
- Special items requested by management

A record must be retained of all Toolbox Talks on an HSF16 Form and submitted to the Project Manager, giving the following details:

- Site
- Duration
- Brief details of Talk
- Date of induction
- Name and signature of all attendees
- Name of the briefer

Toolbox talks are to be carried out on a fortnightly basis as a minimum and also as and when required or dictated.

- No. 1. General Duties
- No. 2. Advice to Employees
- No. 3. Responsibilities
- No. 4. Housekeeping
- No. 5. Personal Points
- No. 6. Working Dress
- No. 7. Eye Protection
- No. 8. Heads & Feet
- No. 9. Noise
- No. 10. Skin Care
- No. 11. Alcohol
- No. 12. Fire
- No. 13. Manual Handling
- No. 14. Safe Stacking
- No. 15. Hand Tools
- No. 16. Portable Electric Tools
- No. 17. Working Safely with Electricity
- No. 18. Welding Safely
- No. 19. The Safe Use of Ladders
- No. 20. Step Ladders
- No. 21. Trestle Scaffolds
- No. 22. Tower Scaffolds
- No. 23. Do's & Don'ts on Scaffold
- No. 24. Openings & Edges
- No. 25. Work on Roofs

- No. 27. Excavations
- No. 28. Demolition
- No. 29. Slings
- No. 30. Chains
- No. 31. Shackles
- No. 32. Hooks & Eye Bolts
- No. 33. Working with Compressed Air Tools
- No. 34. Banksmen/Slingers
- No. 35. Compressed Gas Cylinders
- No. 36. Cartridge Hammers or Rivet Guns
- No. 37. Abrasive Wheels
- No. 38. Control of Substances Hazardous to Health Regulations
- No. 39. Use of Fire Extinguish

SECTION 16 - COMMUNICATION

16.1 – GENERAL

The successful implementation of this Health & Safety Plan depends upon there being adequate coordination, communication and liaison between the various parties. Hughes & Salvidge site staff will encourage continuous informal liaison, discussion and provision of information with all concerned to ensure effective co-ordination of all activities on site. In addition, the following formal arrangements have been made:

16.2 – PROGRESS MEETINGS

The Project Manager is responsible for arranging necessary meetings in order to ensure all parties are up to date with the progress of the project.

The nature of the project means that informal meetings will take place continually between different parties to ensure uninhibited progress of the works. However, as a minimum requirement, the following meetings will be arranged:

DAILY ACTIVITY BRIEFINGS (DAB)

- Meetings prior to commencement of each shift between Site Manager/Site Supervisor and staff on site, to discuss the day's work/No Go areas/plant movements/asbestos removal areas.
- Meeting with client's representative to discuss the day's work along with traffic movements etc.

WEEKLY MEETINGS

- Tool Box Talks with all operatives. Particular subjects can range from manual handling to asbestos removal. The Site Manager/Site Supervisor can decide as to subject matter to suit site conditions.
- Progress meetings with Hughes & Salvidge's Project Manager to discuss every aspect of the works.

MONTHLY MEETINGS

- Progress meetings with client's representative, Principal Designer and Hughes & Salvidge will be chaired by the Principal Designer. These meetings will be to discuss all matters including programme, etc.

16.3 – BETWEEN HUGHES & SALVIDGE AND THE CLIENT'S REP/PRINCIPAL DESIGNER

Hughes & Salvidge and the client's representative will review the implementation of the Health & Safety Plan as an agenda item at their progress meeting, which will be held weekly. The Site Manager/Site Supervisor will not instruct personnel or contractors to carry out work on a site without the required consultation and cooperation.

16.4 – BETWEEN HUGHES & SALVIDGE AND SUBCONTRACTORS

Hughes & Salvidge will hold regular planning and coordination meetings as appropriate with each subcontractor where health & safety will be the first item on the agenda. At these meetings matters related to the assessment of risk or proposed methods of work will be discussed, as will the interface with the contractors' activities. A record will be maintained and circulated of all the relevant discussions regarding health and safety and the environment.

Hughes & Salvidge management must satisfy themselves the subcontractor is competent and must assess their impact on other works on the site. It may be that the interfaces are totally incompatible in which case a change in working methods or phasing of the work may be necessary to reduce risk.

Co-ordination and liaison of day-to-day health and safety matters will be carried out between each subcontractor's nominated manager and managers from Hughes & Salvidge's team. Each member of Hughes & Salvidge's team will be responsible for ensuring that appropriate records of such co-ordination and liaison are maintained.

Assessment of Subcontractors

We use only approved subcontractors on our sites. This involves the completion of our Subcontractor Health and Safety Questionnaire by the subcontractor for approval by our Health and Safety Advisor and Technical Director. All potential subcontractors are vetted in accordance with our BS EN ISO 9001 certification and if successful placed on our Approved Subcontractors' List.

Once employed, subcontractors must adhere to our subcontractors' code of practice which we issue to them and ask them to sign to show that they have read it and will comply.

Method Statements will be required from these subcontractors for any work being carried out on site. The Method Statement must be agreed with Contracts Management and the Site Supervisor before work begins. A copy of the document is kept on site to enable the maintenance and monitoring of compliance. Subcontractors are also monitored on a daily basis by the Site Supervisor.

Safety and environmental information is disseminated to subcontractors using various methods and documents, these include: Pre-Start Meetings, Site Specific Inductions, Tool Box Talks, Company Memo's, Presentations, Seminars, Company Health Safety & Environmental Handbook, Pre-Construction Information, Method Statements, Risk Assessments, COSHH Assessments, Permit to Work, Subcontract Agreements, Subcontract Code of Practice, etc.

Each document is issued to the subcontractor so that they can read and understand the hazards, risks and associated control measures. The documents are signed as a record of issue, understanding and compliance.

We also undertake a subcontractor performance review post project which is completed by the Health and Safety Advisor, Contracts Manager and Site Supervisor (project team). Feedback is given to the subcontractor and if improvement is needed the subcontractor must demonstrate that they have rectified this.

16.5 – VISITS BY THE HEALTH & SAFETY EXECUTIVE

Any visit to a project by a Health & Safety Executive Inspector will be notified by Site Manager/Site Supervisor to the Hughes & Salvidge's Project Manager and the Health & Safety Adviser promptly.

16.6 – OCCUPIED ADJOINING PREMISES

Prior to works commencing, Hughes and Salvidge will make a letter drop to local residents / building occupiers, providing basic details of the project and telephone numbers for key members of the project team.

Monthly Newsletters will also be produced, providing updates as to the status of the works, these will be emailed to stakeholders of neighbouring businesses and put on notice boards around the campus
