


Tree schedule				
Tree No	Species	Category	RPA Radius	Tree Works
All retained trees & hedges				
Carry out safety check and lift over site to 3-4m as necessary.				
G1	Sycamore	B	4.8	-
G2	Sycamore, cherry, ash, elm, hawthorn	C	3.6	-
G3	White poplar	B	3.6	-
T4	Purple plum	C	5.4	-
G7	Alder	C	3.0	Fell for SINC ground works
G8	Alder	B	4.2	-
G9	Sycamore, ash, alder	B	4.8	-
G10	Alder	B	4.2	-
G11	Alder	B	4.8	-
T12	Alder	C	3.6	-
T13	Alder	C	3.0	-
G39	Alder	C	3.0	-
T40	Alder	U	3.0	Fell for management
T41	Alder	U	3.0	Fell for management
G42	Lime	C	2.4	Fell for haul road access
G43	Alder	B	3.0	Fell for haul road access

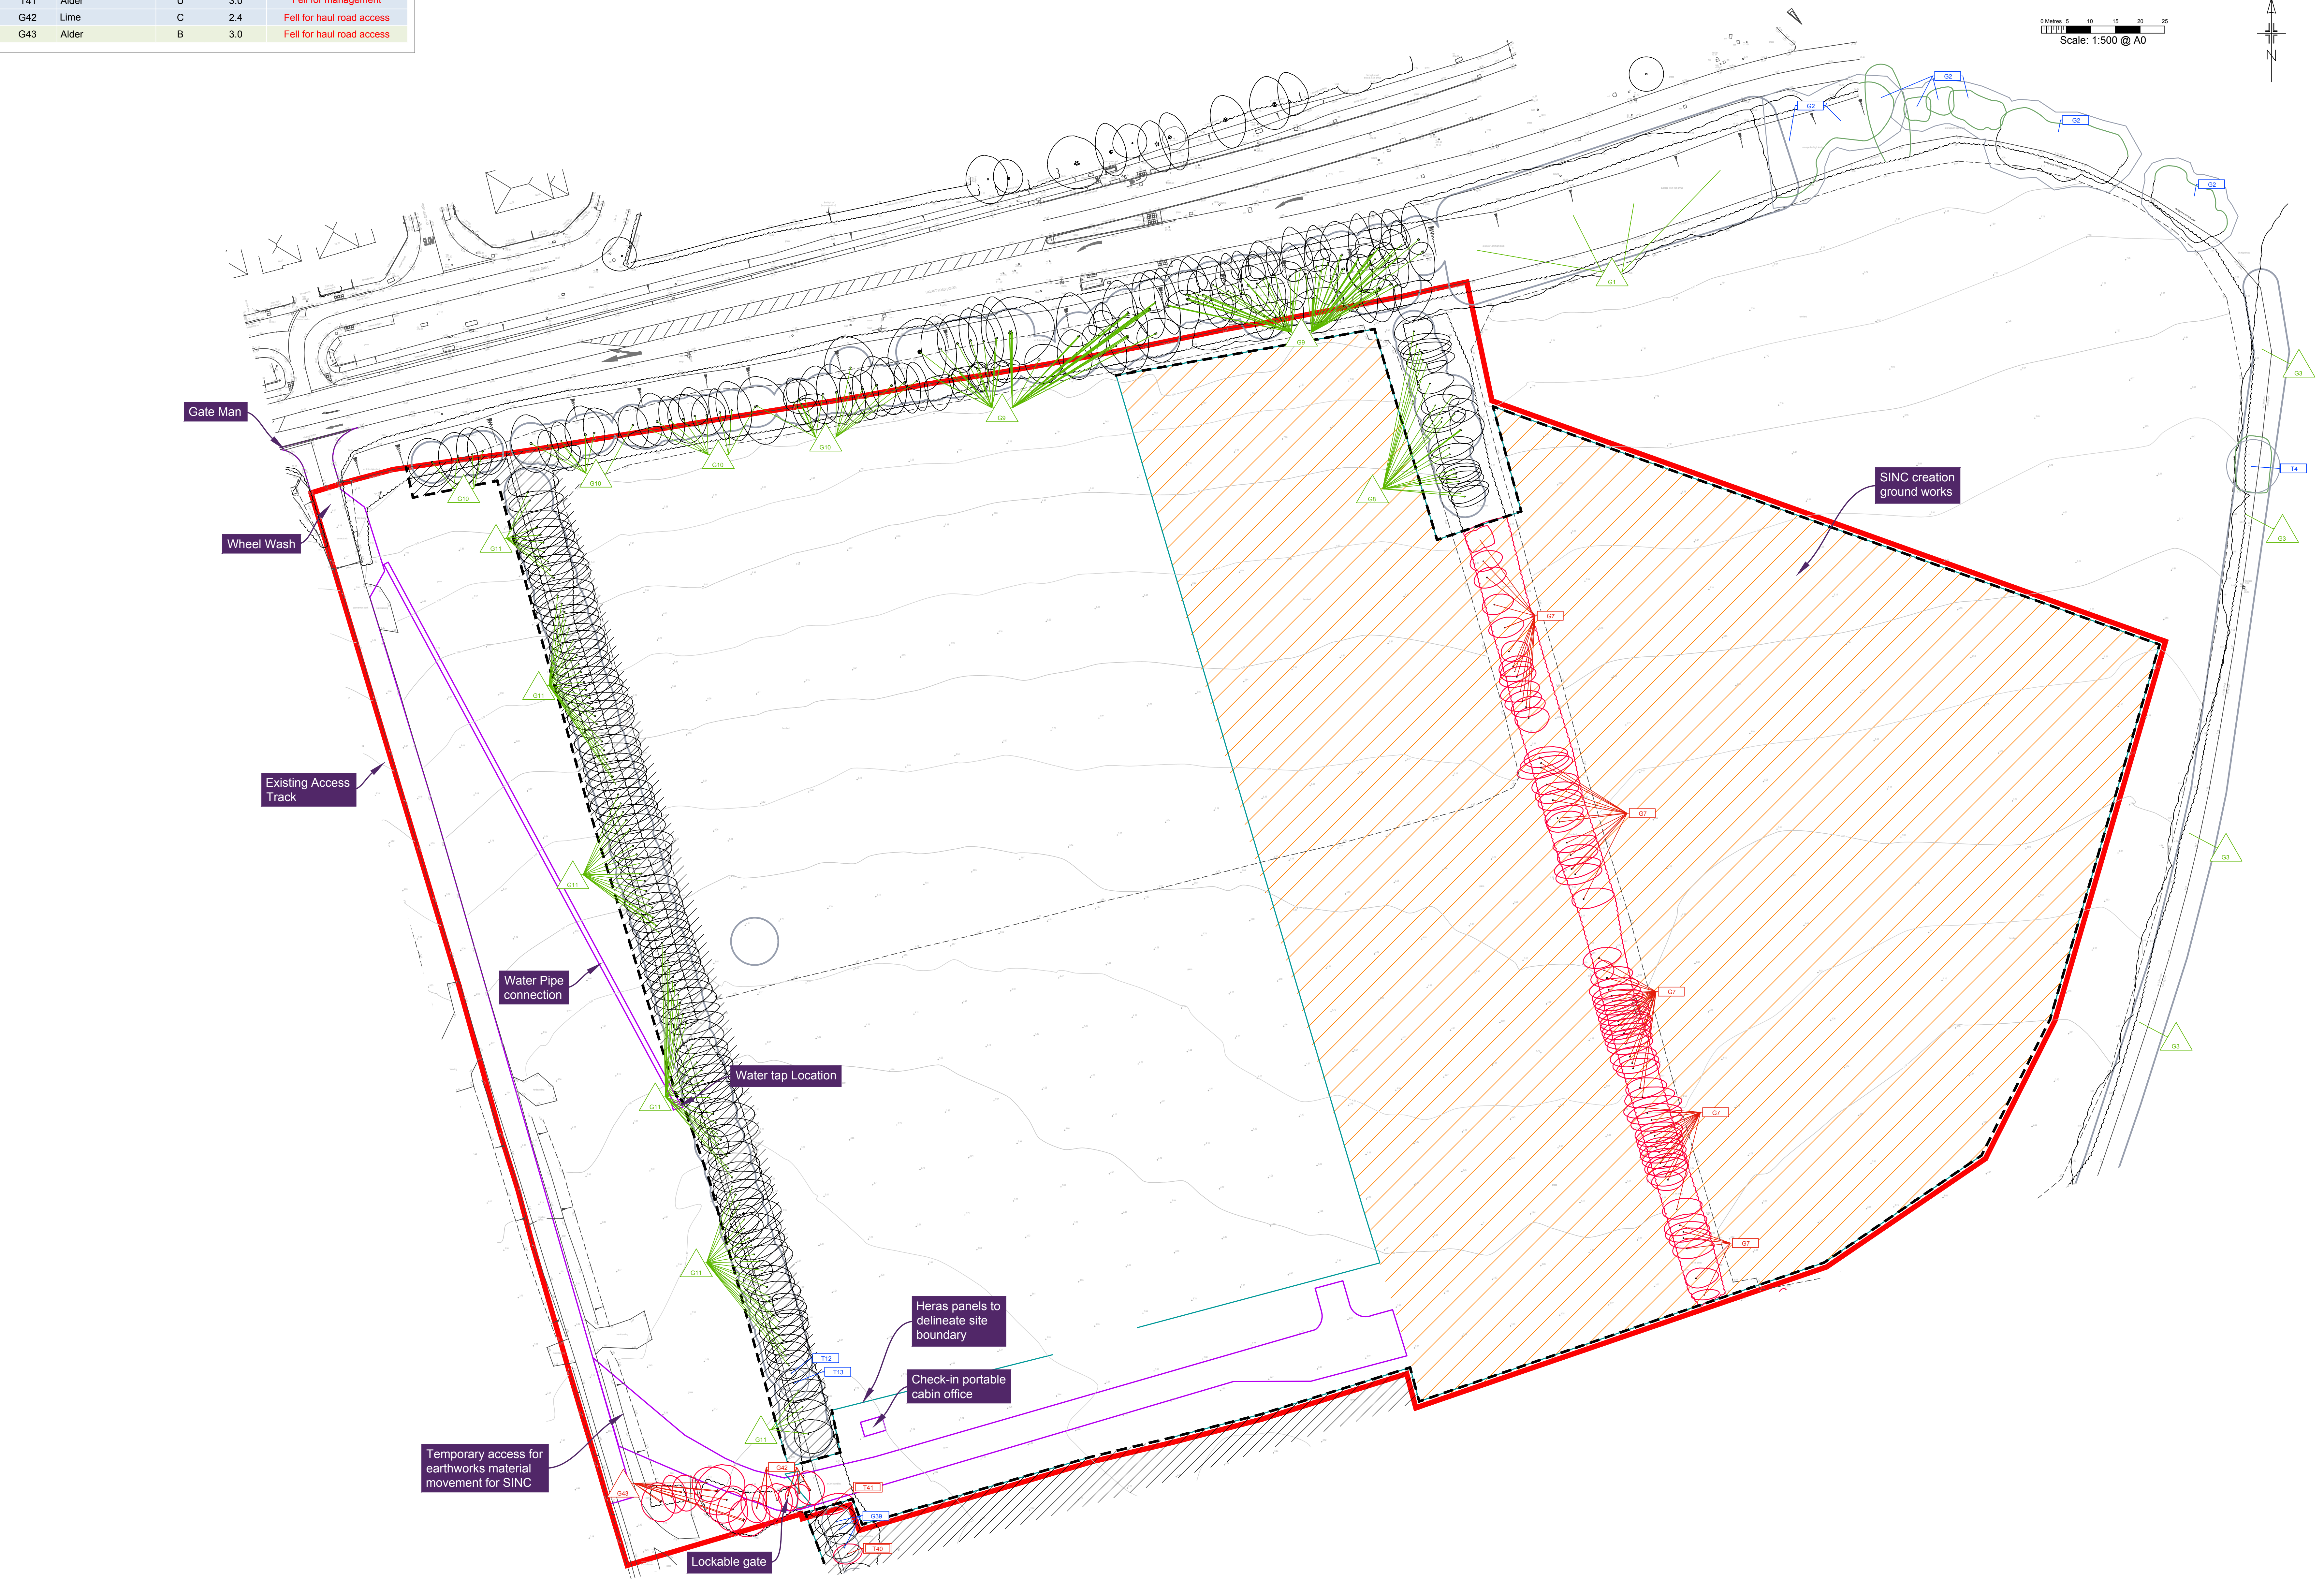

Tree protection plan

Location of trees, categorisation & protection/management proposals at Forty Acres Farm, Havant Road - SINC Groundworks

Barrell Plan Ref: 16270-BT4

Provided Plan Refs: 36FA01 & N812393 PL151

b

barrell

TREE CONSULTANCY

Permission is granted to scale from this drawing for Local Authority Planning Approval purposes relating to tree protection measures only. Where applicable this drawing is to be read in conjunction with the arboricultural report. This drawing is the copyright of Barrell Tree Consultancy 2018. ©

This drawing to be reproduced in colour only.

www.barrelltreecare.co.uk

- BS category B Trees of moderate quality
- BS category C Trees of low quality
- BS category U Trees unsuitable for retention
- Trees to be removed
- Haul road
- Boundary Line
- SINC Ground works area
- Estimated tree positions not included on original land survey and/or adjusted crown spreads
- Construction exclusion zone (CEZ) to be protected by fencing and/or ground protection
- Root protection area (RPA) boundaries for category A and B trees
- Root protection area (RPA) boundaries for category C trees

SGN 1 Monitoring tree protection

Always:

- have a pre-commencement meeting with the tree consultant before development starts
- use the tree consultant to regularly check that protection remains fit for purpose
- use the tree consultant to supervise work in rpas
- keep a written record of supervision

SGN 2 Fencing protected trees

Always:

- install protection before development starts
- make sure protection is fit for purpose, i.e. it prevents damage to trees and soil
- keep protection in place until there is no risk to trees
- get written permission to move or remove any protection

SGN 4 Pollution control

Always:

- keep toxic products away from RPAs

SGN 11 Installing services in RPAs

Always:

- use the tree consultant to supervise work in RPAs
- select the least damaging option when installing services, so prioritise trenchless, over broken trench over continuous trench
- hand-dig trenches if trenchless is not feasible

How to use plan

More detailed guidance on each Site Guidance Note (SGN) can be found in a printed hard copy compilation of all the SGNs issued to the Site Manager at the pre-commencement site meeting (Note: This should be retained on site throughout the duration of works). Additionally, an electronic pdf compilation of all the SGNs, was submitted with this drawing to the local planning authority and the client. Alternatively, a pdf of each SGN can be downloaded by:

- clicking the image links in the electronic pdf version of this plan;
- holding a mobile phone QR (Quick Response) code reader over the QR code in the paper version of this plan; or,
- visiting our website at <https://www.barrelltreecare.co.uk/resources/technical-guidance>
