


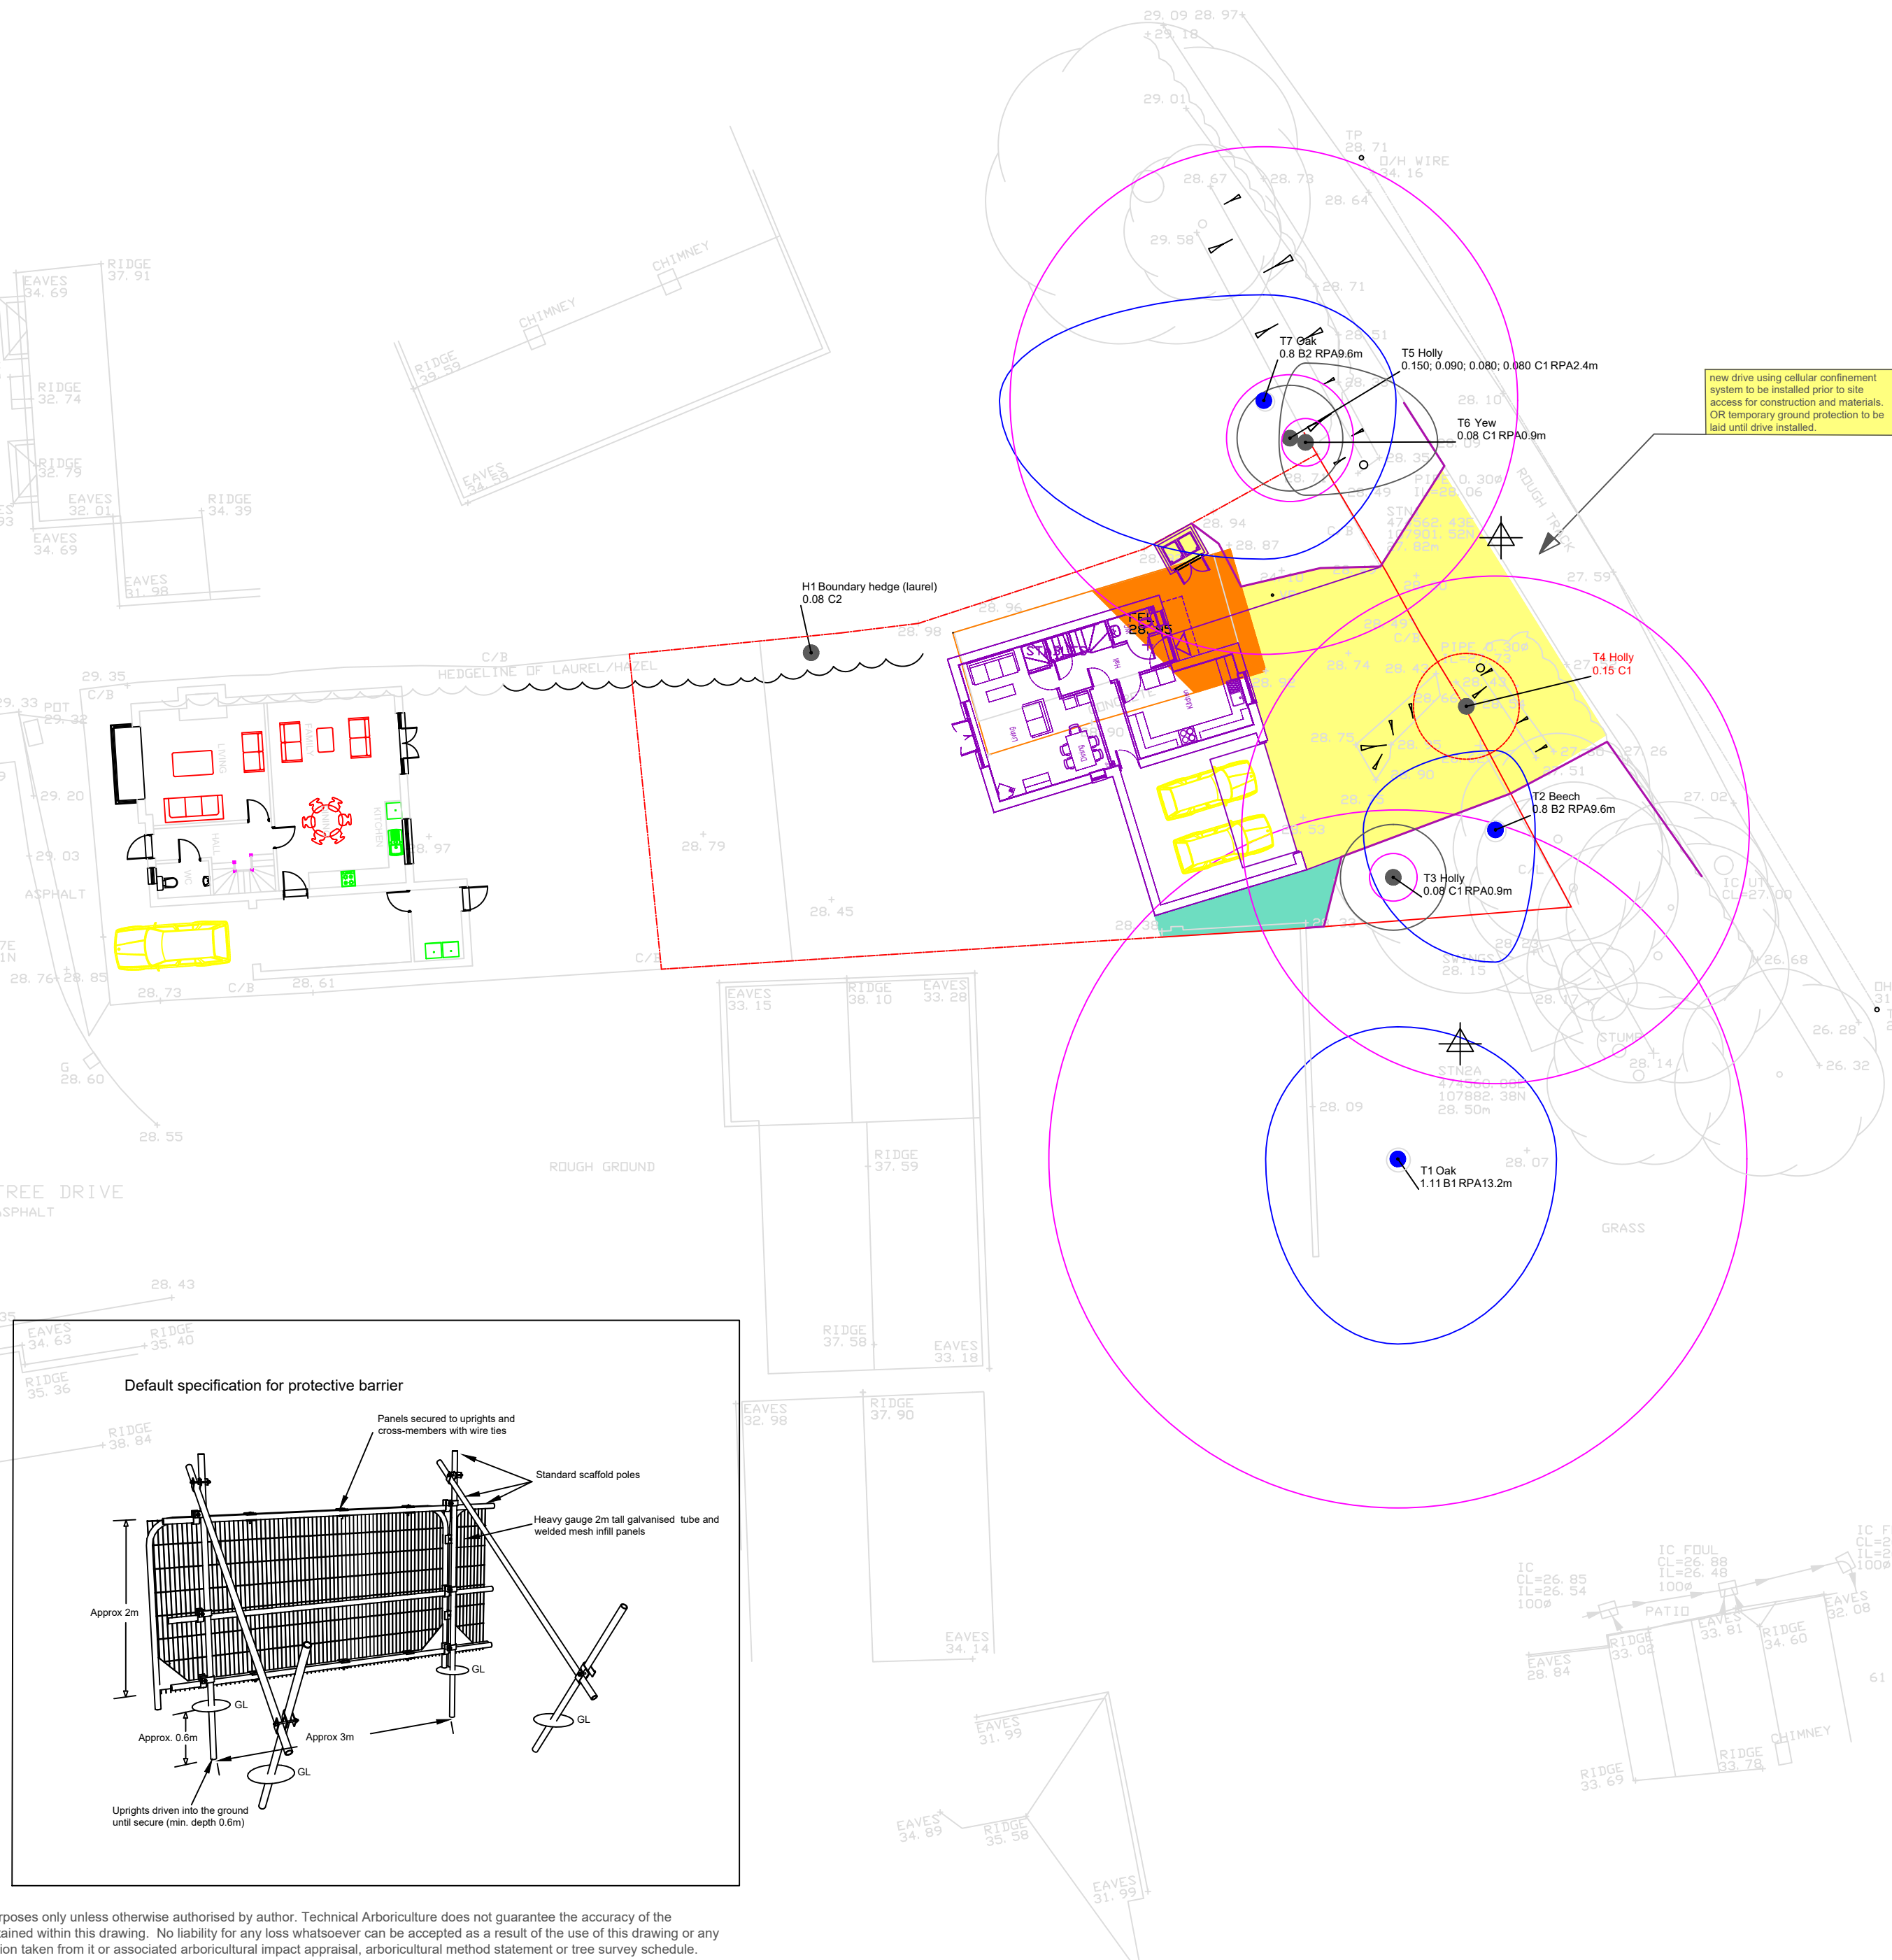

TREE PROTECTION AREA
KEEP OUT!

TREES ENCLOSED BY THIS FENCE ARE PROTECTED
BY PLANNING CONDITIONS AND/OR ARE THE
SUBJECT OF A TREE PRESERVATION ORDER.
CONTRAVENTION OF A TREE PRESERVATION ORDER,
MAY LEAD TO CRIMINAL PROSECUTION
THIS FENCING MUST NOT BE REMOVED WITHOUT
PERMISSION FROM THE TREE AND LANDSCAPE
OFFICER

ATTENTION!





TREE PROTECTION

Tree protection comprises two elements;


1. Fencing AND;
2. ground protection



Do not assume that because you are outside the fence you are outside the RPA.

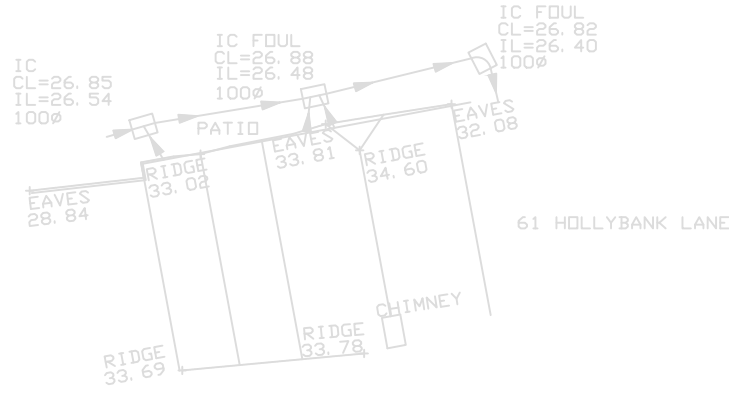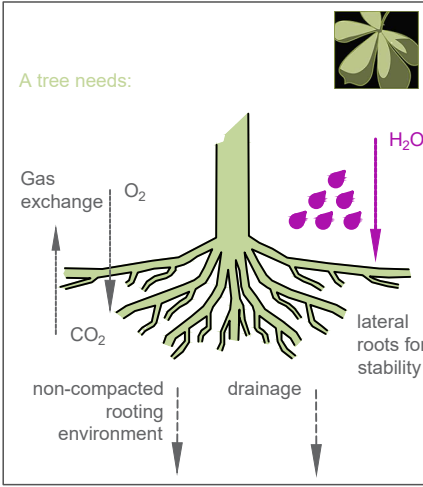

Legend

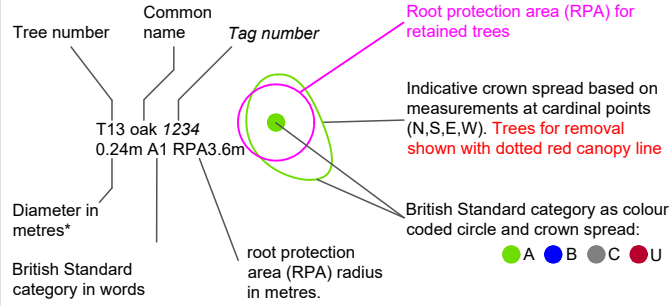

*where the tree is multi stemmed, the figure stated is the calculated combined stem diameter, as recommended by BS5837:2012 (unless otherwise stated in the drawing).

Proposed new development.

Protective fencing to BS5837:2012. Refer to BS5837 figure 2 and figure 3 as appropriate.

Precautions will be required during demolition to prevent damage to RPA and above ground parts of trees. Protective fencing may be relaxed to undertake operations following approval by project arborist and should be replaced once operation is completed. Refer to relevant sections of arboricultural impact appraisal and method statement.

Low impact surfacing will be required to install new access and/or parking areas within RPA to prevent root damage. Protective fencing may be relaxed to undertake operations following approval by project arborist and should be replaced once operation is completed. Refer to relevant sections of arboricultural impact appraisal and method statement.

Space restrictions will require ground protection capable of supporting the level of construction traffic entering the area (refer to guidance in text box within drawing). Refer to relevant sections of arboricultural impact appraisal and method statement.

Ground protection specification for different levels of construction traffic (after BS587:2012):

- Pedestrian movements - scaffold boards placed either on top of a driven scaffold frame to form a suspended walkway; or on top of a compression resistant layer of 100 mm depth of woodchip, laid onto a geotextile membrane;
- Plant (pedestrian operated up to 2 t gross weight) - proprietary, inter linked ground protection boards placed upon a compression resistant layer of 150 mm depth of woodchip, laid onto a geotextile membrane;
- Construction traffic (wheeled or tracked exceeding 2 t gross weight) - an alternative system (e.g. proprietary systems or pre cast reinforced concrete slabs) to an engineering specification designed in conjunction with the project arboricultural consultant, to accommodate the expected loading.

Technical
Arboriculture
www.techarb.co.uk



Technical Arboriculture Limited
1 Chase Farm Close
Waltham Chase
Hampshire
SO32 2UB
01489 896 655 info@techarb.co.uk

PROJECT 61 Hollybank Lane Emsworth
DATE September 2018
JOB REF AIA/AMS-KC/61HOLLYBANK/001
DRAWING NO TCP-KC/61HOLLYBANK/001
DRAWN KC
SCALE 1:200 at A2
STATUS FINAL
REVISION 0

REVISION NOTES

