




Arboricultural Method statement

1.Construction activities must take place from existing hard standing or from protected ground.
2.Unprotected ground within the RPA will be fenced to exclude construction activity, parking, mixing or storage etc.
3.Pre start tree surgery works. Trees along the access route need lifting as indicated to 4.5m above ground level to stop impact damage from breaking branches. Works to be done to BS3998
4.Fencing
Tree protection fencing is specified in BS5837. It must be fit for purpose, tamper-proof, exclude activity with the Root Protection Area (RPA) and resist knocks.
A system such as braced HERAS fencing is suitable such as the default specification at Figure 2 of the BS.
It must have signage affixed to it at maximum 20m intervals.
Fencing must be erected prior to site occupancy. It must remain in place until the end of construction. It will be set out as shown left.
Fencing lines must not be altered or temporarily set back without the prior agreement of the consulting arboriculturist.
The fencing to include the locations proposed for new planting to avoid ground compaction.

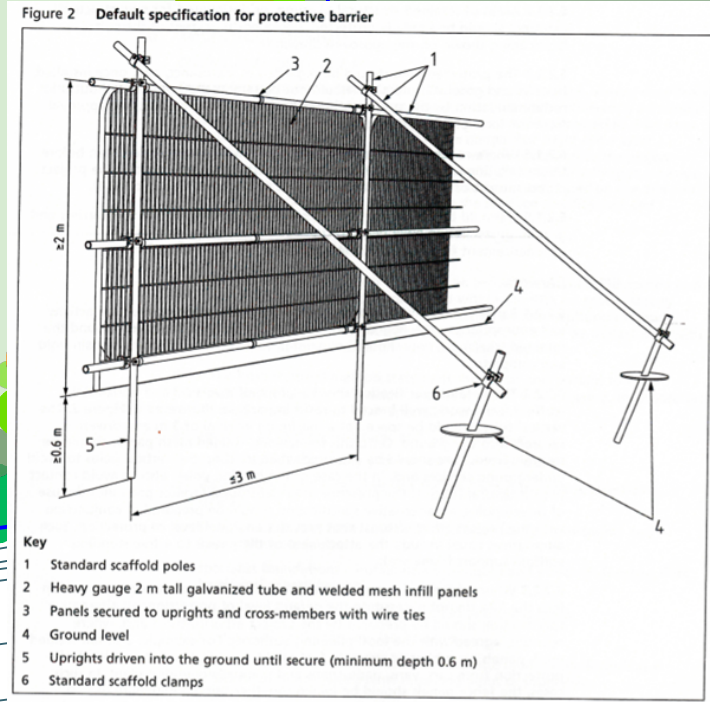

General Notes

1. This drawing is © copyright Hampshire County Council 2023. No unauthorised reproduction of any kind is permitted.

2. No dimensions to be scaled from this drawing. Verify all dimensions prior to construction. Immediately report any discrepancies on the document to the Architect/Contract Administrator. This document shall be read in conjunction with associated models, specifications and related consultant's documents.

3. Drawing to be read with all relevant Architectural, Interiors, Structural, M&E, Drainage/Public Health, Landscape, Civils and Interiors drawings and specifications.


4. This map is reproduced from Ordnance Survey material with the permission of Ordnance Survey on behalf of the controller of Her Majesty's Stationery Office © Crown copyright. Unauthorised reproduction infringes Crown Copyright & may lead to prosecution or civil proceedings (100019180) 2023.

Hampshire County Council

Notes:

Key:

- Vehicle Entrance
- Pedestrian Entrance
- Site Boundary
- Building to be re-clad
- Tarmac Surface
- Sports Pitch
- Playing Field & Soft Landscaping
- New access road tarmac finish over former haul road
- Existing Trees
- Existing Trees (indicative only)
- Crown lift to 4.5m over access road
- Tree Protection fencing



PLANNING

Rev	Description	Date	By	Chkd
P1	SO INITIAL STATUS	22/02/2024	XXX	XXX

HCC Property Services,
Three Ministers House,
76 High Street, Winchester SO23 8UL
tel: (01962) 947801

PROJECT NAME
Crookhorn College

SHEET NAME
Tree Protection Plan and
Arboricultural Method
Statement

DRAWING No.
P-NBC-CrookhornCollege-TTP&AMS-SS23611-1.0

SUITABILITY
code description
SO INITIAL STATUS
