

Tree protection plan
Location of trees, categorisation & protection/management proposals

Dairy Crest Depot, Dunsbury Way, Havant,
Hampshire. PO9 5BQ


Barrell Plan Ref: 22042-2




barrell
TREE CONSULTANCY

Permission is granted to scale from this drawing for Local Authority Planning Approval purposes relating to tree protection measures only. Where applicable this drawing is to be read in conjunction with the arboricultural report. This drawing is the copyright of Barrell Tree Consultancy 2022. ©

This drawing to be reproduced in colour only.
www.barrelltreecare.co.uk

-  BS category B Trees of moderate quality
-  BS category C Trees of low quality
-  Trees to be removed
-  Proposed layout
-  Estimated tree positions not included on original land survey and/or adjusted crown spreads
-  Protective barrier/fencing
-  Construction exclusion zone (CEZ)
-  Construction exclusion zone protected by ground protection
-  Proposed location of new tree planting
-  Root protection area (RPA) boundaries for category A and B trees
-  Root protection area (RPA) boundaries for category C trees

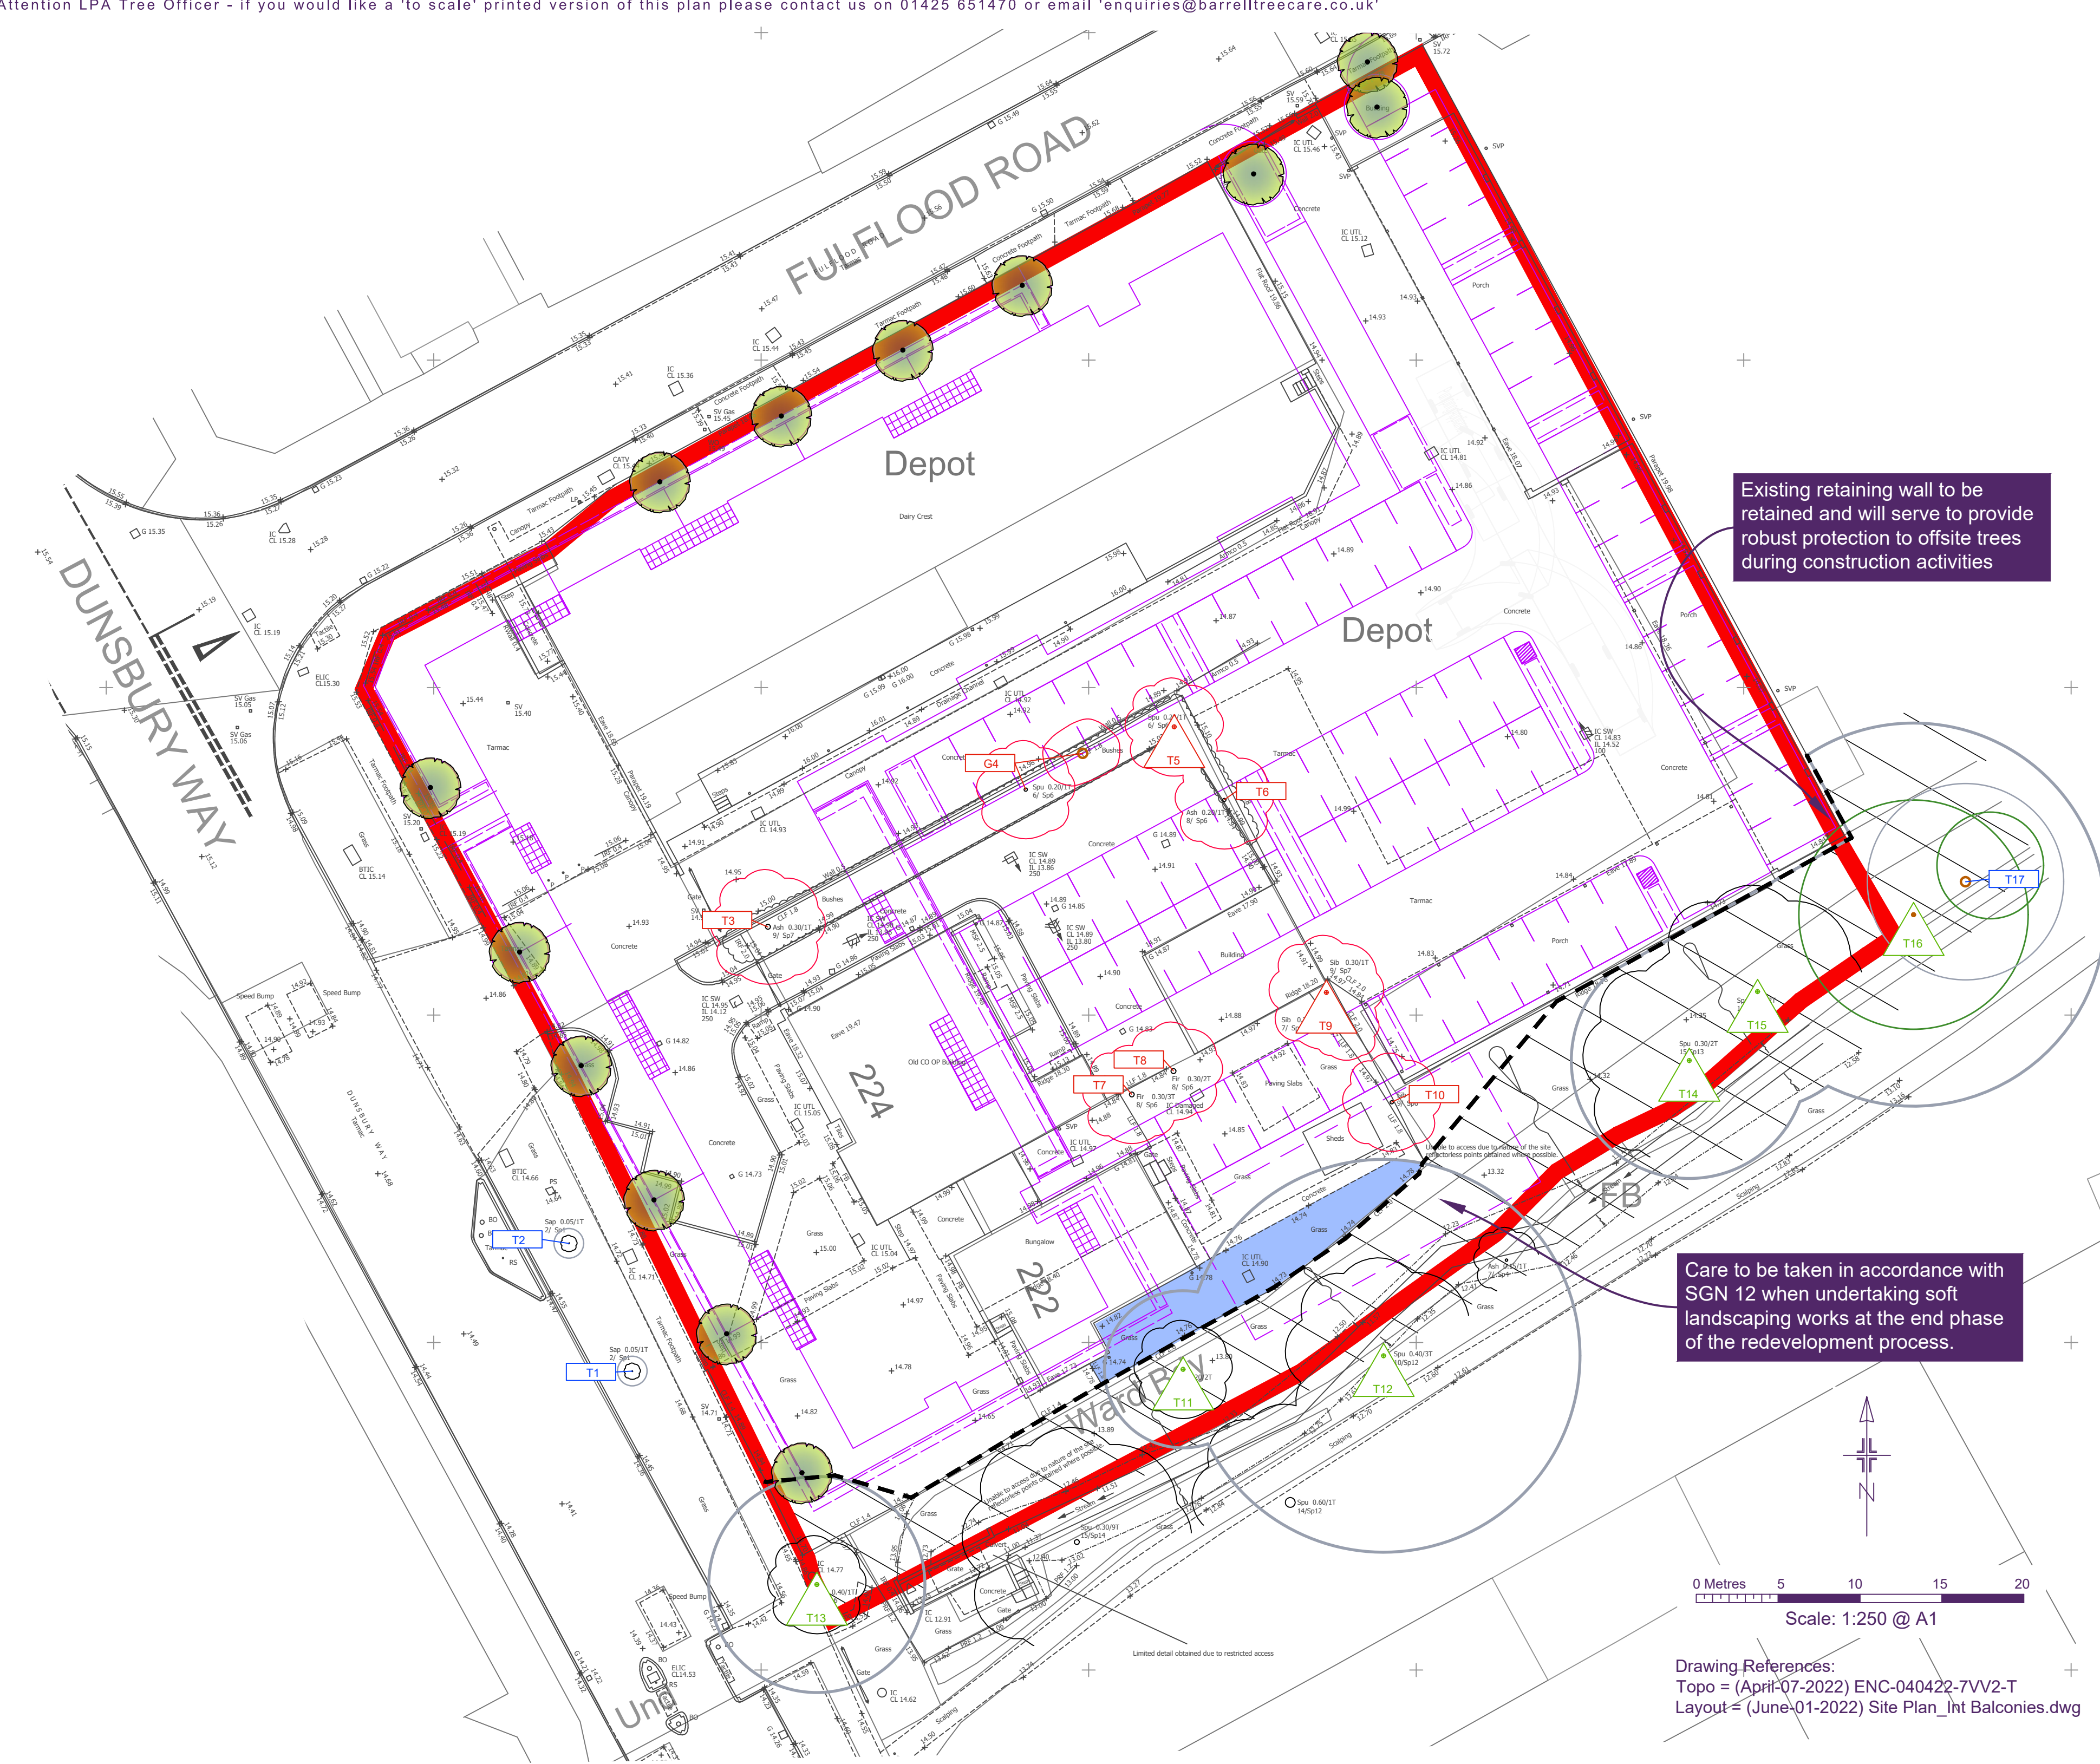

Tree No	Species	Category	RPA Radius	Tree Works
All retained trees				Carry out safety check and lift over site to 3-4 m as necessary.
T1	Cherry	C	0.9	-
T2	Cherry	C	0.9	-
T3	Ash	C	4.8	Fell
G4	Cypress, ash	C	2.4	Fell
T5	Hawthorn	B	4.8	Fell
T6	Ash	C	2.4	Fell
T7	Cypress	C	6.3	Fell
T8	Cypress	C	4.8	Fell
T9	Birch	B	4.8	Fell
T10	Birch	C	4.2	Fell
T11	Hawthorn	B	4.8	-
T12	Willow	B	12.0	-
T13	Apple	B	6.6	-
T14	Alder	B	7.2	-
T15	Alder	B	7.2	-
T16	Alder	B	11.7	-
T17	Alder	C	6.0	-

SGN 1 *Monitoring tree protection*



Always:

- ✓ have a pre-commencement meeting with the tree consultant before development starts
- ✓ use the tree consultant to regularly check that protection remains fit for purpose
- ✓ use the tree consultant to supervise work in RPAs
- ✓ keep a written record of supervision



SGN 3 *Ground protection*



Always:

- ✓ install protection before development starts
- ✓ make sure protection is fit for purpose, i.e. it prevents damage to trees and soil
- ✓ keep protection in place until there is no risk to trees
- ✓ get written permission to move or remove any protection



SGN 11 *Installing services in RPAs*



Always:

- ✓ use the tree consultant to supervise work in RPAs
- ✓ select the least damaging option when installing services, so prioritise trenchless, over broken trench over continuous trench
- ✓ hand-dig trenches if trenchless is not feasible



SGN 2 *Fencing protected trees*



Always:

- ✓ install protection before development starts
- ✓ make sure protection is fit for purpose, i.e. it prevents damage to trees and soil
- ✓ keep protection in place until there is no risk to trees
- ✓ get written permission to move or remove any protection



SGN 4 *Pollution control*



Always:

- ✓ keep toxic products away from RPAs



SGN 12 *Landscaping in RPAs*



Always:

- ✓ use the tree consultant to supervise work in RPAs
- ✓ avoid raising ground levels within 1m of the trunks of retained trees



How to use plan

More detailed guidance on each Site Guidance Note (SGN) can be found in a printed hard copy compilation of all the SGNs, **Manual for Managing Trees On Development Sites version 2.1**, issued to the Site Manager at the pre-commencement site meeting (**Note:** This should be retained on site throughout the duration of works). Additionally, an electronic pdf compilation of all the SGNs, was submitted with this drawing to the local planning authority and the client. Alternatively, a pdf of each SGN can be downloaded by:

1. clicking the image links in the electronic pdf version of this plan;
2. holding a mobile phone QR (Quick Response) code reader over the QR code in the paper version of this plan; or,
3. visiting our website at <https://www.barrelltreecare.co.uk/resources/technical-guidance>
