

Tree protection plan
Location of trees, categorisation & protection/management proposals

Southleigh Park House, Quantell Snell, Eastleigh Road, Havant, Hampshire, PO9 2PE

Barrell Plan Ref: 20122-SchemeBRenumbering



Permission is granted to scale from this drawing for Local Authority Planning Approval purposes relating to tree protection measures only. Where applicable this drawing is to be read in conjunction with the arboricultural report. This drawing is the copyright of Barrell Tree Consultancy 2021. This drawing to be reproduced in colour only.

www.barrelltreecare.co.uk

How to use plan

More detailed guidance on each Site Guidance Note (SGN) can be found in a printed hard copy compilation of all the SGNs, Manual for Managing Trees On Development Sites version 2.1, issued to the Site Manager at the pre-commencement site meeting. (Note: This should be retained on site throughout the duration of works). Additionally, an electronic pdf compilation of all the SGNs, was submitted with this drawing to the local planning authority and the client. Alternatively, a pdf of each SGN can be downloaded by:
1. clicking the image links in the electronic pdf version of this plan,
2. holding a mobile phone QR (Quick Response) code reader over the QR code in the paper version of this plan, or,
3. visiting our website at <https://www.barrelltreecare.co.uk/resources/technical-guidance>


SGN 1 Monitoring tree protection

- Always:**
- have a pre-commencement meeting with the tree consultant before development starts
 - use the tree consultant to regularly check that tree protection remains fit for purpose
 - use the tree consultant to supervise work in RPAs
 - keep a written record of supervision



SGN 7 Excavating in RPAs

- Always:**
- use the tree consultant to supervise work in RPAs
 - use hand tools to dig in RPAs
 - protect exposed roots from sunlight and drying out

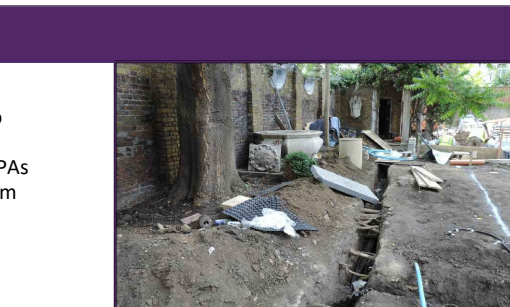

SGN 2 Fencing protected trees

- Always:**
- install protection before development starts
 - make sure protection is fit for purpose, i.e. it prevents damage to trees and soil
 - keep protection in place until there is no risk to trees
 - get written permission to move or remove any protection




SGN 8 Removing surfacing and structures in RPAs

- Always:**
- have a pre-commencement meeting with the tree consultant before development starts
 - use the tree consultant to supervise work in RPAs
 - minimise damage to roots and disturbance to soil in RPAs



SGN 3 Ground protection

- Always:**
- install protection before development starts
 - make sure protection is fit for purpose, i.e. it prevents damage to trees and soil
 - keep protection in place until there is no risk to trees
 - get written permission to move or remove any protection

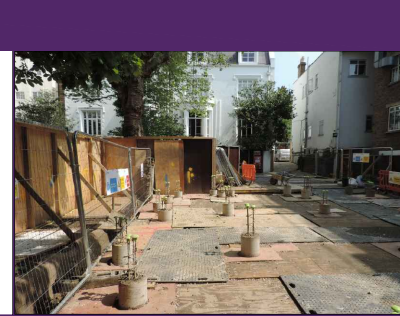

SGN 9 Installing/upgrading surfacing in RPAs

- Always:**
- use the tree consultant to supervise work in RPAs
 - minimise damage to roots and disturbance to soil in RPAs
 - minimise excavation when installing or upgrading surfacing in RPAs



SGN 4 Pollution control

- Always:**
- keep toxic products away from RPAs




SGN 10 Installing structures in RPAs

- Always:**
- use the tree consultant to supervise work in RPAs
 - hand dig, pile, and post locations down to at least 60cm
 - protect White Rot contamination from poured wet concrete



SGN 5 Site cranes & piling rigs

- Always:**
- use the tree consultant to supervise work with cranes and piling rigs in RPAs

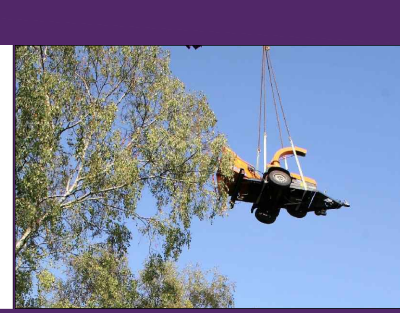

SGN 11 Installing services in RPAs

- Always:**
- use the tree consultant to supervise work in RPAs
 - avoid the least damaging option when installing services, so prioritise trenchless, over broken trench near continuous trench
 - hand dig trenches if trenchless is not feasible



SGN 6 Height restrictions

- Always:**
- prevent the access of vehicles into controlled areas taller than the critical height



SGN 12 Landscaping in RPAs

- Always:**
- use the tree consultant to supervise work in RPAs
 - avoid raising ground levels within 2m of the trunks of retained trees

