



Gifford Tree Service 57 Sea Front Hayling Island Hampshire PO11 0AN
Mobile 07831488456 Email kim@treetesting.com [url:www.treetesting.com](http://www.treetesting.com)

Arboricultural Impact Assessment/Statement and Tree Protection Plan for 14 St. Chatherine's Road Hayling Island Hampshire PO11 .

Prepared by Kim Gifford 26th February 2016

1. Arboricultural Method Statement and Impact Assessment

1.1 The proposal is significantly redesign the existing property of 14 St Catherine's Road Hayling Island Hampshire PO11.

1.2 The following Arboricultural method statement is to provide a protection strategy for the trees immediately adjacent identified in the following Tree Survey and Plan. The Tree Protection Plan (TPP) shows the areas of proposal. Most specimen are classified as B1 category 'specimen of high amenity to the local area'. General observation at the time of inspection is that most trees appear good arboricultural condition and have been maintained on a regular basis. Except for the Chestnut T3 at the front of the property. This specimen has excessive decay it is recommended that it is removed and replanted on the grounds of health and safety.

1.3 The Root Protection Area (RPA) shown require caution to be undertaken to maintain these specimen. Protective barriers as specified in BS5837:2012 (see figure 2 Appendix 1) will be erected before construction. Ref TPP marked as a dashed line. The area of drive way and garage should be constructed with a no dig cellular confined system to reduce the risk of root loss to the adjacent neighboring trees.

1.4 The Oak T1 has a RPA of 8.4m radius. The proposed construction will be undertaken outside of this area as shown on the plan. The Cedar T2 has a RPA of 6m the proposal is outside of this of this area. However precaution need to be implemented by installing ground protection on the front corner of the proposed extension, to limit compaction to this area.

1.5 The operations should be implemented in stages as detailed on the TPP. It is recommended that T3 Chestnut is removed as it is in a poor arboricultural condition extensive cavities and decay in the main stem.

2. Overground Constraints:

2.1 All construction activities will avoid damaging tree canopies and adhere to the exclusion areas under canopies as marked on the Tree protection Plan.

3. Underground Constraints

3.1 Protective fencing and ground protection will be constructed and all works are to be undertaken as with reference to Stages 1 & 2 on the TPP. There will be no construction activity within the RPAs.

4. The project will include a structured procedure of Arboricultural supervision to be detailed in planning conditions. The following method statements should be available on site and conveyed to construction contractors before works commence. The TPP has staged recommendations which should be adhered to without variation unless agreed before.

5.Tree Survey: Schedule

5.1 Method: Visual Tree inspection references, Principles of Tree hazard Assessment and Management by David Lonsdale and The body language of trees by Claus Mattheck and Helge Breuer. The Arboricultural Association guidance note 7 tree surveys a guide to good practice. Lantra award Professional tree inspection. BS5837: 2012 Tree in relation to design, demolition and construction recommendations.

- **Tree Number: T1**
- **Species: Quercus robur (Oak)**
- **Height: 16m>**
- **Stem diameter: 700mm**
- **Crown spreads:N7m E7m S7m W7m**
- **Clearance: 3m>**
- **Root Protection Radius: 8.40m**
- **RPA m2 = 222**
- **Age Class: Very Mature**
- **Physiological Condition: Normal**
- **Structural Condition: Normal**
- **Estimate Life expectancy: 50>**
- **BS5837 Category: B1**
-

Recommendation: Specimen high category protection required. As detailed in TPP.

- **Tree Number: T2**
- **Species: Cedrus (Cedar)**
- **Height: 10m>**
- **Stem diameter: 500mm**
- **Crown spreads:N5m E5m S5m W5m**
- **Clearance: 3m>**
- **Root Protection Radius: 6m**
- **RPA m2 = 113**
- **Age Class: Mature**
- **Physiological Condition: Normal**
- **Structural Condition: Normal**
- **Estimate Life expectancy: 50>**
- **BS5837 Category: B1**
- **Recommendation: Specimen high category protection required. As detailed in TPP.**

- **Tree Number: T3**
- **Species: Aesculus hippocastanum (Horse Chestnut)**
- **Height: 10m>**
- **Stem diameter: 550mm**
- **Crown spreads: N5m E5m S5m W5m**
- **Clearance: 3m>**
- **Root Protection Radius: N/A**
- **RPA m2 = N/A**
- **Age Class: Mature**
- **Physiological Condition: Decayed Cavities**
- **Structural Condition: Decayed**
- **Estimate Life expectancy: N/A**
- **BS5837 Category: U**
- **Recommendation: Remove within the near future.**

- **Tree Number: T4**
- **Species: Sorbus**
- **Height: 6m>**
- **Stem diameter: 100mm**
- **Crown spreads: N3m E5m S3m W3m**
- **Clearance: 1m>**
- **Root Protection Radius: 1.2m**
- **RPA m2 = 5**
- **Age Class: Young**
- **Physiological Condition: Normal**
- **Structural Condition: Normal**
- **Estimate Life expectancy: 50>**
- **BS5837 Category: C**
- **Recommendation: Included in TPP**

- **Tree Number: T5**
- **Species: *Fraxinus excelsior* (Ash)**
- **Height: 10m>**
- **Stem diameter: 400mm**
- **Crown spreads: N5m E5m S5m W5m**
- **Clearance: 3m>**
- **Root Protection Radius: 4.8m**
- **RPA m² = 72**
- **Age Class: Mature**
- **Physiological Condition: Normal**
- **Structural Condition: Normal**
- **Estimate Life expectancy: 50>**
- **BS5837 Category: B1**

• **Recommendation: Specimen high category protection required. As detailed in TPP.**

- **Tree Number: T6**
- **Species: *Aesculus hippocastanum* (Chestnut)**
- **Height: 15m>**
- **Stem diameter: 600mm (Twin stemmed)**
- **Crown spreads: N5m E5m S5m W5m**
- **Clearance: 7.2m>**
- **Root Protection Radius: 6m**
- **RPA m² = 163**
- **Age Class: Mature**
- **Physiological Condition: Normal**
- **Structural Condition: Normal**
- **Estimate Life expectancy: 50>**
- **BS5837 Category: B1**

• **Recommendation: Specimen high category protection required. As detailed in TPP.**

- **Tree Number: T7**
- **Species: Quercus ilex (Holm Oak)**
- **Height: 10m>**
- **Stem diameter: 600mm (Twin stemmed)**
- **Crown spreads:N5m E5m S5m W5m**
- **Clearance: 7.2m>**
- **Root Protection Radius: 6m**
- **RPA m2 = 163**
- **Age Class: Mature**
- **Physiological Condition: Normal**
- **Structural Condition: Severely cut back on neighbours side.**
- **Estimate Life expectancy: 50>**
- **BS5837 Category: B1**
- **Recommendation: Specimen high category protection required. As detailed in TPP.**

- **Tree Number: T8**
- **Species: Prunus**
- **Height: 9m>**
- **Stem diameter: 200mm**
- **Crown spreads:N3m E3m S3m W3m**
- **Clearance: 2.4m>**
- **Root Protection Radius: 2.4m**
- **RPA m2 = 18**
- **Age Class: Mature**
- **Physiological Condition: Dying back**
- **Structural Condition: Normal**
- **Estimate Life expectancy: 10>**
- **BS5837 Category: C**
- **Recommendation: Specimen protection required. As detailed in TPP.**

- **Tree Number: T9**
- **Species: Ilex (Holly)**
- **Height: 9m>**
- **Stem diameter: 200mm**
- **Crown spreads: N3m E3m S3m W3m**
- **Clearance: 2.4m>**
- **Root Protection Radius: 2.4m**
- **RPA m² = 18**
- **Age Class: Mature**
- **Physiological Condition: Normal**
- **Structural Condition: Normal**
- **Estimate Life expectancy: 10>**
- **BS5837 Category: C**
-

Recommendation: Specimen protection required. As detailed in TPP.

6. Contacts:

Local Authority Arboricultural officer
Site Agent
Appointed arboriculturist

6.1 No contractors have been appointed at this stage. If there is a need to review any of the protection plans/method statements in light of additional requirements identified by contractors, written approval for any such modifications will be obtained from the LPA prior to commencement of any work.

7. Specific Methods to be applied during all operations 14 St. Catherine's Road Hayling Island.

7.1 The methodology of the tree protection measures follows a logical sequence of development events. Variations to the sequence could significantly reduce the efficiency of the tree protection measures. Variations to the proposed development will require input prior to commencement of the variations, from the appointed arboriculturist and/or the LPA Arboricultural officer.

7.2 The LPA will be given notice in writing 5 full working days prior to the date of commencement of development to check all tree protection in place.

7.3 All development works within the RPA of any retained tree will be carried out strictly in accordance with the Arboricultural method statement.

7.4 It is recommended that works within the RPA, as well as the installation & modification of all tree protection measures, are carried out under supervision by an arboriculturist. It is the responsibility of the client to appoint an arboriculturist prior to commencement of works. Details of the appointed arboriculturist will be forwarded to the LPA. TBC.

7.5 A schedule of activities that will require Arboricultural supervision at various stages has been produced. This should form the minimum site attendance by the appointed arboriculturist, as well as the Local Authority tree officer (where relevant).

7.6 Periodic reports, along with supporting evidence, will be submitted to the LPA on the tree protection measures, as well as the results of activities within the RPAs of retained trees.

8. Preliminary tree maintenance.

8.1 **Remove Chestnut T3.** Prior to carrying out any tree work, all trees recommended for tree work/removal including their immediately adjacent trees, will be inspected for bird nests (wholly and partially built ones). In the event nests are found, the tree work will not be carried out until the trees are found to be free of the nesting birds & their young. This is a requirement under the Wildlife & Countryside Act 1981 & The Countryside & Rights Of Way Act 2000.

8.2 Should any works become apparent during the construction period. All tree work will be carried out in accordance with **BS3998:2010** and will be carried out without harming retained trees.

9. Preliminary vegetation control.

9.1 Cut only vegetation necessary construction area directly adjacent to the proposal before construction. TBC

10. Preliminary tree protection methods.

Prior to development, the following measures will be carried out:

10.1 All preliminary tree work should be carried out in a way that does not damage the retained trees and/or their rooting mediums and/or their roots.

10.2 **Stage 1 on the TPP.** Protective fencing of the type shown in the protection plan will be placed in the positions indicated on the protection plan. The fencing will be permanently fixed to the ground as shown in the plans, or fixed to a permanent feature. Weatherproof signs will be attached to the fencing, stating their purpose and that they should not be moved.

Stage 2 on the TPP: Ground protection to be installed as TPP example on drawing..

10.3 Ground protection adjacent to T2 as shown on the plan. This will be supervised by the appointed arboriculturist.

10.4 Prior to commencing work on site, all contractors will be given an induction on the tree protection measures employed during the development project and on the potential consequences of disregarding them (pre-commencement meeting).

11. Arboricultural Methods and restrictions during all phases of development:

The following tree protection measures will be adopted throughout the life of the development:

11.1 The fencing comprising the construction exclusion zone will not be moved, except if specified in the tree protection plans. All staff on site will understand the need for protective fencing, as well as any ground protection and to keep strictly within the designated access routes, when moving in/out the site.

11.2 Protective fencing will be maintained & inspected on a weekly basis by the site manager. Inspections will be recorded on an inspection form.

11.3 All damage to protective fencing or accidental damage to trees will be reported to the site manager immediately. Works occurring within the incident vicinity will cease immediately until adequate tree protection measures are re-established. A record of the damage will be made by the site manager and, in consultation with the appointed Arboricultural consultant, remediation measures carried out.

11.4 No materials and/or plant will be stored within the designated root protection area of any of the trees and/or within the delimited construction exclusion areas. Any liquid materials to be stored on site, will be located where, in any event of spillage, will allow for natural run-off to be away from the designated root protection areas and buffer zones and/or stored within a pre-constructed spillage containment area.

11.5 The mixing of concrete and mortar will be performed contained, in such an area where in the event of any spills, any liquid will drain away from the root protection areas and any buffer zones and/or within a pre-constructed spillage containment area.

11.6 There will be no use or movement of any cranes/heavy lifting arms/digger arms and booms of delivery vehicles will be carried out without damage to any part of the retained trees.

11.6 No dry construction materials will be stored within the RPAs of the retained trees, unless adequate ground protection (approved by the appointed arboriculturist), has been installed within the storage area.

11.7 No soil, demolition debris, or any other arisings will be stored within the RPAs or under canopies of the retained trees, whichever is the greater.

11.8 No ground level changes will occur (no grading/levelling/raising), within any RPAs of the retained trees, unless consented to by the LPA & supervised by the appointed arboriculturist. Changes to the ground levels within RPAs of retained trees will follow the advice of the appointed arboriculturist. The existing wall is to be removed and reconstructed by hand only in the same areas and not expanding any excavation.

11.9 No additional tree work will be carried out unless consented to in writing by the LPA

11.10 The positions of all site welfare and storage areas will also be located outside any canopy areas & RPAs of any retained trees.

11.11 No fires will be lit within any RPAs or canopies of retained trees, whichever is the greater

11.12 For the purposes of this method statement, significant roots referred to, constitute individual roots of diameters of 25mm and above, as well as dense fibrous root masses. The significance of both will be determined by an appointed arboriculturist upon discovery of either.

11.13 If roots 20mm and smaller in diameter are damaged that belong to retained trees, these should be cut cleanly and covered in damp Hessian or soil. If roots 25mm and larger are damaged or if a large number of smaller roots are damaged, these should be covered in damp Hessian or soil and advice should be sought from the appointed arboriculturist prior to treating them

12. **Demolition/Preparation:**

12.1 A pre-commencement site meeting will be carried out by all involved in the construction and the supervising arboriculturist, to clarify tree protection measures.

12.2 Tree protection measures will have been installed prior to any commencement of demolition site preparation.

12.3 No plant machinery will encroach on the RPA of the retained trees, unless the ground is adequately protected & the machinery is incapable of striking the canopy or tree stem. If plant machinery is to encroach on protected RPAs of retained trees, this will be supervised by the appointed arboriculturist.

12.4 The protective fencing in the site (protecting trees), will be retained in situ until landscaping operations are to be undertaken. This will provide additional protection for the Root Protection Areas.

12.5 Debris from any preparation work will not be stored within any RPAs of retained trees at any time.

12.6 The tree protection measures will be retained in the positions specified on the Protection Plan.

Structure foundations within RPAs:

12.7 The foundations for the proposed does not encroach on the RPA as detailed on TPP. If roots are encountered, these will be cut cleanly. Excavations in this area will be supervised by the appointed arboriculturist. .

Underground services:

12.9 The excavations for any underground services will be routed outside any RPAs. Underground services be run outside RPAs. Any roots that span the trench during digging will not be cut, but will have damp Hessian sacking placed around them. Damaged roots of up to 2cm diam will, where possible, be cut cleanly and covered. Any substantial roots (larger than 25mm diam), that become damaged or need to be removed, advice will first be sought from the supervising arboriculturist prior to any work being carried out on them. This will be carried out under Arboricultural supervision

12.10 If and when installing infrastructure for underground services, they will be done by hand within any RPA and care will be taken not to damage the exposed roots. Back-fill within an RPA will not be compacted and will possess the same soil profile as the surrounding soil. If there is a need to compact Backfill, in preparation for the reinstatement and/or installation of infrastructure within an RPA, then CU structural soil will be used as Backfill. The above will only be applicable with permission from the LA.

12.11 The timing of any excavations for underground services will coincide with the arrival of materials to be used for the construction of the underground services, to minimise the time that roots are exposed.

13.Landscaping:

13.1 Landscaping operations will commence only when all main construction work has ceased. The protective fencing will be removed immediately prior to commencing these operations.

13.2 No soil lowering will occur within any RPA's.

13.3 The existing soil levels will not be raised within RPAs of retained trees without seeking advice from the appointed Arboricultural consultant.

13.4 Excavations for planting within RPA carried out by hand only down to 600mm. The same will apply for introduction of topsoil, plant transport & mulching.

13.5 All landscaping work within RPA will also be carried out by hand only.

Footpaths/hard surfaces:

13.6 Any exposed roots will be covered with damp Hessian. Debris from the excavation will not be stored in this area but will be immediately removed from the RPA.

13.7 General purpose topsoil to BS3882:2007 will be used to replace the previous hard surface if necessary. N/A

Boundary treatments within RPAs:

13.8 Boundary fences are not proposed to be installed within the RPAs of T1 and T2

14. Post-development tree Care and amelioration

14.1 Once all construction and landscaping activities have been completed, any remaining ground protection/protective fencing will be removed.

14.2 A detailed visual inspection of the retained trees on the site & their RPAs, will be carried out, to check for signs of development damage to both the trees and their rooting environment.
Appropriate remedial tree / soil work will then be recommended by an arboriculturist.

14.3 Any damaged branches will be removed or pruned cleanly in line with current good Arboricultural practice (BS3998:2010) and any specific Arboricultural advice. Any other remedial work will also be carried out as and when recommended.

14.4 An annual tree inspection regime will be implemented to monitor the health of the retained and replaced trees for an agreed period after the development project is complete. The appointed arboriculturist will provide reports to the client & the local authority tree officer at agreed times, on the condition of the retained trees and any remediation work recommended.

15. Site Supervision

15.1 BS5837:2012 recommends site supervision at regular intervals as detailed in the TPP and above stages 1 and 2. Details to be agreed subject to conditions.

This concludes the method statement.

Kim Gifford
Arboricultural Consultant


on retained hard surfacing or it is otherwise unfeasible to use ground pins, e.g. due to the presence of underground services, the stabilizer struts should be mounted on a block tray (Figure 3b).


NOTE 1 Examples of configurations for steel mesh perimeter fencing systems are given in BS 1722-18.

NOTE 2 It might be feasible on some sites to use temporary site office buildings as components of the tree protection barriers, provided these can be installed and removed without damaging the retained trees or their rooting environment.

6.2.2.4 All-weather notices should be attached to the barrier with words such as: "CONSTRUCTION EXCLUSION ZONE – NO ACCESS".

Figure 2 Default specification for protective barrier

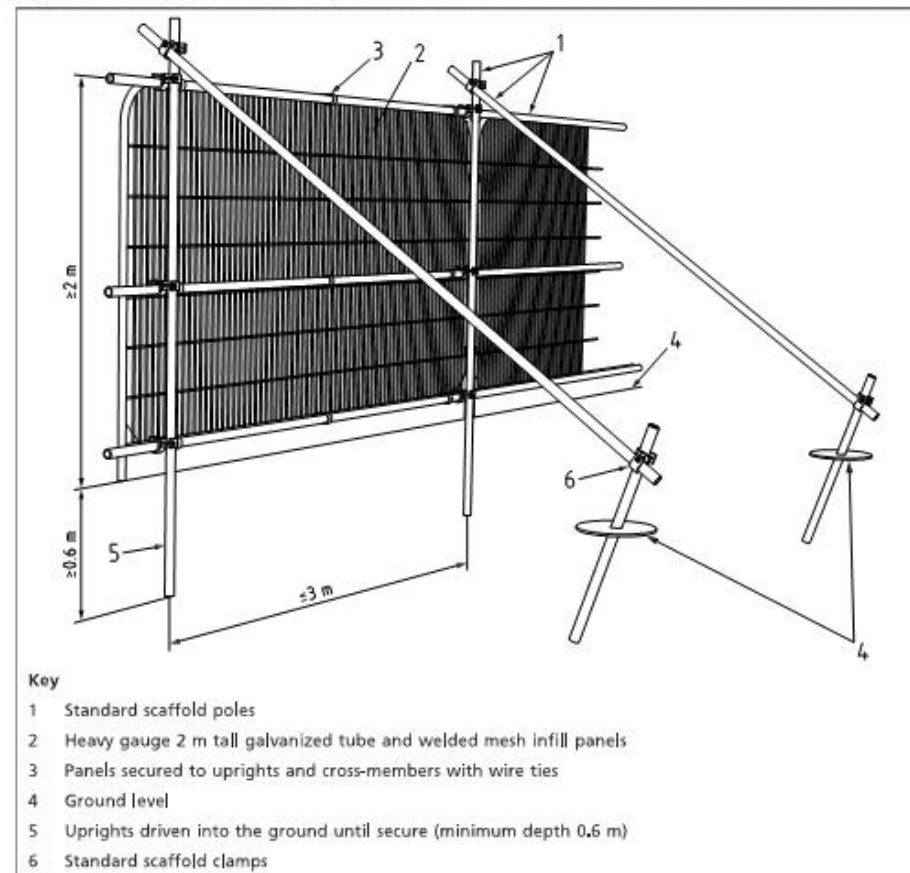

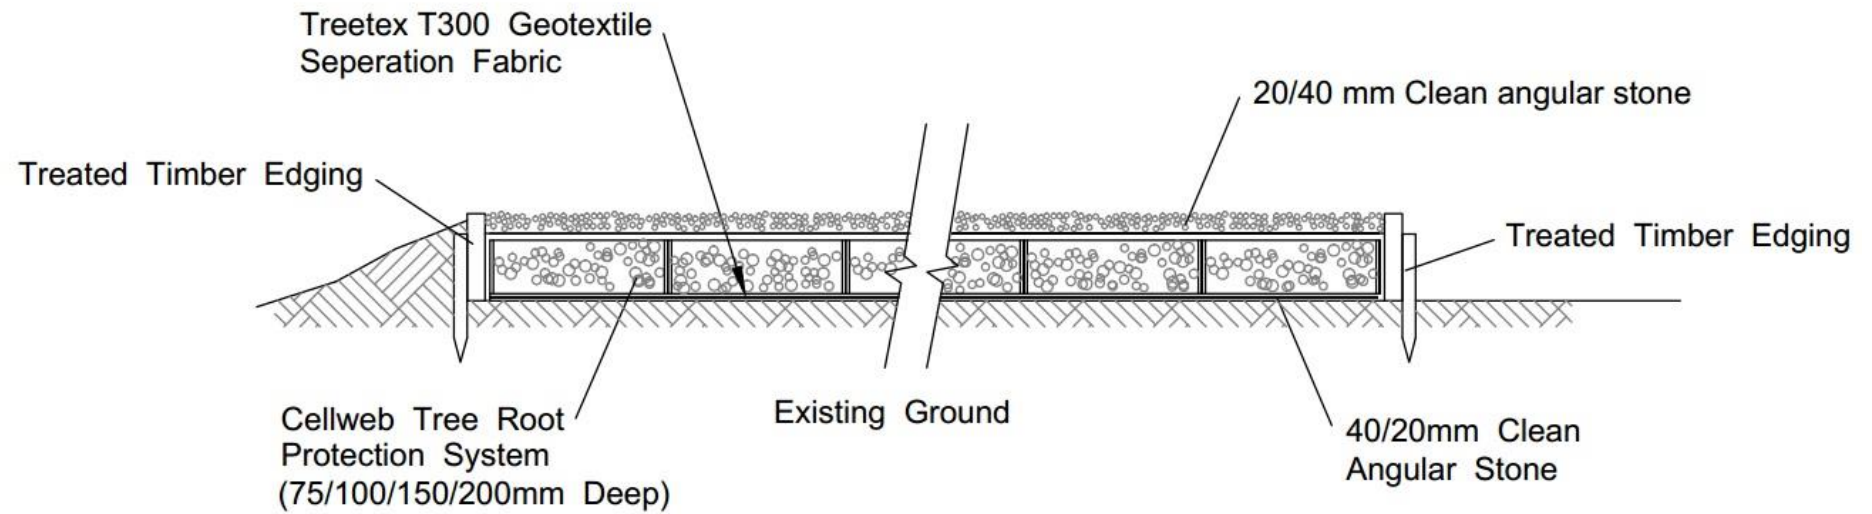

Ground Protection Example
