



Arboricultural Impact Appraisal and Method Statement

St Michaels Convent, Waterlooville

Prepared by
Phillip Brophy HND Arb MA ArborA CEnv MICFor

Date: 12 July 2012
Ref: 11373-AIA3-PB

Validation statement

This report contains the supporting tree information relating to the development proposal to redevelop St Michaels Convent, Waterloooville to provide eighty two new residential dwellings.

For Local Planning Authority (LPA) validation purposes, this report contains the following:

- A full tree survey compliant to the requirements of ***BS5837: (2012 Trees in relation to design, demolition and construction – Recommendations*** undertaken by a qualified arboriculturist
- A plan with a north point showing tree survey information, including BS 5837 categories
- An assessment of the arboricultural implications of development, detailing trees to be retained and removed, and the proposed protection measures (Section 1)
- An arboricultural method statement describing a feasible means of tree protection, its implementation and the phasing of works (Sections 2 and 3)

Summary

Purpose of this document

This is an arboricultural impact appraisal report describing the trees on and near the site, what the impact of the development proposal on those trees will be and how any adverse impact will be mitigated. It also includes an arboricultural method statement describing how trees will be protected and managed during the development. Its purpose is to provide sufficient tree information for the LPA to assess the impact of the proposal on local character in the context of local plan policy, as part of the process of determining the planning application.

The contents of this document

- a **tree protection plan** showing the location of the trees, their categorisation, the location of the new development, the trees to be lost and the tree protection measures;
- an **arboricultural impact appraisal** in Section 1, which describes the impact of the development on trees;
- an **arboricultural method statement** in Section 2, which describes the tree protection measures, and how they will be implemented; and
- a series of **appendices** in Section 3 providing relevant background information and more detailed guidance to supplement the explanations in Section 2.

Background administrative information

Background information on our specific instructions and how we carried them out is included as Appendix 1. All the trees that could be affected were inspected and their details are listed in Appendix 2. Based on this information, guidance was provided to Pope Priestley Architects LLP on the constraints these trees impose on the use of the site. The current layout is a result of this detailed consultation and has evolved taking full account of these constraints.

Summary of the impact on trees and local character

The majority of trees to be lost because of this proposal are low category because of their poor condition or small size. Although the significant boundary tree cover will remain broadly intact a small number of high category trees will also need to be removed. However, these better quality trees are predominately located well within the site and significantly obscured from the majority of public vantages. Given their locations the removal of these trees will have no significant impact on the present character of the area. There is plenty of space for tree planting and a comprehensive new landscape scheme using heavy standard and semi-mature trees included as part of the proposal. The size of these new trees and their future growth will significantly enhance the contribution of this site to local amenity and more than compensate for the loss of existing trees. The proposed changes may affect further trees if appropriate protective measures are not taken. However, if adequate precautions to protect the retained trees are specified and implemented through the arboricultural method statement included in this report, the development proposal will have no significant impact on the contribution of trees to local amenity or character.

Phillip Brophy HNDArb MARborA CEnv MICFor

Explanatory notes for the tree protection plan

The tree protection plan (our reference 11373-BT4a-c) is based on the provided information. It should only be used for dealing with the tree issues and all scaled measurements must be checked against the original submission documents. The precise location of all protective measures should be confirmed at the pre-commencement meeting before any demolition or construction activity starts. Its base is the existing land survey with the proposed layout superimposed, so the two can be easily compared. It shows:

- the existing trees numbered, with high categories (A & B) highlighted in green triangles and low categories (C & U) highlighted in blue rectangles;
- the trees to be removed indicated by a red dashed crown outline; and
- the location of the construction exclusion zone (CEZ) to be protected by barriers formed by fencing and/or ground protection; and
- the location of precautionary areas outside the fencing where special care will be taken.

Section 1

Arboricultural impact appraisal

This arboricultural impact appraisal describes our assessment of how the proposal will affect trees and any impact this will have on local amenity and character. The impact on trees is summarised at the beginning in 1.1, more detailed explanation of this analysis is set out in 1.2 and the proposed mitigation measures are described in 1.3.

Section 1: Arboricultural impact appraisal

1.1 SUMMARY OF THE IMPACT ON TREES

Development proposals can impact on trees by causing them to be removed, by adversely affecting their health through disturbance in root protection areas (RPAs) or by severe pruning. However, in many instances, disturbance to trees close to development activity can be reduced to tolerable levels through the use of precautionary measures. Our assessment of the trees that will be affected by this proposal and those that need to be protected by special precautions are summarised in Table 1 where each tree and group is identified by its individual number.

Table 1: Summary of trees that will be affected and protected

	British Standard 5837 category		
	A (High quality)	B (Moderate quality)	C (Low quality)
Trees/groups to be removed	72	10, 30, 41, 43, 44, 65, 66, 70, 77, 90, 92	1, 4, 5, G9 (part), 11, 25, 26, 34, 35, G37, 38, 39, 40, G42, 46, 48, 49, 50, 55, G58, G61, 62, G63, 64, 67, 68, 71, 79, 80, 81, 82, 83, 84, 86, 87, G88, H89, 91, G93 (part), G94, G95 (part), G96 (part)
Trees/groups to be protected through special precautions (other than fencing and ground protection)	24, 54, 59, 69	8, 12, G13, 27, 28, G52, 53, 56, 60	7, 33

Abbreviations: G = group; H = hedge

1.2 DISCUSSION OF THE IMPACT ON VISUAL AMENITY

1.2.1 Trees to be removed for development (10, 30, 41, 43, 44, 65, 66, 70, 72, 77, 90 and 92)

One category A tree and eleven category B trees will be removed. These trees are located well within the site and with the exception of tree 41, have no significant prominence as skyline features from any surrounding public viewpoints. Despite having the potential for long term retention, their removal will have very little impact on local amenity because of the backdrop of large trees to be retained. These significant retained trees will buffer any loss in the short term whilst the proposed new tree planting becomes established and matures.

Thirty individual, seven groups, one hedge and parts of four other groups of category C trees will be removed. None of these trees are of sufficient importance due to small size, poor condition or sustainable structural form to be worthy of influencing any layout. They are not important in the overall planning context and their loss should not influence the determination of this application.

Section 1: Arboricultural impact appraisal

1.2.2 **Trees to be protected through the use of special precautions (7, 8, 12, G13, 24, 27, 28, 33, G52, 53, 54, 56, 59, 60 and 69)**

All the retained trees will be protected from damage by the use of barriers (fencing and ground protection). Additionally, in the precautionary area shown on the tree protection plan, special precautions relating to the management of existing and new structures, surfacing and services will be required. All these protective measures are shown on the plan and explained in the arboricultural method statement in Sections 2 and 3 of this report. If the precautions set out in this arboricultural method statement are implemented as described, these trees can be successfully retained without any adverse impact on them or on visual amenity.

1.2.3 **Trees advised for removal for management reasons (36, 45, 47, 76, 78, 85, 98 and 104)**

In addition to trees to be removed because of the development proposal, further trees have been advised for removal in the interest of good management. These works are advisory and are not a direct result of this proposal, so they should not be attributed to it. They are not listed in Table 1 for that reason.

1.3 PROPOSALS TO MITIGATE ANY IMPACT

1.3.1 **Protection of retained trees**

The successful retention of trees depends on the quality of the protection and the administrative procedures to ensure those protective measures remain in place whilst there is an unacceptable risk of damage. An effective means of doing this is through an arboricultural method statement that can be specifically referred to in a planning condition. An arboricultural method statement for this site is set out in Sections 2 and 3 of this report. Implementation of this method statement will allow all the retained trees to survive without any adverse impact and allow them to continue to contribute to local amenity and character.

1.3.2 **New tree planting**

As part of the redevelopment proposal, a comprehensive new landscaping scheme has been drafted by TGD Landscape Ltd that includes provision for a significant number of new heavy-standard and extra heavy standard trees to be planted around the site in sustainable locations. One of the key design objectives of the new tree planting element of this scheme was to select and propose suitable trees that would integrate within their setting and therefore enable them to reach their mature dimensions without causing excessive inconvenience and therefore maximise long term sustainability. Secondly the selection of species sought to be reflective and of the surrounding landscape character of the wider area whilst maintaining its own overall identity and that of the development scheme as a whole. Additionally, where appropriate (such as The Green and the Hermitage stream), the design sought to enhance, diversify and strengthen existing levels of tree cover. The detail of this scheme will remain flexible and open to amendment if necessary.

Section 1: Arboricultural impact appraisal

1.4 SUMMARY OF THE IMPACT ON VISUAL AMENITY

The majority of trees to be lost because of this proposal are low category because of their poor condition or small size. Although the significant boundary tree cover will remain broadly intact a small number of high category trees will also need to be removed. However, these better quality trees are predominately located well within the site and significantly obscured from the majority of public vantages. Given their locations the removal of these trees will have no significant impact on the present character of the area. There is plenty of space for tree planting and a comprehensive new landscape scheme using heavy standard and semi-mature trees included as part of the proposal. The size of these new trees and their future growth will significantly enhance the contribution of this site to local amenity and more than compensate for the loss of existing trees. The proposed changes may affect further trees if appropriate protective measures are not taken. However, if adequate precautions to protect the retained trees are specified and implemented through the arboricultural method statement included in this report, the development proposal will have no significant impact on the contribution of trees to local amenity or character.

Section 2

Arboricultural method statement

This is an arboricultural method statement describing how trees will be protected and managed during the development of the site. Its purpose is to explain how and when the protection measures should be installed, and how they will be maintained for the duration of the development activity.

The following explanations relate specifically to this site and they should be read in conjunction with the attached plan. Appendix 3 sets out further guidance to supplement the following explanations.

A copy of this report must be permanently available on site for the duration of the development activity. It can be:

- included in tendering documentation to identify and quantify the tree protection and management requirements;
- used to plan the timing of site operations to minimise the impact on trees; and
- referenced on site for practical guidance on how to protect important trees.

Section 2: Arboricultural method statement

2.1 ARBORICULTURAL SUPERVISION

2.1.1 General principles

An arboricultural consultant will be appointed by the developer to advise on the tree management for the site and to attend:

1. the pre-commencement meeting before any work starts;
2. regular supervision visits as agreed at the pre-commencement meeting; and
3. as needed to oversee any specific works that could affect trees.

Additionally, the consultant will have a supervisory input into operations that could adversely affect protected trees (see 2.2 below).

2.1.2 Detailed proposals

More specifically, the form and purpose of the supervision will be as follows:

- **Pre-commencement meeting:** A pre-commencement meeting will be held on site before any of the site clearance and construction work begins. This would normally be attended by the site manager, the arboricultural consultant and a LPA representative. If a LPA representative is not present, the arboricultural consultant will inform the LPA in writing of the details of the meeting. All tree protection measures detailed in this document will be fully discussed so that all aspects of their implementation and sequencing are understood by all the parties. This will include agreeing the form and location of the most appropriate combination of fencing and/or ground protection to be used as barriers for the CEZ. Any agreed clarifications or modifications to the consented details will be recorded and circulated to all parties in writing. This meeting is where the details of the programme of tree protection will be agreed and finalised, which will then form the basis of any supervision arrangements between the arboricultural consultant and the developer.
- **General site management:** It is the developer's responsibility to ensure that the details of this arboricultural method statement and any agreed amendments are known and understood by all site personnel. Copies of the agreed documents will be available on site and the site manager will brief all personnel who could have an impact on trees on the specific tree protection requirements. This will be a part of the site induction procedures and written into appropriate site management documents.
- **Ongoing supervision of operations that could affect trees:** Once the site is active, the arboricultural consultant will visit at an interval agreed at the pre-commencement site meeting. This would normally be every two to four weeks for general supervision, but could be at a longer interval if agreed between the parties. The supervision arrangement will be sufficiently flexible to allow the supervision of all sensitive works as they occur. The arboricultural consultant's

Section 2: Arboricultural method statement

initial role is to liaise with the developer and the LPA to ensure that protective measures are fit for purpose and in place before any works start on site. Once the site is working, that role will switch to monitoring compliance with arboricultural planning conditions and advising on any tree problems that arise or modifications that become necessary.

- **Proof of compliance to help refute liability and facilitate the discharge of planning conditions:** All supervisory visits will be formally confirmed in writing and circulated to all relevant parties, including the LPA. The purpose of these written records is firstly to provide proof of compliance that will allow the developer to robustly demonstrate adherence to best practice in the event of any disputes, and secondly to help the LPA efficiently discharge the relevant planning conditions.

2.2 PROGRAMME AND PHASING OF TREE MANAGEMENT

In overview, it is anticipated that the following on-site arboricultural input is likely to be needed:

1. Pre-commencement meeting
2. Preliminary tree felling and pruning
3. Installation of CEZ barriers (fencing and/or ground protection)
4. Careful removal of existing buildings
5. Careful removal of existing surfacing
6. Reconditioning/upgrading of existing surfacing
7. Installation of new structures
8. Installation of special surfacing
9. Installation of new services or upgrading of existing services
10. Removal of protective measures
11. Tree planting and general landscaping

More specifically, a preliminary programme for the arboricultural input is set out below:

Finalising tree management details after consent, but before work starts	
Action	Arboricultural input
Review of tree protection and any emerging design issues that may affect trees with the construction team	• Meeting/discussion with relevant members of the developer's team to explain the extent of the tree constraints • Review working space requirements to consider CEZ fencing and ground protection adjustments to improve site functionality • Review drainage proposals and identify potential conflicts with RPAs • Review any post-consent layout changes that may affect trees • Review all works within RPAs that may affect trees • Identify any potential conflicts and work towards resolutions • Preparation of working drawings, if necessary
Review consented tree protection proposals for discussion at pre-commencement meeting	If necessary: • prepare revised plans and specifications • liaise with LPA to discuss modifications
Review the / Preparation of a / construction method statement to detail how the site activities will account for the protection of trees	• If necessary, advise in its preparation / updating

Section 2: Arboricultural method statement

Briefing landscape architect on restrictions imposed on new landscape design by RPAs	- Advise landscape architect of the RPA locations, the restrictions to landscaping activity that applies and the details of agreed new tree planting - Review the final landscaping proposals to identify any conflicts between tree protection and landscaping
Pre-commencement site meeting with supervising arboriculturist, site manager and the LPA representative (if appropriate)	- Meeting on site - Agree detail of supervision requirements, i.e. frequency of visits and reporting - Review tree protection, if already installed - Agree any changes to CEZ barrier combinations of fencing and ground protection
Site operations before demolition/construction starts on site	
Action	Arboricultural input
Tree works carried out	Review the site requirements with the tree work contractor
Installation of tree protection for agreement by the LPA	- If appropriate, preparation of any revised plans and specifications for agreement by the LPA - Photographs showing relevant aspect of installed tree protective measures - Liaise with the contractor installing protection until satisfactorily completed
Installation of new special surfacing	Meeting with contractor for briefing before installation, with further supervision visits as necessary at the discretion of the arboricultural consultant
Demolition	Liaise with the demolition contractor about tree protection
Operations within precautionary areas that could affect trees during construction	
Action	Arboricultural input
Removal of existing structures and/or surfacing to be replaced with ground protection or new special surfacing	Meeting with contractor for briefing before work starts, with further supervision visits as necessary at the discretion of the arboricultural consultant
Installation of new structures	Meeting with contractor for briefing before work starts, with further supervision visits as necessary at the discretion of the arboricultural consultant
Removal of surfacing retained as ground protection to be replaced with soft landscaping	- Meeting with contractor for briefing before work starts, with further supervision visits as necessary at the discretion of the arboricultural consultant NOTE: This should only be authorised once there is no risk of RPA damage from the construction activity
Installation of new special surfacing inside the CEZ after barriers have been removed	Meeting with contractor for briefing before installation, with further supervision visits as necessary at the discretion of the arboricultural consultant
Installation of new custom designed structures inside the CEZ after barriers have been removed	Meeting with contractor for briefing before installation, with further supervision visits as necessary at the discretion of the arboricultural consultant
Installation of new services	Meeting with contractor for briefing before work starts, with further supervision visits as necessary at the discretion of the arboricultural consultant
Operations that could affect trees after construction is completed	
Action	Arboricultural input
Removal of barriers and ground protection	- Meeting with contractor for briefing before work starts, with further supervision visits as necessary at the discretion of the arboricultural consultant NOTE: This should only be authorised once there is no risk of RPA damage from the construction activity
New tree planting	Check tree size, species, quality, handling, site preparation and planting comply with the specification
Soft and hard landscaping	Meeting with contractor for briefing before work starts, with further supervision visits as necessary at the discretion of the arboricultural consultant
Tree planting maintenance	Liaise with landscape contractor to check maintenance complies with the specification

The precise order and timing of some of these operations may change due to site operating requirements, but all operations that can affect trees will remain under arboricultural supervision.

Section 2: Arboricultural method statement

2.3 GENERAL TREE MANAGEMENT AND PROTECTION

2.3.1 General site operation

The day-to-day running of the site will take full account of the tree protection measures set out in this document, a copy of which will be kept on site at all times. All site personnel will be briefed on the tree protection requirements as part of the site induction procedures.

2.3.2 Tree works

The proposed tree works are set out in the work recommendations column of the tree schedule in Appendix 2. The trees to be removed are highlighted with red text in the schedule. The location of each tree by number is shown on the plan and those to be removed are indicated with a red number and a red crown outline.

2.3.3 Protection of the CEZ by the use of fencing and ground protection

BS 5837 describes the CEZ as the RPA surrounding retained trees that is to be protected from any disturbance caused by construction activity. In practice, this can be done by any combination of fencing and ground protection, to be finalised and agreed at the pre-commencement meeting.

- **Protective fencing:** On the tree protection plan, the approximate boundary of the CEZ is shown by the heavy black dashed line, with the diagonal black hatching indicating the enclosed CEZ. Further detail on fencing options is included in Appendix 3 (paragraphs 3–6). The precise form of the fencing can vary, provided it is fit for purpose in that it prevents damaging activities within the CEZ that it encloses.
- **Ground protection:** Where it is not practical to protect the CEZ by the use of fencing alone, BS 5837 (6.2.3.1) allows for the fencing to be set back and the soil protected by ground protection. This allows fencing to be set back to improve access, with the ground protection preventing damage to the CEZ outside the protection of the fencing. A range of methods can be used including retaining existing hard surfacing or structures that already protect the soil, installing new materials or a combination of both. Further detail on ground protection options is included in Appendix 3 (paragraph 6). Whatever the choice of method, the end result must be that the underlying soil (rooting environment) remains undisturbed and retains the capacity to support existing and new roots.

Throughout this report, there is a presumption that all RPAs identified for protection on the plan outside the CEZ will be protected from soil degradation at all times during any demolition and construction. This applies to all the shaded precautionary areas shown on the plan at all times during the development while there is a risk of damage to the RPAs of retained trees. All work operations in RPAs will be strictly controlled in accordance with BS 5837, as explained in Appendix 3. All barriers, whether fencing or ground protection, must remain intact and fit for purpose for the duration of any

Section 2: Arboricultural method statement

development activity that could cause damage. The barriers are intended to prevent any unsupervised activities within the protected CEZ. All construction activities with the potential to disturb RPAs must be subject to arboricultural supervision. Additionally, once the barriers are removed, any landscaping activity must be carefully controlled in RPAs.

2.3.4 Control of activities within precautionary areas

Precautionary areas are shown on the tree protection plan as coloured shading outside the main protective barriers of the CEZ. They indicate where agreed activities can be carried out within RPAs, provided sufficient care is taken to ensure that any impact on retained trees is minimised. This specifically applies to excavation, but also covers all other development operations with the potential to adversely affect trees. All activities within precautionary areas must be carried out in accordance with the guidance principles set out in Appendix 3 and be supervised by an arboricultural consultant. In particular, this guidance applies to removing surfacing and structures, upgrading surfacing and services, and installing new structures and soft landscaping.

2.3.5 Control of activities near RPAs

Any risk to trees from activities outside RPAs, but close enough to have a knock-on impact, will be assessed during the day-to-day running of the site and appropriate precautions put in place to reduce that risk. More specifically, all cement mixing and washing points for equipment and vehicles will be outside RPAs. Where the contours of the site create a risk of polluted water or toxic liquids running into RPAs, a precautionary measure of using heavy-duty plastic sheeting and sandbags with the ability to contain accidental spillages will be put in place to prevent contamination.

2.3.6 New tree planting

Although new trees can be planted at any stage in the development process, it usually happens towards the end, along with the general landscaping. On this site, eighty five new trees, will be planted and maintained according to the guidance in Appendix 3 (paragraphs 25 and 26) at the locations illustrated on the plan. It is proposed that the detail of the species and sizes are agreed with the LPA through a condition to ensure that the final scheme optimises the potential of the space available. Any trees that die or progressively decline within five years will be replaced and maintained until successfully established.

Additionally, where these new trees are located next new hard surfacing a minimum of nine cubic metres (9m² x 1m depth) per tree of below ground preparation using structured tree soil and a root guidance product will be installed according to the guidance in Appendix 3 (paragraphs 27 and 28).

Section 2: Arboricultural method statement

2.4 SPECIFIC TREE PROTECTION REQUIREMENTS

The specific tree protection operations, in roughly the order that they will be carried out, are explained in detail in the following subsections. Where appropriate, more detailed guidance is referenced in Appendix 3 to supplement the following explanations.

2.4.1 Installation of CEZ barriers (fencing and/or ground protection)

The CEZ boundary is shown on the tree protection plan as the heavy black dashed line. Its location is approximate because its precise position will need to be finalised on site, depending on the local site conditions. If necessary, BS 5837 allows the fencing location to be moved provided the exposed CEZ is protected by ground protection, but this would need to be formally agreed by all parties at the pre-commencement meeting. Once the tree works have been carried out, the appropriate fencing and ground protection will be installed before any construction work starts, following the guidance in Appendix 3 (paragraphs 3–6).

2.4.2 Removal of buildings within RPAs

Several buildings and associated structures are to be removed throughout the site as part of the redevelopment process. Where possible and appropriate to the timings of onsite operations the foundations of these structures will remain in place to provide a suitable level of ground protection during the main redevelopment process. Once these main phases are complete and the risk of damage to tree roots has decreased then these retained elements will be replaced with either new permeable surfacing or soft landscaping. Specifically these works are occurring adjacent to trees 28, 33, 53 and 54. All demolition will be undertaken in a manner to avoid disturbance to any roots that may have grown beneath them. This work will be done in accordance with the guidance in Appendix 3 (paragraphs 7–10).

2.4.3 Removal/reconditioning of existing surfacing and replacement with new surfacing

Trees 7, 12, 24, 27, 28, and parts of groups 13 and 52 may be affected by the realignment works to the existing access routes. I have carefully reviewed the levels in these areas and it would be feasible to install custom designed no-dig specification surfacing without causing any significant disturbance to the RPAs. From our previous experience at installing such surfacing (www.barrelltreecare.co.uk/case-studies/SurfacingNearTrees.pdf), I am confident that this can be implemented without significant harm to the trees, with the detail to be agreed as part of a planning condition. This surfacing solution is within the advice set out in BS 5837 (8.6) and would be appropriate in this situation. Any impact should be minimised by following the guidance set out in Appendix 3 (paragraphs 7–17) where illustrative specifications for special surfacing can also be found. It is envisioned that the existing surfacing will be utilised for the main phases of the redevelopment with additional ground protection added to areas exposed to heavy usage by large vehicles. This will ensure that the

Section 2: Arboricultural method statement

potential risks of compaction and direct root damage are minimised. Once these main phases of redevelopment are complete the existing surfacing within these areas will either be reconditioned with a new permeable wearing course or completely removed (including all sub base material) and replaced with a new permeable construction.

2.4.4 Installation of new special surfacing

The proposed new surfacing within areas of existing soft landscaping adjacent to trees 59, 60, 69 and part of groups 13 and 52 will be constructed using a low-impact, no-dig construction using CellWeb or a similar product. The area to be covered will need to be levelled before the CellWeb is installed as described in Appendix 3 (paragraphs 7–17). I have carefully reviewed the levels in these areas and it would be feasible to install custom designed no-dig specification surfacing without causing any significant disturbance to the RPAs. From our previous experience at installing such surfacing (www.barrelltreecare.co.uk/case-studies/SurfacingNearTrees.pdf), I am confident that this can be implemented without significant harm to the trees, with the detail to be agreed as part of a planning condition. This surfacing solution is within the advice set out in BS 5837 (8.6) and would be appropriate in this situation. Any impact should be minimised by following the guidance and illustrative specifications included in Appendix 3 (paragraphs 7–17). As these areas are located outside of the CEZ all surfacing measures must be installed as part of the initial tree protection works across the site in order to prevent damage to the RPA from the construction activity. In the event that these surfacing measures cannot be installed before works start then they should be enclosed within the CEZ and attended to at a later date.

2.4.5 Installation of new pathway

Sections of the proposed new pathway that crosses the existing grotto and open space known as The Green will lie within the RPAs of trees 8, 27, 28 and groups 3 and 13. The formation of this pathway within these areas will conform to the specification set out above in section 2.4.4 to ensure that no adverse impact occurs. As these areas are located within the CEZ it is intended that the construction of the pathway will be undertaken following the completion of the main redevelopment works. All works will be subject to supervision.

2.4.6 Replacement of existing structures and areas of hard surfacing with new soft landscaping

Trees 28, 33, 53, 54 and 56 have built form elements and areas of existing hard standing within their RPAs, the removal of which may result in adverse impact unless undertaken with care. Where possible these existing elements will remain insitu (with any building being reduced to foundation level) throughout the main phases of the redevelopment process. This will ensure that the risk to tree roots that may exist below these foundations and surfacing sub bases is minimised. Once the main onsite construction works are complete then all retained surfacing and foundation within these areas will be

Section 2: Arboricultural method statement

broken up by hand and replaced with new soft landscaping. Any impact should be minimised by following the guidance set out in Appendix 3.

2.4.7 Installation of new services or upgrading of existing services

It is often difficult to clearly establish the detail of services until the construction is in progress. Where possible, it is proposed to use the existing services into the site and keep all new services outside RPAs. However, where existing services within RPAs require upgrading or new services have to be installed in RPAs, great care must be taken to minimise any disturbance. Trenchless installation should be the preferred option but if that is not feasible, any excavation must be carried out by hand according to the guidelines in Appendix 3 (paragraph 22). If unexpected services do need to be installed within RPAs, written approval must be obtained from the LPA before any works are carried out.

2.4.8 Removal of protective measures

All protective barriers must remain in place until the construction activity is finished and there is no realistic risk of damage to the protected soil surfaces.

2.4.9 Landscaping and reinstatement

The final tidying up and reinstatement can only be carried out when all the protective barriers have been removed, which means great care is needed by all the contractors to observe the tree protection requirements. No machines can be used within RPAs, which specifically includes rotovators, and all new planting and soil level variations must be agreed and supervised by the arboriculturist. All these works will be carried out strictly in accordance with the guidance in Appendix 3 (paragraph 25).

Section 3

Appendices

Appendix 1: Administrative information, site visit and data collection

Administrative information

1. Instruction

We are instructed by Linden Homes Southern to inspect the significant trees that could be affected by the development proposal at St Michaels Convent, Waterloooville, and to prepare the following information to accompany the planning submission:

- a schedule of the relevant trees to include basic data and a condition assessment
- an appraisal of the impact of the proposal on trees and any resulting impact that has on local amenity
- an arboricultural method statement dealing with the protection and management of the trees to be retained

2. Documents provided

The tree protection plan is derived from the following provided information:

- Land survey, drawing number Wvland1.Dwg / HLS0161, received by email on 2 December 2011
- Layout, drawing reference 'PP1144 SITE PLAN FOR MODEL EXPORT.dwg', received by email on 9 July 2012

3. Limitations of this report

The following limitations apply to this report:

- **Statutory protection:** The existence of tree preservation order or conservation area protection does not automatically mean trees are worthy of being a material constraint in a planning context. Trees can be formally protected, but be in poor structural condition or in declining health, which means that they are unsuitable for retention or influencing the future use of the site. Furthermore, a planning consent automatically takes precedent over these forms of protection, which makes them of secondary importance. For these reasons, we do not check statutory protection as a matter of course in the process of preparing this report. However, if any tree works are proposed before a planning consent is given, then the existence of any statutory protection must be checked with the LPA.
- **Ecology and archaeology:** Although trees can be valuable ecological habitat and can grow in archeologically sensitive locations, we have no specialist expertise in these disciplines and this report does not consider those aspects.

4. Technical references

This arboricultural method statement is based on the following primary technical references:

- British Standards Institution (2012) BS 5837: *Trees in relation to design, demolition and construction – Recommendations*
- National Joint Utilities Group (2007) Volume 4, Issue 2: *Guidelines for the planning, installation and maintenance of utility apparatus in proximity to trees*

Appendix 1: Administrative information, site visit and data collection

5. Qualifications and experience

This report is based on my site observations and the provided information, interpreted in the context of my experience. I have experience and qualifications in arboriculture that can be reviewed at www.barrelltreecare.co.uk/about-us.php.

Site visit and data collection

6. Site visit

I visited to collect the tree data on 8 December 2011. All my observations were from ground level without detailed investigations and I estimated all dimensions unless otherwise indicated. I did not have access to trees outside the boundaries or on other private properties and have confined observations of them to what was visible from within the grounds of the convent. The weather at the time of inspection was dull, damp and drizzling, with average to poor visibility.

7. Brief site description

The site known as St Michaels Convent is located a short distance north east of Waterlooville town centre. It is primarily accessed by a road known as Villa Gardens on the southern side of London Road (A3), although an additional access is also maintained from Hulbert Road (B2150) to the south. The site is currently administered by the English Province of Our Lady of Charity and consists of a variety of buildings of mixed form and elevation, the most prominent of which are the grade II listed St Michael's Convent and Church of the Sacred Heart, Waterlooville. A large area of open space known as 'The Green' is situated to southern side of the access driveway that links to Villa Gardens. This driveway then divides into two service roads which provide access around the main complex of buildings which are centrally located within the site. To the east of this complex of buildings there is a large open area of landscaping that is divided into areas of formal garden, open grassland and orchard. The levels within this eastern area of the site decrease steadily to the Hermitage stream area which is defined by a number of large and mature alder trees. A variety of predominated deciduous trees are scattered throughout the site and several of which form significant skyline features within the broader landscape.

8. Collection of basic data and compliance with BS 5837

Each tree was inspected and the numbering scheme is indicated on the tree protection plan. Obvious hedges and groups were identified where appropriate. For each individual tree, group and hedge, information was collected on species, height, diameter, maturity and potential for contribution to amenity in a development context. As advocated in BS 5837, each tree was then allocated to one of four categories (A, B, C or U), which reflected its suitability as a material constraint on development. Each category A, B and C tree was automatically assigned sub-category 1 unless otherwise stated. When collecting this information, specific consideration was given to any low branches that may influence future use, age class, physiological condition, structural condition and remaining contribution. Where appropriate, crown spreads were also noted where they differed from those shown on the provided land survey. This data with explanatory notes is set out in the tree schedule included as Appendix 2 and the supporting plan information. Each tree inspection was of a preliminary nature and did not involve any climbing or detailed investigation beyond what was visible from accessible points at ground level. BS 5837 (4.4.2) sets out recommendations for the collection of data and this report is fully compliant with that advice in the context of the BS 5837 Foreword, which states: *"Any user claiming compliance*

Appendix 1: Administrative information, site visit and data collection

with this British Standard is expected to be able to justify any course of action that deviates from its recommendations." In that context, we will justify any deviation in this report from the strict BS 5837 recommendations on request.

9. Calculation of RPAs

Following the recommendations in Table D1 of BS 5837, the diameter of each tree was rounded up to the next 2.5cm increment, with the radius of a nominal circle and the resultant RPA taken directly from that table. These details are listed out for each tree at the end of Appendix 2.

10. Specific observations of individual trees

During the data collection, defects in the following tree were noted that are relevant to the assessments in this report:

- **Tree 41:** This category B tree is not an outstanding individual due to its advanced maturity, twin stemmed nature and the presence of a wood decaying fungal pathogen within its lower stem area. This pathogenic presence is likely to significantly decrease the time over which this tree can be sustainably retained. As such it is concluded that the current constraint posed by the tree should not influence the planned redevelopment, however, suitable mitigation via the landscape plan should be put in place to compensate for the loss of what is currently a large and prominent tree. At the time of my visit photos were taken of this tree and a selection follow:

Appendix 1: Administrative information, site visit and data collection



Photo 1: Distance view of tree 41 highlighting its twin stemmed nature with a further major stem division at approximately 6m

Appendix 1: Administrative information, site visit and data collection



Photo 2: Close up detail of bracket fungus (*Ganoderma* sp) observed at the base of tree 41 (southern side).

Appendix 1: Administrative information, site visit and data collection



Photo 3: View of tree 41 from northern aspect, highlighting twin stemmed nature

Appendix 1: Administrative information, site visit and data collection

11. LPA consultation and feedback

During the process of the current application on the site, there have been various discussions and a recent site visit on 14 March 2012 with Mr J Gargett, the Havant Borough council tree officer. During the site visit a preliminary layout (PP144 SK12) was discussed and the following detail agreed upon:

1. The proposed tree losses arising from the layout - with the exception of trees 41, 70 and 72 – do not pose a significant risk of adverse impact in respect to local amenity or landscape character provided that significant new tree planting is included as part of the scheme in mitigation. NB on subsequent consideration Mr Gargett determined that although tree 41 has a number of years of sustainable existence, the presence of the fungus at the base of this tree will mean that the tree will have much reduced life expectancy and should not impose significant constraint on a redevelopment proposal.
2. The trees within the area of the site defined as the orchard were not of a sustainable condition and had limited long term sustainability. Nonetheless, mitigation for their removal should form part of the proposal.

12. Plan updates

During the site visit, several trees (34, 83, 97, 107, 108, 118, 119, 120; groups 94, 117 and parts of groups 37, 88 and 95), were noted not to be accurately shown on the land survey. Their approximate locations have been illustrated on the tree protection plan, but these positions have not been accurately surveyed. These additions are not considered to have affected the report conclusions, but if their locations are deemed important, then they should be accurately surveyed and formally added to the topographic survey.

13. The use of the tree information in layout design

Following the inspection of the trees, the information listed in Appendix 2 was used to provide constraints guidance to the architect based on the locations of all the category A and B trees. All the category C and U trees were discounted because they were not considered worthy of being a material constraint. This guidance identified the estimated developable footprint of the site and was considered by the architect to arrive at the submitted design. For conciseness, and because it is not a BS recommendation, this detailed constraints advice has not been included in this report, although there is a summary at the end of Appendix 2.

Appendix 2: Tree schedule and notes on interpreting data

NOTE: Colour annotation is A & B trees with green background; C & U trees with blue background; trees to be removed in red text.

Tree No	Species	Height (m)	Diameter (cm) @ 1.5m	Maturity	Low Branches	Category	Notes	Tree Works	RPA radius (m)	RPA area (m2)
All retained trees & hedges							Deadwood and lift to 3-4m over site as necessary			
T1	Sycamore	9	40	Maturing	-	C	Multi stemmed, ivy clad, poor structural form	Fell	4.8	72
T2	Norway maple	9	32*	Maturing	-	B	Poor structural form, marginal B tree	-	3.8	46
G3	Norway maple	9	32	Maturing	-	B	-	-	3.8	46
T4	Sycamore	7	32	Young	-	C	Twin stem at base	Fell	3.8	46
T5	Ash	10	22*	Young	-	C	Ivy clad, suppressed by G3	Fell	2.6	22
T6	Laburnum	4	30	Mature	-	C	Decay at base, poor condition	-	3.6	41
T7	Purple plum	8	40	Mature	-	C	Twin stem at 1.5m above ground level	-	4.8	72
T8	Whitebeam	8	50*	Mature	-	B	Historic tag number 3230, limited deadwood	-	6.0	113
G9	Cherry	5	15	Young	-	C	Small tree, poor structural form	Fell selected individuals	1.8	10
T10	Oak	12	47*	Young/maturing	-	B	Marginal B tree, secondary branch at 1.5m above ground level, suppressed by adjacent tree	Fell	5.6	100
T11	Oak	12	52*	Maturing	-	C	Twin stemmed at 0.5m above ground level, ivy clad, poor structural form	Fell	6.2	122
T12	Ash	11	42*	Maturing	-	B	Secondary branch at 1.5m above ground level, marginal category B tree	-	5.0	80
G13	Hawthorn	7	37*	Mature	-	B	Historic tag number 3325, marginal due to size,	-	4.4	62

Appendix 2: Tree schedule and notes on interpreting data

Tree No	Species	Height (m)	Diameter (cm) @ 1.5m	Maturity	Low Branches	Category	Notes	Tree Works	RPA radius (m)	RPA area (m2)
							deadwood within canopy, ivy clad			
G14	Willow	11	50	Young/maturing	-	C	Multi stemmed at ground level, poor structural form	-	6.0	113
H15	Hornbeam	5	15	Young	-	C	Sparse unmanaged hedge	-	1.8	10
T16	Fruit	10	25*	Maturing	-	C	Suppressed by adjacent trees	-	3.0	28
T17	Cotoneaster	4	25	Maturing	-	C	Multi stemmed at base	-	3.0	28
T18	Crab	8	45	Mature	-	C	Multi stemmed at ground level, poor structural form	-	5.4	92
G19	Weeping silver birch	4	20	Maturing	-	C	Ivy clad, small, poor structure	-	2.4	18
T20	Rowan	5	15	Young	-	C	Poor structural form, twin stemmed at 0.5m above ground level	-	1.8	10
T21	Crab	7	50	Mature	-	C	Ivy clad, multi stemmed from base, poor form	-	6.0	113
G22	Poplar	17	47*	Maturing	-	C	History of reduction pruning, needs to be retained at current dimensions	-	5.6	100
H23	Beech	1.8	10	Maturing	-	C	Formally maintained hedge	-	1.2	5
T24	Oak	14	82*	Mature	-	A	Historic tag number 3276, marginal category A tree suppressing T10	-	9.8	304
T25	Crab	7	50	Mature	-	C	Multi stemmed at ground level, poor structural form	Fell	6.0	113
T26	Monterey cypress	11	70*	Mature	-	C	Extensive decay throughout tree, screens T27	Fell	8.4	222
T27	Monterey cypress	17	95*	Mature	-	B	Evidence of historic storm damage, historic suppression from a tree since removed	-	11.4	408
T28	Monterey cypress	17	122*	Mature	-	B	Past storm damage in	-	14.6	673

Appendix 2: Tree schedule and notes on interpreting data

Tree No	Species	Height (m)	Diameter (cm) @ 1.5m	Maturity	Low Branches	Category	Notes	Tree Works	RPA radius (m)	RPA area (m2)
							canopy			
T29	Irish yew	8	50	Maturing	-	B	-	-	6.0	113
T30	Ash	14	45*	Maturing	-	B	Signs of canker	Fell	5.4	92
T31	Ash	14	45	Maturing	-	C	Located on adjacent land, ivy clad, poor form	-	5.4	92
T32	Sycamore	11	30	Maturing	-	C	Twin stemmed, poor form, ivy clad	-	3.6	41
T33	Oak	13	90*	Over-mature	-	C	Ivy clad, extensive dieback in upper canopy	-	10.8	366
T34	Cypress	5	35	Maturing	-	C	Multi stemmed	Fell	4.2	55
T35	Sorbus	7	30	Maturing	-	C	Multi stemmed at base, poor form	Fell	3.6	41
T36	Maple	6	10	0	-	U	Dead tree	Fell	1.2	5
G37	Cypress	12	40	Maturing	-	C	Ivy clad, poor form within group, evidence of historic reduction at 3m above ground level	Fell	4.8	72
T38	Cypress	5	30	Maturing	-	C	Multi stemmed, ornamental planting	Fell	3.6	41
T39	Yew	4	20	Young	-	C	Small tree, poor structural form	Fell	2.4	18
T40	Purple plum	7	25	Maturing	-	C	Poor form, large secondary branch from base	Fell	3.0	28
T41	Ash	27	137*	Over-mature	-	B	Historic tag number 3402, twin stemmed at 2.5m above ground level, evidence of storm damage throughout canopy, large deadwood, large Ganoderma sp fungal bracket noted at base.	Fell	15.0	707
G42	Apple, laburnum, horse chestnut	8	35	Maturing/mature	-	C	Small trees	Fell	4.2	55
T43	Norway maple	14	52*	Maturing	-	B	Suppressed by T44, marginal	Fell	6.2	122

Appendix 2: Tree schedule and notes on interpreting data

Tree No	Species	Height (m)	Diameter (cm) @ 1.5m	Maturity	Low Branches	Category	Notes	Tree Works	RPA radius (m)	RPA area (m2)
							B tree, poor canopy structure			
T44	Monterey cypress	13	130	Over-mature	-	B	Two main stems, historic storm damage	Fell	15.0	707
T45	Monterey cypress	9	55*	Over-mature	-	U	-	Fell	6.6	137
T46	Willow	17	52*	Mature/over mature	-	C	Four main stems, ivy clad, very poor structural form	Fell	6.2	122
T47	Ash	12	35*	Maturing	-	U	Asymmetrical canopy, significant stem wounding and decay	Fell	4.2	55
T48	Willow	9	60	Over-mature	-	C	Regeneration from old collapsed stump	Fell	7.2	163
T49	Cherry	8	30	Maturing	-	C	Multi stemmed from ground	Fell	3.6	41
T50	Fruit	6	20*	Mature	-	C	-	Fell	2.4	18
T51	Crab	4	10	Mature	-	C	Deadwood in upper canopy	-	1.2	5
G52	Lime	17	70*	Mature	-	B	-	-	8.4	222
T53	Oak	15	100*	Mature	-	B	Located on boundary, historic crown reduction but since regrown, ivy clad	-	12.0	452
T54	Oak	16	100	Mature	-	A	Ivy clad, evidence of historic pruning	-	12.0	452
T55	Rowan	6	12	Maturing	-	C	Ivy clad	Fell	1.4	7
T56	Oak	15	110*	Mature	-	B	Historic pruning, past decay at pruning points	-	13.2	547
T57	Ash	9	35	Maturing	-	C	Very poor form, ivy clad throughout canopy	-	4.2	55
G58	Cypress	9	20	Maturing	-	C	-	Fell	2.4	18
T59	Oak	18	75*	Mature	-	A	-	-	9.0	254
T60	Oak	12	45	Maturing	-	B	Twin stemmed at 1m above ground level, located on adjacent land	-	5.4	92
G61	Laurel, maple, cherry	7	30	Mature/maturing	-	C	-	Fell	3.6	41

Appendix 2: Tree schedule and notes on interpreting data

Tree No	Species	Height (m)	Diameter (cm) @ 1.5m	Maturity	Low Branches	Category	Notes	Tree Works	RPA radius (m)	RPA area (m2)
T62	Cherry	9	33*	Mature	-	C	Past pruning, areas of canker	Fell	4.0	49
G63	Cypress	11	28*	Young/maturing	-	C	Closely planted, causing group suppression	Fell	3.4	35
T64	Cherry	4	25*	Mature	-	C	Canker, strimmer damage, bracket fungus at base	Fell	3.0	28
T65	Red chestnut	9	38*	Maturing	-	B	Good potential, causing disturbance to driveway	Fell	4.6	65
T66	Red chestnut	5	24*	Young	-	B	Marginal category B tree due to small size	Fell	2.9	26
T67	Plum	8	40	Mature	-	C	Multi stemmed at ground level	Fell	4.8	72
T68	Cypress	5	25	Maturing	-	C	Twin stemmed, poor form	Fell	3.0	28
T69	Oak	18	110*	Mature	-	A	-	-	13.2	547
T70	Silver birch	15	45*	Mature	-	B	-	Fell	5.4	92
T71	Cherry	9	25*	Mature	-	C	Suppressed by T70	Fell	3.0	28
T72	Willow	12	65*	Mature	-	A	Evidence of past storm damage, minor deadwood	Fell	7.8	191
G73	Oak	18	75*	Mature	-	B	Located on boundary, evidence of reduction pruning	-	9.0	254
T74	Ash	18	85	Mature	-	B	Located on boundary, twin stemmed, marginal category B tree due to poor form	-	10.2	327
T75	Ash	10	27	Maturing	-	C	-	-	3.2	33
T76	Poplar	19	50	Maturing	-	U	Significant lean, poor structural form	Fell	6.0	113
T77	Poplar	22	50*	Maturing	-	B	Twin stemmed at 7m above ground level, marginal category B tree	Fell	6.0	113
T78	Poplar	10	25	Maturing	-	U	Historic failure at 3m above ground level, some regrowth from failure point	Fell	3.0	28
T79	Poplar	13	35	Maturing	-	C	Suppressed by adjacent tree, poor structure, recent failure	Fell	4.2	55

Appendix 2: Tree schedule and notes on interpreting data

Tree No	Species	Height (m)	Diameter (cm) @ 1.5m	Maturity	Low Branches	Category	Notes	Tree Works	RPA radius (m)	RPA area (m2)
							in upper canopy, marginal category C tree			
T80	Poplar	20	50	Maturing	-	C	Poor structural form, large wound on main stem at 6m above ground level	Fell	6.0	113
T81	Poplar	22	50*	Maturing	-	C	Significant lean, poor structural form	Fell	6.0	113
T82	Poplar	13	40	Maturing	-	C	Suppressed by T81, very poor form, asymmetric canopy	Fell	4.8	72
T83	Gledista	3	10	Young	-	C	Damage in upper canopy	Fell	1.2	5
T84	Fruit	3	20	Mature	-	C	Historic pruning for fruit production now lapsed	Fell	2.4	18
T85	Cherry	2	30	Mature	-	U	Significant reduction pruning	Fell	3.6	41
T86	Ash	9	37*	Maturing	-	C	Self sown, poor structural form, multi stemmed at 2m above ground level	Fell	4.4	62
T87	Apple	6	40	Mature	-	C	Completely ivy clad	Fell	4.8	72
G88	Fruit	3	20	Mature/over mature	-	C	-	Fell	2.4	18
H89	Privet	2	10	Mature	-	C	Formally managed hedge, ivy throughout	Fell	1.2	5
T90	Horse chestnut	11	52*	Maturing	-	B	Old wound at 1.8m, slight canopy suppression by adjacent tree T19, marginal category B tree	Fell	6.2	122
T91	Ash	17	77*	Mature	-	C	Historic tag number 3400, historic ivy recently severed and dying back, major wound failure at previous point of codominance at 1.5m above ground level	Fell	9.2	268
T92	Horse chestnut	11	60*	Maturing	-	B	Suppressed by T19, twin stemmed at 1.8m above	Fell	7.2	163

Appendix 2: Tree schedule and notes on interpreting data

Tree No	Species	Height (m)	Diameter (cm) @ 1.5m	Maturity	Low Branches	Category	Notes	Tree Works	RPA radius (m)	RPA area (m2)
							ground level, marginal category B tree			
G93	Apple	4	25	Mature	-	C	-	Fell selected individuals	3.0	28
G94	Ash	7	20	Young	-	C	Self sown trees	Fell	2.4	18
G95	Fruit	6	35	Mature	-	C	-	Fell selected individuals	4.2	55
G96	Fruit	2	15	Maturing/mature	-	C	-	Fell selected individuals	1.8	10
T97	Willow	10	20	Young	-	C	Regenerated stump	Fell	2.4	18
T98	Oak	14	80	Over-mature	-	U	Ivy clad	Fell	9.6	290
T99	Oak	18	120	Mature	-	A	Ivy throughout	-	14.4	651
T100	Lime	8	20*	Maturing	-	C	Suppressed by T99	-	2.4	18
G101	Sycamore, ash	14	25	Maturing	-	C	Overgrown, ivy clad	-	3.0	28
T102	Ash	13	25	Young	-	C	Self sown	-	3.0	28
T103	Yew	14	50	Maturing	-	C	Twin stemmed from base, damage in upper canopy, marginal category B tree	-	6.0	113
T104	Oak	16	70	Mature	-	U	Major structural failure, wildlife benefit	Fell	8.4	222
T105	Beech	20	62*	Mature	-	A	Historic tree tag 3331, large secondary branch at 1.3m above ground level, marginal category A tree	-	7.4	174
T106	Alder	18	90	Mature	-	C	Multi stemmed at 1.4m above ground level, ivy clad, located at side of stream	-	10.8	366
T107	Alder	11	27*	Maturing	-	C	Root damage, basal decay	-	3.2	33
T108	Ash	11	27	Maturing	-	C	Twin stem 0.5m above ground level, poor form	-	3.2	33
T109	Alder	17	62*	Mature	-	B	-	-	7.4	174
T110	Alder	18	120	Mature	-	B	Historic tag number 3382, deadwood in upper canopy, multi stemmed from base, 2	-	14.4	651

Appendix 2: Tree schedule and notes on interpreting data

Tree No	Species	Height (m)	Diameter (cm) @ 1.5m	Maturity	Low Branches	Category	Notes	Tree Works	RPA radius (m)	RPA area (m2)
							main stems, fungal bracket on east stem			
G111	Alder	20	60	Mature	-	B	Marginal category B tree, cavities, old stem wound, could be coppiced	-	7.2	163
T112	Ash	19	85	Mature	-	B	Twin stemmed at base, marginal category B tree	-	10.2	327
T113	Alder	17	80	Mature	-	B	Twin stemmed at base, ivy clad	-	9.6	290
G114	Alder	17	65	Mature	-	B	Multi stemmed from ground, areas of past wounding, ivy clad stem, marginal category B tree	-	7.8	191
G115	Alder, sycamore	16	40	Maturing	-	C	Poor structural form, ivy clad	-	4.8	72
T116	Ash	14	45	Maturing/mature	-	C	Historic tag number 3389, heavy historic lean to south east, located on adjacent land	-	5.4	92
G117	Ash	20	40	Young/maturing	-	C	Poor structural form, ivy throughout, located on adjacent land, canopy suppression due to proximity of adjacent trees	-	4.8	72
G118	Ash	20	75	Mature	-	C	Ivy to 8m, honey fungus (Armillaria sp) throughout main stems, past branch failure noted at 8m	-	9.0	254
T119	Oak	18	95	Mature/over mature	-	B	Twin stemmed at base, crown suppression, ivy obscured close inspection	-	11.4	408
T120	Chestnut	16	55	Mature	-	B	Located on adjacent land	-	6.6	137
T121	Magnolia	7	25	Mature	-	C	Twin stem at base, ornamental planting	-	3.0	28

Appendix 2: Tree schedule and notes on interpreting data

Appendix 2: Tree schedule and notes on interpreting data

Explanatory notes for schedule

- **Abbreviations:**

G	: Group
H	: Hedge
RPA	: Root protection area

- **Botanical tree names:**

Alder	: <i>Alnus cordata</i>
Apple	: <i>Malus sp</i>
Ash	: <i>Fraxinus excelsior</i>
Beech	: <i>Fagus sylvatica</i>
Cherry	: <i>Prunus sp</i>
Cotoneaster	: <i>Cotoneaster sp</i>
Crab	: <i>Malus sp</i>
Cypress	: <i>Cupressus sp</i>
Gledista	: <i>Gledista sp</i>
Fruit	: <i>Malus sp, Prunus sp or Pyrus sp</i>
Hawthorn	: <i>Crataegus monogyna</i>
Hornbeam	: <i>Carpinus betulus</i>
Horse chestnut	: <i>Aesculus hippocastanum</i>
Irish yew	: <i>Taxus baccata</i> 'Fastigiata'
Laburnum	: <i>Laburnum sp</i>
Laurel	: <i>Prunus laurocerasus</i>
Lime	: <i>Tilia sp</i>
Magnolia	: <i>Magnolia sp</i>
Maple	: <i>Acer sp</i>
Monterey cypress	: <i>Cupressus macrocarpa</i>
Norway maple	: <i>Acer platanoides</i>
Oak	: <i>Quercus robur</i>
Plum	: <i>Prunus sp</i>
Poplar	: <i>Populus sp</i>
Privet	: <i>Ligustrum vulgare</i>
Purple plum	: <i>Prunus cerasifera</i> 'Nigra'/'Pissardii'
Red horse chestnut	: <i>Aesculus carnea</i>
Rowan	: <i>Sorbus aucuparia</i>
Silver birch	: <i>Betula sp</i>
Sorbus	: <i>Sorbus sp</i>
Sycamore	: <i>Acer pseudoplatanus</i>
Weeping silver birch	: <i>Betula pendula</i> 'Tristis'
Whitebeam	: <i>Sorbus aria</i>
Willow	: <i>Salix sp</i>

- **BS 5837 (2005) compliance:** All data has been collected based on the recommendations set out in subsection 4.2 of BS 5837.
- **Site limitations:** Where there is restricted access to the base of a tree, its attributes are assessed from the nearest point of access. Climbing inspections are not carried out during a walkover tree survey and, if heavy ivy is present, tree condition is assessed from what can be seen from the ground. A separate note is recorded if further investigation may be required to clarify its status.
- **Crown spreads:** Crown spread dimensions are not listed in the tree schedule because they are illustrated on the land survey base to all the plans in this document. Where crown spreads of

Appendix 2: Tree schedule and notes on interpreting data

significant trees on site are found to deviate from those shown on the provided land survey, we have noted it in the text of the report and annotated it on our plans.

- **Dimensions:** All dimensions are estimated unless annotated with a '*'.
- **Species:** Species identification is based on visual observations. Where there is some doubt over tree identity, sp is noted after the genus name in the botanical names section above to indicate that the species cannot be reliably identified at the time of the survey. Where there is more than one species in a group, only the most frequent are noted and not all the species present may be listed.
- **Height:** Height is estimated to provide a broad indication of the size of the tree.
- **Trunk diameter:** Trunk diameter is estimated or measured and recorded in 2.5cm increments as advised in BS 5837 Table D1. It is measured with a diameter tape unless access is restricted, direct measurement is not possible because of ivy on the trunk or the tree is assessed as poor quality. The point of measurement and the adjustments for stem variations are as advised in Figure C1 of BS 5837.
- **Maturity:** In planning context, maturity provides a simplistic indication of a tree's ability to cope with change and its potential for further growth. For the purposes of this report, young indicates a potential to significantly increase in size and a high ability to cope with change, maturing indicates some potential to increase in size and a medium ability to cope with change, and mature indicates little potential to increase in size and limited ability to cope with change.
- **Low branches:** Any low branches that would not be feasible for removal during normal management and should be considered as a design constraint are noted here and explained in the notes.
- **Category:** Our assessment automatically considered tree physiological/structural condition (BS 5837 4.4.2.5h), and so these are not listed separately in the schedule. Additionally, the category accounts for the remaining contribution (BS 5837 4.4.2.5i) as greater than 40 years for A trees, greater than 20 years for B trees, at least 10 years for C trees and less than 10 years for U trees, so this is also not listed separately in the schedule. Category A, B and C trees are automatically as sub-category 1 unless otherwise stated.
- **Notes:** Only relevant features relating to physiological or structural condition and low branches that may help clarify the categorisation are recorded. If there are no notes, then the presumption should be that no relevant features were observed.
- **Tree works:** The inspection of all trees was of a preliminary nature and only defects visible from the ground have been identified. Each individual tree may not have been inspected closely because of access difficulties and only defects visible from the inspection point have been noted. In addition to tree removals for development and management reasons, further works are listed to establish acceptable levels of risk. All trees should be deadwooded and lifted to 3–4m above the site and hedges pruned back to reform the original hedge form, where appropriate. Only works in excess of this have been listed for individual trees. The following points should also be noted before carrying out any works:
 1. **Reporting during work operations:** In the context of the preliminary nature of the tree inspection, any defects that may affect tree safety discovered by the contractor when carrying out the work recommendations should be reported to the supervising officer. Modification to the schedule of works may be required because of these reports. The contractor should be specifically instructed on this point.
 2. **Implementation of works:** All tree works should be carried out to BS 3998 *Recommendations for Tree Work* as modified by more recent research. It is advisable to select a contractor from the local authority list and preferably one approved by the Arboricultural Association. Their Register of Contractors is available free from The Malthouse, Stroud Green, Standish, Stonehouse, Gloucestershire GL10 3DL; phone 01242 522152; website www.trees.org.uk.

Appendix 2: Tree schedule and notes on interpreting data

3. **Statutory wildlife obligations:** The Wildlife and Countryside Act 1981 as amended by the Countryside and Rights of Way Act 2000 provides statutory protection to birds, bats and other species that inhabit trees. All tree work operations are covered by these provisions and advice from an ecologist must be obtained before undertaking any works that might constitute an offence.
4. **Stumps:** Stumps to be removed within the RPAs of retained trees should be ground out with a stump grinder to minimise any disturbance unless otherwise authorised by the supervising officer.

Appendix 3: Protecting retained trees


Introduction

1. Purpose and use of this guidance

This general guidance is for construction site management to help protect trees that have been agreed for retention. It must be read in conjunction with the site-specific proposals shown on the tree protection plan and explained in the body text of this report. It supplements and expands upon the principles set out in the British Standards Institution (2012) BS 5837: *Trees in relation to design, demolition and construction – Recommendations* (www.bsigroup.com) and the National Joint Utilities Group (NJUG) (2007) Volume 4, Issue 2: *Guidelines for the planning, installation and maintenance of utility apparatus in proximity to trees* (www.njug.org.uk). More specifically, it describes useful practical precautions that can be taken when working close to retained trees and provides sources of further information. Important terms include:

- **Root protection areas (RPAs):** RPAs are the areas surrounding retained trees where disturbance must be minimised.
- **Construction exclusion zone (CEZ):** This is the RPA where no construction activity should occur and damage is prevented by either installing fencing to restrict access or installing ground protection that allows limited access above the ground, while protecting the rooting environment below.
- **Precautionary area:** This is RPA outside the CEZ where limited works are proposed, but must be carried out with care to minimise any impact on the tree rooting environment.

These areas are illustrated on our plans and annotated as follows:

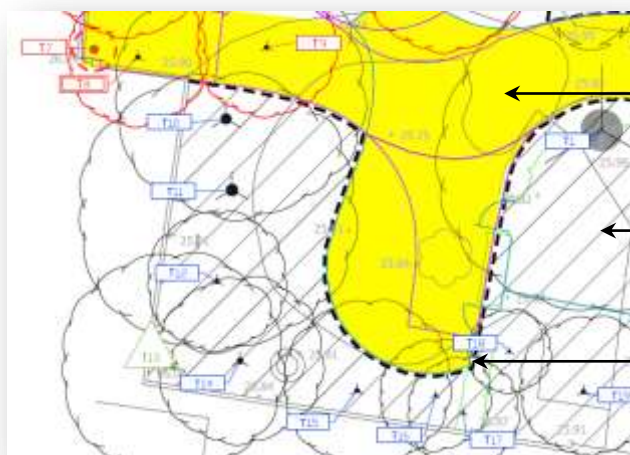

The yellow fill is the precautionary area

The light black diagonal hatch is the CEZ

The heavy black dashed line is the CEZ boundary

At the planning stage, this guidance describes practical methods and examples of how trees can be protected to assist the local planning authority (LPA) in deciding whether the proposal is feasible. If the LPA issues consent, this guidance, in conjunction with the report and tree protection plan,

Appendix 3: Protecting retained trees

will act as a written record for reference during the construction process. Once work starts on site, this guidance is designed to help the site personnel implement effective tree protection. All personnel working in RPAs must be familiar with this document and be properly briefed about their responsibilities to protect important trees.

2. Arboricultural supervision

All work within RPAs requires a high level of care. Qualified arboricultural supervision is essential to minimise the risk of misunderstanding and misinterpretation. Site personnel must be properly briefed about protecting retained trees before any work starts. Ongoing work near trees must be inspected regularly by an arboriculturist and, on completion, the work must be signed off to confirm compliance by the contractor. This supervision arrangement will normally include a pre-commencement meeting, regular inspection visits and sufficient flexibility to allow for visits as necessary to deal with emerging tree protection issues.

Primary tree protection

3. Primary tree protection

The CEZ is the RPA surrounding retained trees that must be protected from any disturbance by the construction activity. In practice, this can be done by any combination of fencing and ground protection, to be finalised and agreed at the pre-commencement meeting. Whether the CEZ is protected by fencing or ground protection, all the protective measures must be installed before the start of any site works that could affect trees. No protective measures should be removed or temporarily dismantled without consulting the supervising arboriculturist. Furthermore, the condition of all the protective measures should be regularly monitored to ensure they remain fit for purpose. The main means of preventing damage to trees and their RPAs in the CEZ are fencing, barriers and ground protection.

4. Protective fencing

Various fencing options are illustrated in figure 1 and photos 2–4 below. The minimum specification for the fencing must be as described in figure 2 of BS 5837 (figure 1 below) or an equivalent design that effectively restricts access to the RPA it protects.

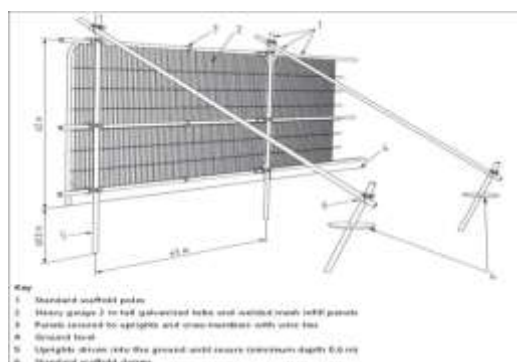


Figure 1: Recommendations taken from figure 2 of BS 5837.



Photo 2: Heras fencing wired to scaffold braced posts is a robust and effective interpretation of the BS specification.

Appendix 3: Protecting retained trees



Photo 3: Close up of bracing detail, essential for increasing the stability of the vertical framework.



Photo 4: Board specification on secure wooden posts is a suitable alternative to the standard braced scaffold design.

The precise form of the fencing can vary, provided it is fit for purpose in that it effectively restricts access and damaging activities within the RPA that it encloses. More specifically, behind the fencing, there must be no vehicular access; no fires; no storage of excavated debris, building materials or fuels; no mixing of cement; no service installation or excavation; no raising or lowering of soil levels; and no excessive cultivation for landscape planting. Any variations to these restrictions must be agreed by the supervising arboriculturist.

5. Trunk protection

Where individual trunks or branches are vulnerable to impact damage, a framework of scaffold or wood can be constructed to provide protection (photos 5 and 6).



Photo 5: A scaffold braced framework surrounding the trunk reduces the risk of accidental impact.



Photo 6: Board secured to scaffold framework adds another layer of protection for vulnerable trunks and branches.

6. Ground protection

Where it is not practical to protect the CEZ by the use of fencing alone, BS 5837 (6.2.3) allows for the fencing to be set back and the soil protected by ground protection. This allows improved access during construction, with the ground protection preventing damage to the CEZ outside

Appendix 3: Protecting retained trees

the protection of the fencing. A range of methods can be used, including retaining existing hard surfacing or structures that already protect the soil, installing new materials, or a combination of both. Whatever the choice of method, the end result must be that the underlying soil (rooting environment) remains undisturbed and retains the capacity to support existing and new roots. Photos 7–14 illustrate a range of practical solutions that can effectively protect CEZs of retained trees.



Photo 7: Heavy-duty plywood set onto a compressible woodchip layer and pinned into position is suitable to spread the loading from pedestrian access.



Photo 8: Spreading soil excavated from footings is an effective way of buffering the plywood surface from the wear of light vehicles.



Photo 9: Plywood fixed to a wood frame is another effective method of protecting soil from pedestrian compaction.



Photo 10: A scaffold framework attached to the main scaffold fencing can be used to support either scaffold planks or plywood to create an elevated platform with a gap beneath.

Appendix 3: Protecting retained trees



Photo 11: Cellular products are a very effective means of providing ground protection where heavy vehicle use is expected. Here, it is being used to temporarily widen an existing road, to be removed once the construction is finished.



Photo 12: Custom designed sectional tracks can be joined to support very heavy traffic use through sensitive areas.



Photo 13: A combination of retaining existing surfacing and using temporary construction cabin accommodation can be a very effective means of preventing damage to sensitive areas.



Photo 14: Steel plates can be an effective way of temporarily reinforcing weak surfacing over a construction access during the development activity.

Guidance for working in precautionary areas

7. Excavation and dealing with roots

Precautionary areas are RPAs outside the CEZ, i.e. they are areas where construction activity can take place, but it must be carried out with care to avoid damaging the sensitive rooting environment. BS 5837 (7.2) makes provision for excavating in RPAs, explaining that all excavation must be carried out carefully using hand-held tools and preferably by compressed air soil displacement, taking care not to damage the bark and wood of any roots (photo 15, 16 and 17).

All soil removal must be done with care to minimise the disturbance of roots beyond the immediate area of excavation. Where possible, flexible clumps of smaller fibrous roots should be retained if they can be displaced temporarily or permanently beyond the excavation without damage. If digging by hand, a fork should be used to loosen the soil and help locate any substantial roots. Once roots have been located, the trowel should be used to clear the soil away from them without damaging the bark. Exposed roots to be removed should be cut cleanly with

Appendix 3: Protecting retained trees

a sharp saw or secateurs 10–20cm behind the final face of the excavation. Roots temporarily exposed must be protected from direct sunlight, drying out and extremes of temperature by appropriate covering such as dampened hessian sacking (photo 18). If necessary, roots less than 2.5cm in diameter can be cut cleanly without consultation with the supervising arboriculturist. Roots greater than 2.5cm in diameter should be retained where possible and only cut after consultation with the supervising arboriculturist.



Photo 15: Careful hand-digging using conventional tools is acceptable for exposing roots in RPAs.



Photo 16: Air spades are very effective at exposing roots and services with minimal damage.



Photo 17: Air spades are particularly useful where roots are very dense.



Photo 18: Exposed roots must be protected from light, drying out and extremes of temperature by covering with hessian sacking and boards until they can be covered back with soil.

8. Removing hard surfacing and structures in precautionary areas

For the purposes of this guidance, the following broad definitions apply:

- **Hard surfacing:** Any hard surfacing used as a vehicular road, parking or pedestrian path including tarmac, solid stone, crushed stone, compacted aggregate, concrete and timber decking. This does not include compacted soil with no hard covering.
- **Structures:** Any man-made structure above or below ground including service pipes, walls, gate piers, buildings and foundations. Typically, this would include drainage structures, car-ports, bin stores and concrete slabs that support buildings.

Appendix 3: Protecting retained trees

9. Access

Roots frequently grow adjacent to and beneath existing surfacing and structures, so great care is needed during access and demolition. Damage can occur through physical disturbance of roots and/or the compaction of soil around them from the weight of machinery or repeated pedestrian passage. This is not generally a problem whilst surfacing and structures remain in place because they spread the load on the soil beneath and further protective measures are not normally necessary. However, once that protection is removed and the soil below is newly-exposed, the potential for damage to roots becomes an issue.

In summary, there should be no vehicular or repeated pedestrian access unless existing ground protection is retained or new protective measures are installed (photo 19). All exposed RPAs must be protected until there is no risk of damage from the development activity.



Photo 19: Ground protection must be used where repeated foot or vehicle traffic could cause compaction in sensitive RPAs. It can be as simple as plywood for pedestrians, but must be more robust for vehicles.



Photo 20: Machines with a long reach can be used to lift out heavy surfacing and structures as long as the machine sits outside the RPA and the exposed surface is protected before there is any further access.

10. Removal of material

Removing existing surfacing and structures is a high-risk activity for any adjacent roots and the following guidance must be observed:

1. Appropriate tools for manually removing debris may include a pneumatic breaker, crow bar, sledgehammer, pick, mattock, shovel, spade, trowel, fork and wheelbarrow (photos 21 and 22). Secateurs and a handsaw must also be available to deal with any exposed roots that have to be cut.
2. Machines with a long reach may be used if they can work from outside RPAs or from protected areas within RPAs (photo 20), but they must not encroach onto unprotected soil in RPAs.
3. Debris to be removed from RPAs manually must be moved across existing hard surfacing or temporary ground protection in a way that prevents compaction of soil. Alternatively, it can be lifted out by machines, provided this does not disturb RPAs (photo 20).
4. Great care must be taken throughout these operations not to damage roots as set out in paragraph 7 above.

Appendix 3: Protecting retained trees

5. If appropriate, leaving below ground structures in place should be considered if their removal may cause excessive root disturbance.



Photo 21: Careful lifting of cemented-in sets round this tree allowed them to be re-laid on a permeable sand base, improving the water input into the soil around the trunk.



Photo 22: These trees had impermeable surfacing right up to their trunks, which had to be removed by hand before installing new structures.

11. Installation of new surfacing in precautionary areas

BS 5837 (7.4) confirms that new surfacing can be installed within RPAs, but it has to be carried out with care. These operations are potentially damaging to trees because they may require changes to existing ground levels, resulting in localised soil structure degradation and/or disrupt the efficient exchange of water and gases in and out of the soil. Older trees are much more prone to suffer from such changes than young and maturing trees. Adverse impact on trees can be reduced by minimising the extent of these changes in RPAs. Generally, the most suitable surfacing will be relatively permeable to allow water and gas movement, load spreading to avoid localised compaction and require little or no excavation to limit direct damage. The actual specification of the design is an engineering issue that needs to be considered in the context of the bearing capacity of the soil, the intended loading and the frequency of loading. The detail of product and specification are engineering issues and must be provided by appropriate specialists.

12. Cellular confinement systems

BS 5837 (7.4.2.) sets out that no-dig, three dimensional cellular confinement systems can be used as the basis for extending hard surfacing into RPAs. It is our experience (www.barrelltreecare.co.uk/case-studies/SurfacingNearTrees.pdf) that this type of surfacing can be installed in the majority of situations without any significant adverse impact on adjacent trees, provided that proper consideration is given to all the circumstances. Most of our experience is with the CellWeb system supplied by Geosynthetics Ltd (www.geosyn.co.uk) and because of its sustained good performance over time, this is our preferred choice of product. The product is made from heavy-duty plastic that can be pulled apart to open into cells. These are then filled with washed stone, after the product is spread over the ground and pinned in place. This forms a base layer that acts as a floating raft, spreading the load across the whole construction width. The base layer can be topped with a variety of finishes as illustrated in figure 23. Photos 24 and 25 show the product spread over the ground and then filled with stone to produce the base layer.

Appendix 3: Protecting retained trees

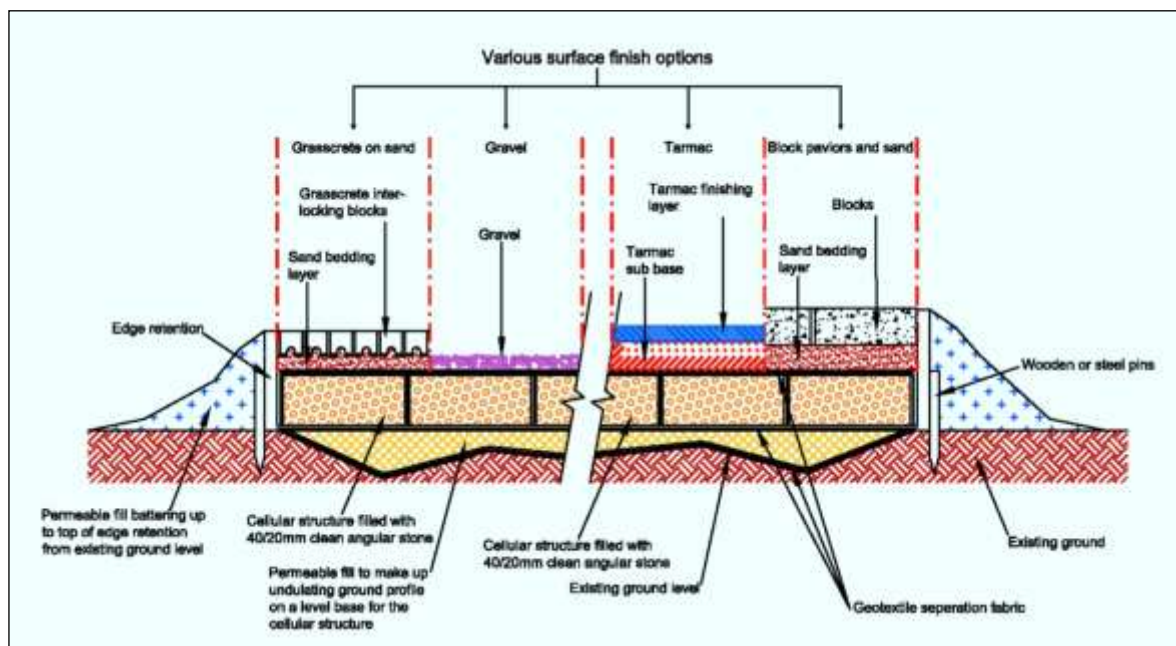


Figure 23: This conceptual cross-section illustrates the structural elements of the system and the multiple surfacing options that can be used with it.



Photo 24: The three-dimensional cells are opened up, spread across the area to be surfaced and pinned in place ready for the stone filling.



Photo 25: The stone-filled cells spread the load of traffic and the geotextile membrane on the ground prevents migration of the stone into the soil profile.

13. Dealing with undulating surfaces and establishing a tolerable level of excavation

The precise location and depth of roots within the soil is unpredictable and will often only be known when careful digging starts on site. Ideally, all new surfacing in RPAs should be no-dig, i.e. requiring no excavation whatsoever, but this is rarely possible on undulating surfaces. New surfacing normally requires an evenly graded sub-base layer, which can be made up to any high points with granular, permeable fills such as crushed stone or sharp sand. This sub-base must not be compacted as would happen in conventional surface installation. Some limited excavation is usually necessary to achieve this and need not be damaging to trees if carried out carefully and

Appendix 3: Protecting retained trees

large roots are not cut. Tree roots and grass roots rarely occupy the same soil volume at the top of the soil profile, so the removal of an established turf layer up to 5cm is unlikely to be damaging to trees. However, this may not be possible where there is no grass because tree roots may grow right up to the soil surface. In some situations, it may be possible to dig to a greater depth depending on local conditions, but this would need to be assessed by an arboriculturist if excavation deeper than 5cm is anticipated.

On undulating surfaces, finished gradients and levels must be planned with sufficient flexibility to allow on-site adjustment if excavation of any high points reveals large unexpected roots near the surface. If the roots are less than 2.5cm in diameter, it would normally be acceptable to cut them and the gradient formed with the preferred minimal excavation of up to 5cm. However, if roots over 2.5cm in diameter are exposed, cutting them may be too damaging and further excavation may not be possible. If that is the case, the surrounding levels must be adjusted to take account of these high points by filling with suitable material. If this is not practical and large roots have to be cut, the situation should be discussed with the supervising arboriculturist before a final decision is made.

14. Sub-base and finishing layers

Once the sub-base has been formed, the load spreading construction is installed on top without compaction. In principle, the load spreading formation will normally be cellular and filled with crushed stone, although the detail may vary with different products. Suitable surface finishes include washed gravel, permeable tarmac or block pavements set on a sand base (figure 23). However, for lightly loaded surfacing of limited widths (<3m) such as pedestrian paths, pre-formed concrete slabs may be appropriate if the sub-base preparation is as set out above.

15. Edge retention

Conventional kerb edge retention set in concrete-filled excavated trenches is likely to result in damage to roots and should be avoided. Edge retention in RPAs must be designed to avoid any significant excavation into existing soil levels (BS 5837, 7.4.3) and there are a number of approaches that are fit for this purpose. For block pavements, the use of pre-formed edging secured by metal pins is effective and can be reinforced by concrete supports as long as there is no excavation into the soil (photo 26). Railway sleepers (photo 27) pinned in place or wooden boards (photo 28) are two options, depending on the expected loading of the surfacing. A permeable soil fill can then be used to batter the grade back down to the existing soil level.

Appendix 3: Protecting retained trees



Photo 26: A conventional concrete haunching can be used to retain new surfacing as long as it is not dug into a trench - here it is placed on top of the CellWeb layer.



Photo 27: Although this is only a temporary surface, railway sleepers pinned into the ground can be used to retain the edges of new surfacing.



Photo 28: Wooden board pinned in place or held in position with backfilled topsoil can provide more informal and rustic surface edging.



Photo 29: In some situations, it may be appropriate to cast a free floating concrete surface directly onto the soil surface provided provision is made to prevent soil contamination while the concrete is being poured, i.e. an impermeable membrane separating the concrete from the soil.

16. Footpaths and surfacing without a load-spreading base layer

In some situations, limited-width floating concrete rafts constructed directly onto the soil surface may be acceptable for both pedestrian (photo 29) and vehicular access (photo 30), but the design must not include any strip-dug supports. If concrete is poured directly, precautions must be taken to ensure that no toxic fluids can contaminate the adjacent soil. Alternatively, elevated paths supported on low impact frames or post supports allow a decking surface to cross sensitive areas (photos 31 and 32). Where paths are installed very close to trunks, provision must be made for distortion from future root growth by selecting flexible components for the supporting frame and surfacing (photo 33).

Appendix 3: Protecting retained trees



Photo 30: This temporary access for heavy construction traffic on the outer edge of a RPA is a concrete slab cast above ground level and will be removed when the project is completed.



Photo 31: Board walks supported on posts or a light frame are another way of providing pedestrian access across sensitive RPAs.



Photo 32: New surfacing can be supported above the ground on posts leaving the soil surface beneath undisturbed.



Photo 33: Where surfacing is needed close to rapidly growing buttress roots, a light metal frame with rubberised surfacing will allow the path to distort without cracking as the roots grow.

17. Installing new surfacing on top of existing surfacing

In some instances, existing surfacing can be retained and used as a base for new surfacing. Normally, this will not result in significant excavation that could expose roots and so special precautions are not necessary. However, if large roots already protrude above the proposed sub-base level, then the precautions and procedures set out above must be observed. If the retained surfacing is impermeable, it may improve conditions for tree roots if it is punctured before the new surfacing is laid, but this is detail that should be agreed with the supervising arboriculturist.

18. Installation of new structures in precautionary areas

New structures in RPAs are potentially damaging to trees because they may disturb the soil and disrupt the existing exchange of water and gases in and out of it. Mature and over-mature trees are much more prone to suffer because of these changes than young and maturing trees. Adverse impact on trees can be reduced by minimising the extent of these changes in RPAs. This can be done by constructing the main structures above ground level on piled supports and redirecting water to where it is needed. The detailed design and specification of such structures is an engineering issue that should be informed and guided by tree expertise.

Appendix 3: Protecting retained trees

19. Small sheds, carports and bin stores

Light structures do not normally require substantial foundations and can have permeable bases. Ideally, their bases should be of a no-dig, load-spreading construction set directly on to the soil surface. They require a flat base and so an undulating site will need levelling to provide a suitable surface. Excavation of any high points by up to 5cm and filling depressions with permeable fill to provide a flat base will normally be acceptable provided no roots greater than 2.5cm in diameter need to be cut. If large roots are found, the preferred course of action would be to raise the base level of the structure by filling rather than cutting roots. However, if this is not practical and large roots have to be cut, the situation should be discussed with the supervising arboriculturist before a final decision is made. Light covering structures can be fixed onto a frame that can rise directly from the base or be fixed to supports either banged into the ground or set in carefully dug holes (photo 34). Provided the supports are well spaced, i.e. greater than 1.5m apart, and of a relatively narrow diameter, i.e. not in excess of 15cm, it is unlikely they will cause any significant disturbance to RPAs (photo 35).



Photo 34: These carports are formed by wooden posts above a three dimensional cellular no-dig and load-spreading surface of permeable crushed stone.



Photo 35: This deck supported above the ground on small posts provides a low-impact alternative to conventional patio surfacing in RPAs.

20. New foundations for free-standing walls, gate piers, buildings and bridges

Conventional strip foundations in RPAs for any significant structure may cause excessive root loss and are unlikely to be acceptable. However, BS 5837 (7.5) confirms special engineered foundations can be used in RPAs. Damaging disturbance can be significantly reduced by supporting the above ground part of the structures on small diameter piles and beams or cast floor slabs set above ground level (photos 36 and 37). The design should be sufficiently flexible to allow the piles to be relocated if significant roots are encountered in the preferred locations (photos 38 and 39). Before the actual installation of the new structure starts, any vulnerable RPA should be protected by temporary ground protection as set out in paragraph 6 above (one option shown in photo 39). At expected pile or gate pier locations, gaps in the ground protection should be left to allow access to the soil beneath. The preferred pile locations should be carefully excavated to a depth of 60cm to establish if there are any significant roots over 2.5cm in diameter that could be damaged. If significant roots are found, they should be dealt with as set out in paragraph 7 above or the pile location may have to be moved slightly (photo 38).

Appendix 3: Protecting retained trees

Once the piles have been installed, the ground protection is usually removed ready for the installation of the slab supporting the structure (photos 40 and 41). It is important to note that the lowest points of the new structure, i.e. the underside of the main slab and any pile-capping beam must be above the ground level between the piles and there should not be any further excavation. The supported structure base can be pre-cast and imported to the site ready to fix or can be cast in position using shuttering for the sides and a biodegradable void-former for the base (photo 42). BS 5837 (7.5.4) recommends that where impermeable structures cover significant proportions of RPAs, it may be necessary to provide water input through redirecting roof drainage beneath the supporting slab (photo 43).



Photo 36: Small diameter piles (less than 150mm) are an effective means of supporting structures in RPAs with minimal disturbance.



Photo 37: It is possible to support very large structures on piles within sensitive RPAs without any significant adverse impact on tree roots.



Photo 38: Where piles are proposed close to trunks, it is essential to excavate 50–75cm deep to see if there are any significant roots in the way, with provision to move the pile location if roots are found (note the pile was finally installed to avoid this root).



Photo 39: Ground protection must be used to spread the load of the piling rig once excavation has confirmed that no substantial roots are in the preferred pile location.

Appendix 3: Protecting retained trees



Photo 40: Once the piles have been installed (yellow tops), the ground protection to support the piling rig is removed ready to fix the void-former onto the bare soil, in advance of pouring the building slab.



Photo 41: Piles can also be used to support bridges across sensitive RPAs, but the temporary ground protection has to be removed before the main structure is either imported in or cast on site.



Photo 42: Where a slab is cast on site, a biodegradable void-former (red arrow) temporarily supports the weight of the liquid concrete until it sets. The void-former can then be wetted and washed away to leave a void or left to degrade naturally, both of which allow movement of air beneath the slab.



Photo 43: This reinforced base slab for a double garage has drainage provision (red arrow) beneath the structure to redirect roof runoff to supply roots with water.

Gate piers generally require larger holes and have less flexibility for relocation if large roots are found. Localised loss of roots may be unavoidable, so each situation should be assessed on its own merits by the supervising arboriculturist once the careful excavations have been completed. When installing any of these structures, the ground protection must remain in place until the construction is completed and there is no risk of damage to RPAs.

21. Walls on existing foundations and retaining walls

A free-standing wall on an existing foundation is unlikely to require any additional excavation and so its construction should have no adverse impact on RPAs if the appropriate ground protection is in place while the new wall is being built. However, replacing existing walls or constructing new walls that retain the soil of RPAs normally requires some limited excavation back into the exposed soil face to provide a working space of at least 10–20cm behind the inside wall face. This should be done carefully and limited to no more than required to construct the new wall. Any roots found should be dealt with as set out in paragraph 7 above. Once the wall is completed, any voids behind it should be filled with good quality top soil and firmed into place, but not over

Appendix 3: Protecting retained trees

compacted. Specific difficulties with large roots that are found during the course of the construction should be referred to the supervising arboriculturist.

22. Services

Excavation to upgrade existing services or install new services in RPAs may damage retained trees. Where possible, all services should be outside RPAs and installation in RPAs should only be chosen as a last resort. If installation within RPAs is being considered, as advised in 4.1.3 of the NJUG guidance, the decision should be made in consultation with the LPA or the supervising arboriculturist before any work is carried out. If service installation is agreed within RPAs, the NJUG protocol as set out in 4.1.3 of its guidance should be used to decide the most appropriate method. In summary, this sets out that *"Acceptable techniques in order of preference are; a) trenchless, ... b) Broken trench – hand-dug ... c) Continuous trench – hand-dug"*. If trenchless methods are to be used, there is normally a starting pit and a finishing pit that have to be dug at each end of the service run and these must be outside RPAs (photo 44). Where a hand-digging option is agreed (photo 45), any roots discovered during the excavations should be dealt with as set out in paragraph 7 above. Where possible, backfilled material around excavated services must not be heavily compacted, with specific advice provided in 4.1.5 of the NJUG guidance.



Photo 44: If possible, thrust boring is the preferred option for installing service routes through the RPAs of important trees, but there has to be space at the start and finish to dig substantial working pits.



Photo 45: Continuous trenches dug by hand so that important roots can be retained (with the service ducting threaded beneath) is an effective means of minimising damage (note the ground protection boards with soil piled on top on the left).

23. Fuel and chemical storage

Appendix 3: Protecting retained trees

Spilt chemicals that can soak into RPAs will kill existing roots and may prevent new roots growing, so provision must be made to minimise the risk of contamination to soil within the normal risk management protocols for the site. This would normally include means of containing spillages and procedures for clearing them up if they occur (photo 46).



Photo 46: Where fuel or other chemical are stored on site, it is now standard practice to have emergency spillage kits available to restrict the environmental impact of accidents.



Photo 47: Soil bunding or a supporting framework covered in heavy-duty plastic sheeting is essential where there is a risk of spillages contaminating RPAs. This specifically applies to cement mixing areas and vehicle washing facilities.

24. Cement mixing and vehicle washing points

All cement mixing and vehicle washing points must be located outside RPAs, with provision to contain any spillages. Where the contours of the site create a risk of polluted water or toxic liquids running into RPAs, a precautionary measure of bunding or a frame, sealed with heavy-duty plastic sheeting sufficient to prevent contamination (photo 47), must be used to contain accidental spillages.

Soft landscaping and new tree planting

25. Upgrading existing soft landscaping or replacing existing surfacing or structures with new soft landscaping

For the purposes of this guidance, soft landscaping includes the re-profiling of existing soil levels and covering the soil surface with new plants or an organic covering (mulch). It does not include the installation of new structures or compacted surfacing, which are considered as substantial works and covered in the preceding sections of this document.

Soft landscaping activity after construction can be extremely damaging to trees. No significant excavation or cultivation, especially by rotovators, should occur within RPAs. Where new designs require levels to be increased to tie in with new structures or the removal of an existing structure has left a void below the surrounding ground level, good quality and relatively permeable top soil should be used for the fill. It should be firmed into place, but not over compacted, in preparation for turfing or careful shrub planting. Ideally, all areas within 1m of tree trunks should be kept at the original ground level and have a mulched finish rather than grass to reduce the risk of mowing damage (photos 48 and 49).

Appendix 3: Protecting retained trees



Photo 48: The RPA of this tree was not effectively protected during construction and excessive compaction of the soil meant it died soon after this turf covered up the damage.



Photo 49: This tree had tarmac parking within its RPA that was removed and replaced with an organic mulch near the trunk and limited no-dig surfacing on the outer edges of its RPA.

26. New tree planting

Where new trees are proposed, the species, location and size will be explained within the text of the report and illustrated on the accompanying plan. Essential considerations on a tree-by-tree basis for the successful establishment and sustainability of new trees include:

- 1 **Planting locations:** Illustrative locations are shown on the appropriate plans. The final location for each tree must be agreed with the supervising officer after consideration of the prevailing site conditions in the immediate vicinity.
- 2 **Site preparation:** All competing weed vegetation within 1m of the stem must be mechanically removed or chemically killed to leave a weed-free planting area.
- 3 **Tree quality:** New trees must be specifically checked before planting to confirm that they are healthy and free of structural defects.
- 4 **Planting pits:** All planting must be into good topsoil and the pits excavated to a size of at least 10cm beyond the maximum dimensions of the loose roots or root-ball. The bottoms and sides of pits should be forked and broken up for a distance of at least 10cm beyond the pit boundaries before planting. The larger the tree, the greater this broken-up area needs to be, which can be up to 50cm and more for the larger semi-mature trees.
- 5 **Drainage:** Planting pits must be free-draining to avoid prolonged waterlogging. This specifically applies to poorly draining soils such as clay, where breaking up the pit bottom and sides is essential for the new tree to survive.
- 6 **Planting depth:** Planting the roots too deeply can seriously damage and kill trees. They should be planted no deeper than the depth that they were growing in the nursery, i.e. the base of the stem where it meets the roots at the root collar, should be no deeper than the final ground level around the planting pit.
- 7 **Stabilising by staking and guying:** Most trees taller than 1.5m at planting are likely to need stabilising until new supporting roots have grown. For all trees up to semi-mature size, this

Appendix 3: Protecting retained trees

should be in the form of short staking so that the tree is held 0.5–0.75m above ground level and no higher. For the larger semi-mature trees, either above ground guying of the stem with cables or securing the root-ball below ground is essential to allow new anchoring roots to develop.

- 8 **Protection:** Where there is a risk of browsing damage from animals, stems must be protected with individual guards or more substantial fenced protection, if appropriate.
- 9 **Mulching:** The area surrounding each new tree up to at least 1m from the stem must be covered with a 50mm depth of composted woodchip mulch. Cut grass must not be allowed to grow right up to the stem as it competes for water and nutrients, and predisposes the stem to mowing damage during maintenance.
- 10 **Watering:** All new trees must be watered in periods of dry and hot weather until they are established to be independent in the landscape. This must be for at least one year for smaller trees and could extend for up to four years for larger trees. All standard and larger trees must have a suitable means of ensuring that water reaches the deeper roots, usually in the form of a perforated pipe installed around the rootball at the time of planting.
- 11 **Annual maintenance:** All newly planted trees must be inspected on an annual basis until they are successfully established. All failures must be replaced. Annual maintenance must include keeping the planting area weed-free and topping up the woodchip mulch.
- 12 **Tree size:** Nurseries can supply most species of tree at a variety of sizes, ranging from small whips less than a metre in height up to large semi-mature specimens up to 12m height and more from some specialist growers. Figure 50 provides a simple guide on the commonest forms and sizes, and photos 51 and 52 indicate the variety of trees available.

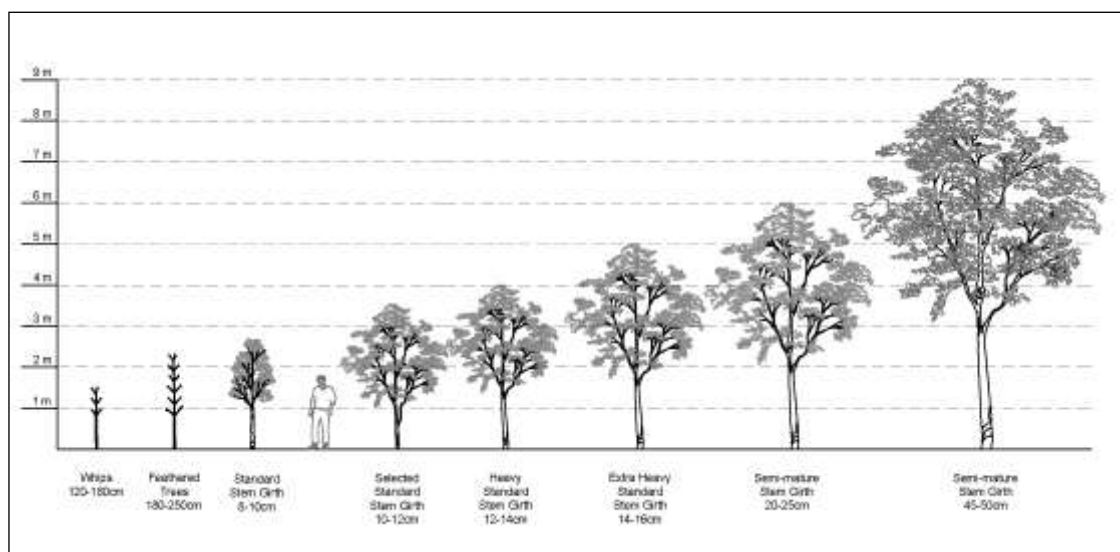


Figure 50: Summary of common conventions used by nurseries to describe tree types and sizes.

Appendix 3: Protecting retained trees

- 13 **Tree form:** Selecting the most appropriate tree for the location so that it does not out-grow the space available is important to avoid future inconvenience to occupiers. Specialist nurseries are able to supply a wide range of different forms (shape, size and proportion) and varieties with different aesthetic characteristics such as leaf shape, branching habit and foliage colour.



Photo 51: Hillier nurseries in Hampshire have a wide range of tree forms and species to provide instant effect in formal landscapes.



Photo 52: Barcham nurseries in Cambridgeshire specialise in supplying large trees for urban planting.

The larger semi-mature trees over 4–5m in height and the more unusual forms and varieties can be supplied by specialist nurseries (try www.barcham.co.uk, www.hilliertrees.co.uk and www.civictrees.co.uk). Such trees must be planted by experienced landscape contractors for the best results.

27. Structural tree soil

Structural tree soil is a man-made growing medium for trees with a high proportion of angular stone, which provides support for surfacing above while still maintaining voids that roots can grow in. It allows surfacing to be installed close to trees and for roots to establish beneath, making it suitable for growing trees in parking areas (photos 53 and 54). It is generally installed to a depth of about 1m, and filled in layers of about 300mm that can be progressively compacted to provide sufficient bearing for the new surfacing, without compromising future root growth. It is sometimes called tree sand or Amsterdam tree soil, and an internet search on either of these names will identify local suppliers. Three commercial suppliers can be found at www.landtechsoils.co.uk, www.treesand.co.uk and www.woodlandhp.co.uk.

Appendix 3: Protecting retained trees



Photo 53: Structural tree soil retains sufficient structure for tree roots to grow, even when compacted.



Photo 54: It allows trees to be successfully established in areas of extensive hard surfacing, with very little, if any, loss of parking space

28. Silva Cells and root deflectors

It is possible to establish trees in fully paved areas using structural supports that protect the soil beneath the surface from being compacted. These are effectively large containers made of concrete or combinations of metal and plastic, which support the surface above and any loads it has to carry. They are filled with soil to provide a viable rooting environment for trees, allowing large trees to provide sustainable amenity in highly urbanised settings. Such systems also have the added advantage that they allow storage of rainwater, significantly reducing the rate of flow of water from paved areas during peak periods. One of the most widely used systems is the DeepRoot Silva Cell (www.deeprout.com) (photos 55–57), but other products are available.



Photo 55: The individual Silva Cells can be assembled in layers and service ducting threaded through before filling with soil and fitting the reinforced tops.



Photo 56: Drainage from adjacent buildings can be directed into Silva Cells, significantly buffering rainwater runoff from urbanised areas.

New trees planted near surfacing can cause distortion damage from root growth if the appropriate precautions are not taken. Problems of this nature can be significantly reduced by installing root deflectors around the rootballs of new trees at the time of planting (photo 58). New roots growing out from the rootball meet the plastic profiled surface, deflecting them downwards, where they grow outwards at a lower level. Although they do eventually grow back near the surface, the onset of any damage is significantly delayed and it is usually far enough

Appendix 3: Protecting retained trees

away from the trunk for remedial works to be carried out without seriously affecting the stability of the tree. However, these products are not suitable for all situations, especially on shallow soils, and so their use should always be considered very carefully in the context of individual site conditions. Try www.deeproot.com and www.greenleaftrees.co.uk, or internet search on 'root deflectors' for more information on products.



Photo 57: The finished surfacing is profiled to leave the tree pit open, ready to be filled with good quality topsoil and the new tree.



Photo 58: This excavated tree shows the root deflectors that were installed when it was planted seven years previously. The product has deflected roots downwards and prevented damage to the adjacent surfacing. Note that this is a permeable sandy soil and the roots were able to grow beneath the bottom of the deflectors.

barrell
TREE CONSULTANCY

Field House, Fordingbridge Business Park, Ashford Road, Fordingbridge, Hampshire SP6 1BY

T: 01425 651470 E: info@barrelltreecare.co.uk

www.barrelltreecare.co.uk
