

SITE MANAGER - ENSURE NO OPERATIONS WITHIN RPA WITHOUT CONSULTATION WITH PROJECT ARBORICULTURAL CONSULTANT (INCLUDES ECOLOGICAL MEASURES SUCH AS REPTILE FENCING)

Arboricultural supervision

Minimum expectations:

1. pre-commencement meeting - see box below.
2. protective measures install/sign off
3. demolition and hard surface removal in RPA.
4. foundations in RPA.
5. any other potentially damaging operations in RPA.

The above should be documented as part of an auditable system of arboricultural site monitoring by the project arboricultural consultant. Refer to relevant sections of arboricultural impact appraisal and operation guidance in arboricultural method statement. If in doubt contact author of this document.

Important note

A pre-commencement meeting must be held on site before any development, demolition or site preparation works start.

The methods of tree protection outlined on this plan and within the associated arboricultural report should be fully discussed at this meeting so that all aspects of their implementation and sequencing are made clear to all parties.

Any clarifications or modifications must be recorded and circulated to all parties in writing.

Refer to arboricultural impact appraisal.

If existing footings cannot be reused then existing foundations in RPA may be removed using hand tools under arboricultural supervision.

New wall footings may not exceed dimensions of existing and trench shall be lined with plastic sheeting to prevent leaching of cement to tree roots of protected tree.

Brick entrance
Existing pilasters retained and extended to existing footings with electric gates (material TBC)

New brick wall built off existing footings

New low wall built off existing footings



Existing foliage retained and landscaped

Existing hard surface to be retained as ground protection.


hand dig under the RPA supervision

Root protection zone

green line - tree protection barrier BS5837 Refer to documents

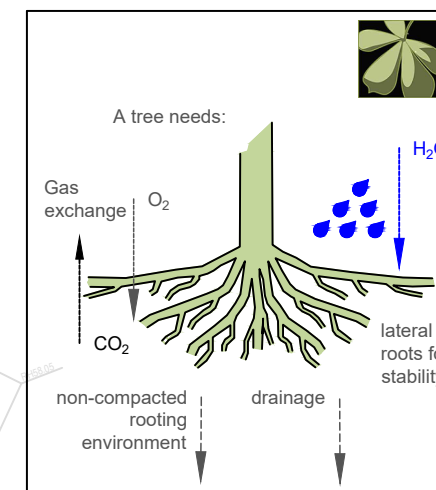

Legend

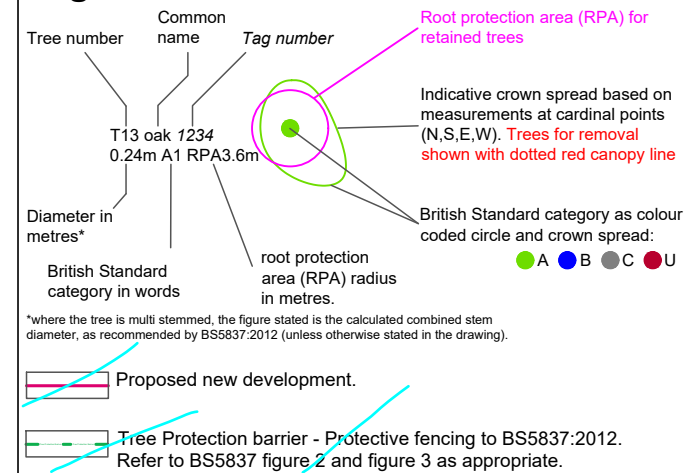

Proposed new development.
Tree Protection barrier - Protective fencing to BS5837:2012. Refer to BS5837 figure 2 and figure 3 as appropriate.

Technical Arboriculture
www.techarb.co.uk

Technical Arboriculture Limited
1 Chase Farm Close
Waltham Chase
Hampshire
SO32 2UB
01489 896 655 info@techarb.co.uk

PROJECT 39 PORTSDOWN HILL ROAD
DATE February 2023
JOB REF AIA/AMS-KC/39PORTSDOWN/001
DRAWING REF TPP-KC/39PORTSDOWN/001
DRAWN KC
SCALE 1:200 at A3
STATUS FINAL
REVISION 0

REVISION NOTES

