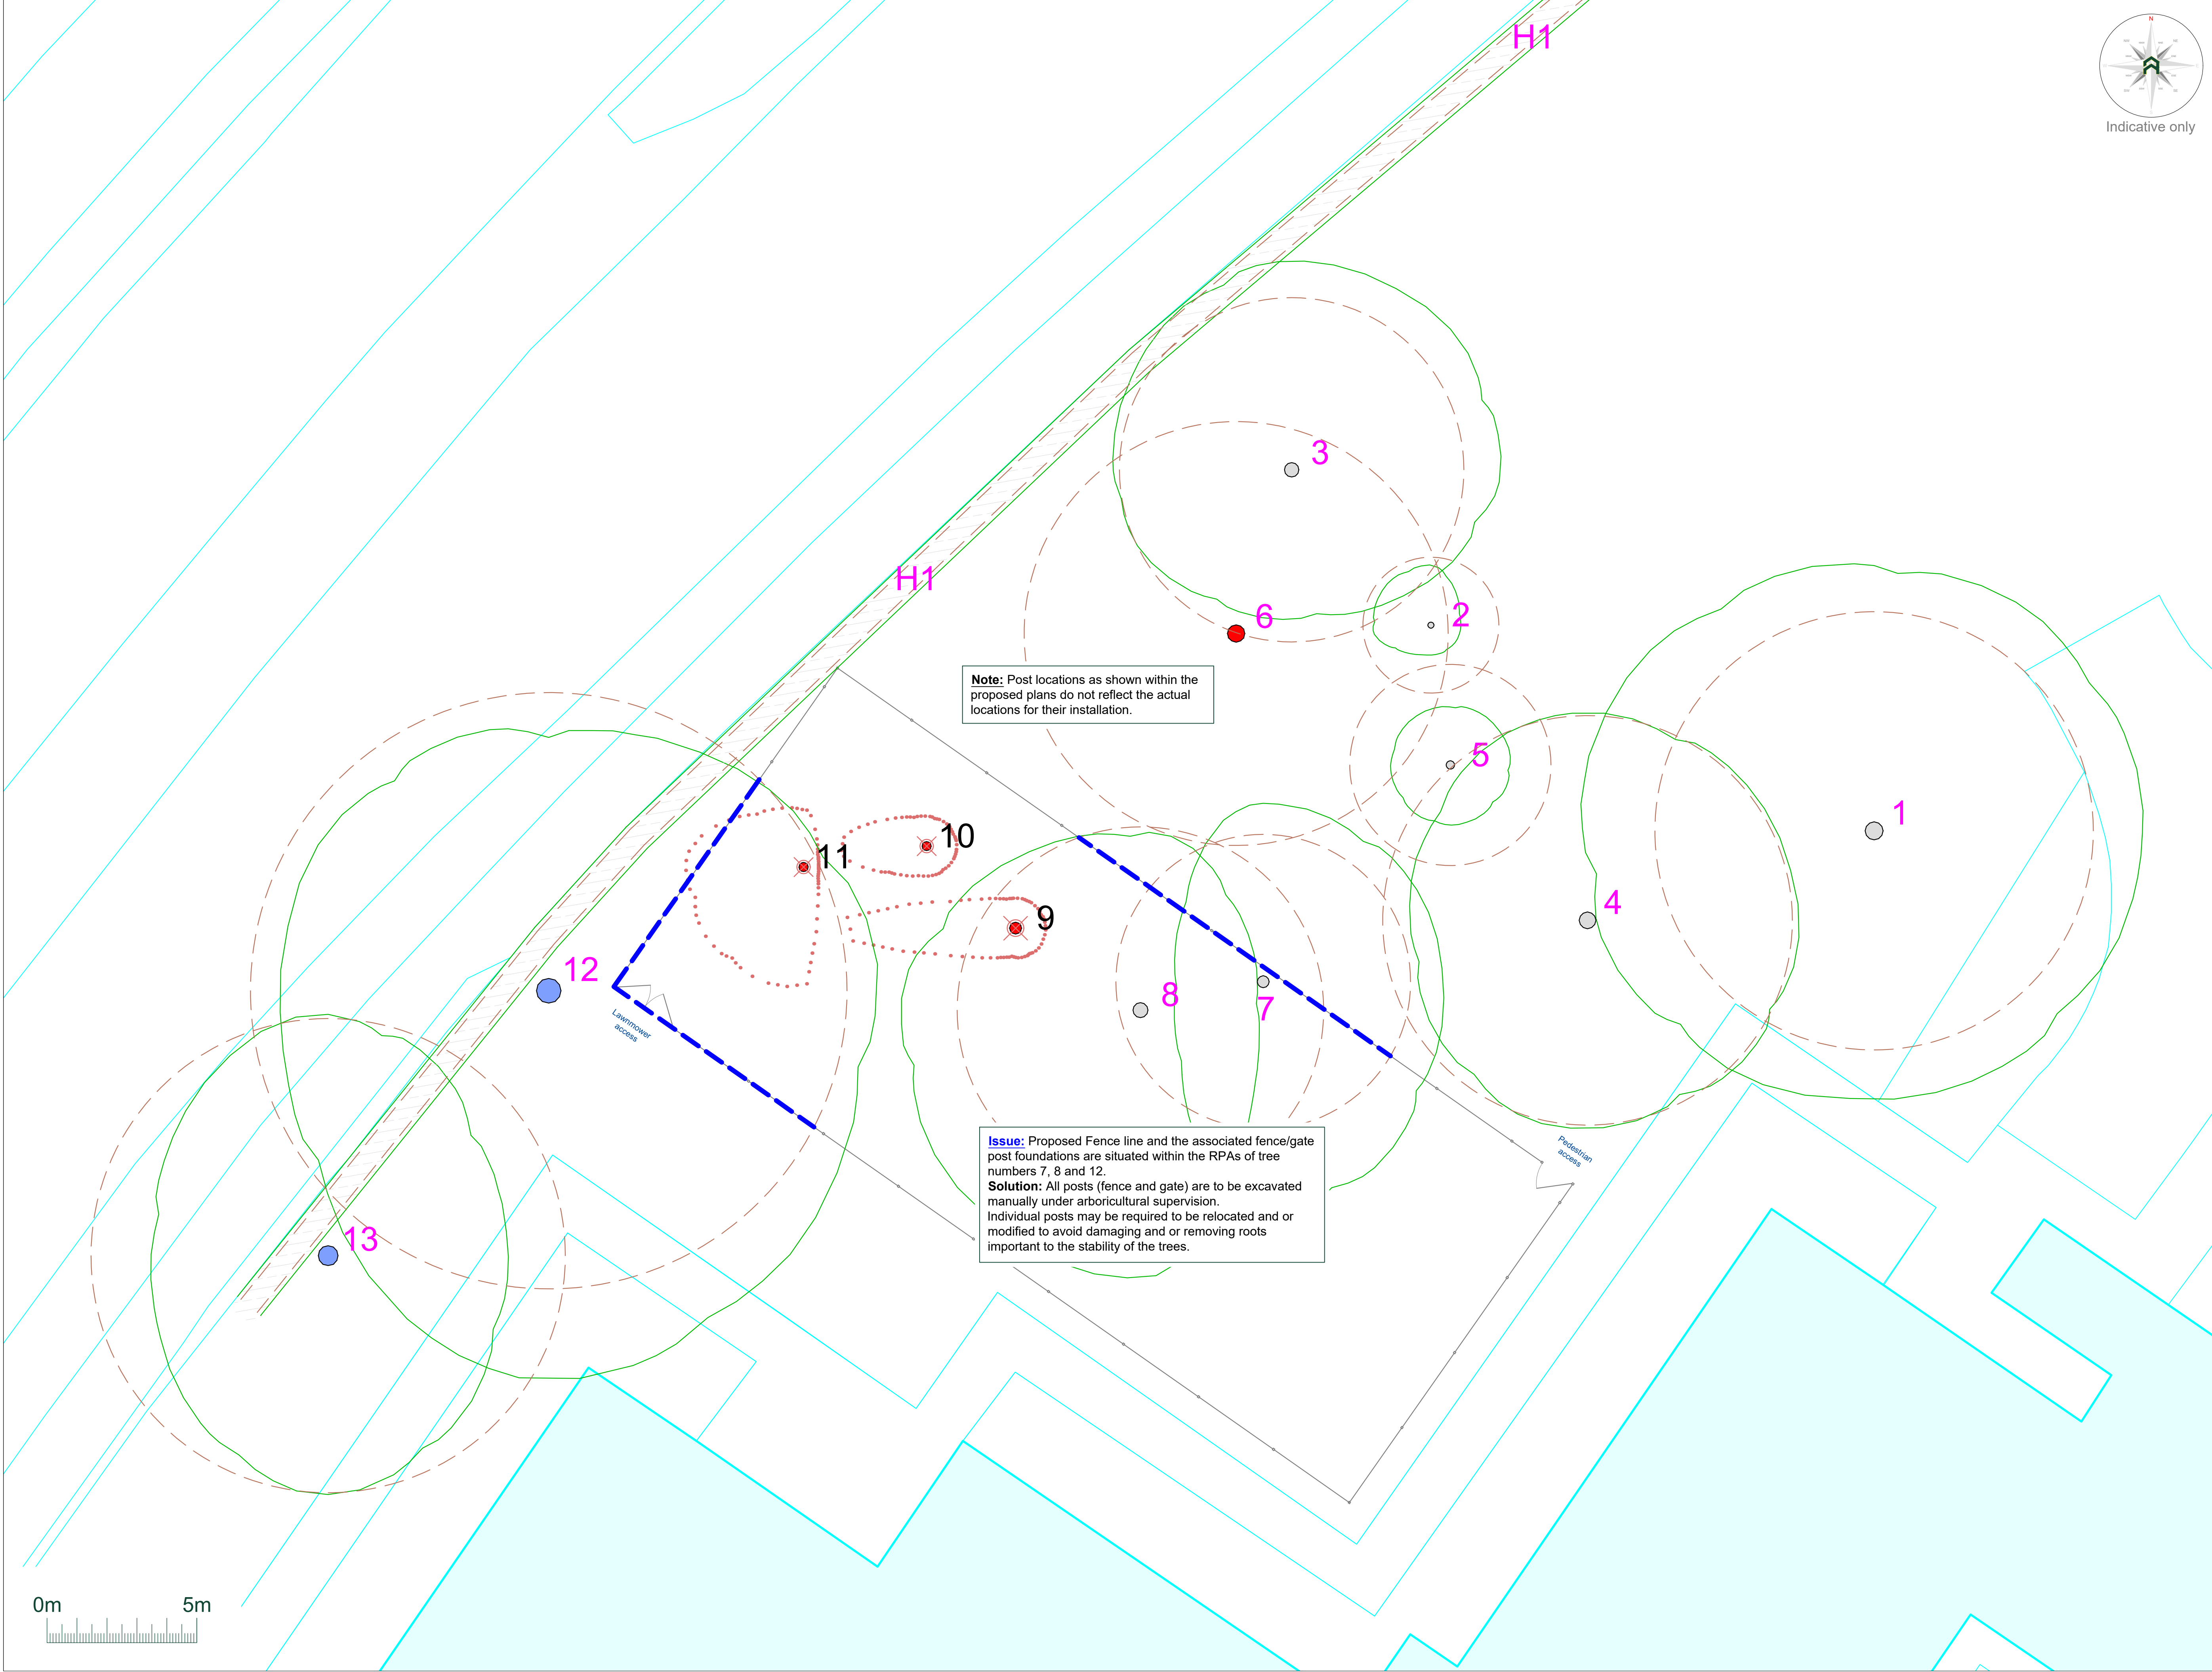


Arboricultural Impacts

Impacts	Nos. of trees
Trees to be removed	4
Groups / Hedges to be removed (Partial removal of groups)	0 (0)
Trees with proposed incursions into RPAs	3
Groups / Hedges with proposed incursions into RPAs	0
Trees that will require pruning	4
Groups / Hedges that will require pruning	0
Trees to be transplanted	0
Groups / Hedges to be transplanted	0

No.	Species	Proposed structure	Incursion
7	Ash	Nursery compound fence	RPA / Canopy
8	Ash	Nursery compound fence	RPA / Canopy
12	Red oak	Nursery compound fence	RPA / Canopy

Tree Work Schedule

No.	Species	Works	Category
3	Ash	Monitor ADB symptoms	C
4	Ash	Crown clean; Monitor ADB symptoms	C
6	Ash	Fell to 5m above GL	U
7	Ash	Crown clean; Crown lift E & S canopy to 5m above GL	C
8	Ash	Crown lift S & W canopy to 5m above GL	C
9	Ash	Fell to ground level, grind out stump	U
10	Ash	Fell to ground level, grind out stump	U
11	Ash	Fell to ground level, grind out stump	U
12	Red oak	Crown lift N, E & W canopy to 5m above GL	B

All tree work is to be undertaken in accordance with British Standard BS 3998:2010 Tree work - Recommendations.
All arising's are to be removed and the site is to be left as found.
Care is to be taken of the ground around retained trees to make sure that it does not become compacted as a result of tree surgery operations. No equipment or vehicles such as timber lorries, tractors, excavators or cranes shall be parked or driven beneath the crowns of any retained trees, to prevent subsequent compaction and root death.

No. of individual trees to be removed			
U	A	B	C
4	0	0	0

No. of groups / hedges to be removed			
U	A	B	C
0 (0)	0 (0)	0 (0)	0 (0)

() = Partial removal of a groups

Arboricultural Method Statement

All tree work is to be undertaken in accordance with British Standard BS 3998:2010 Tree work - Recommendations.
Please refer to Arbtech Consulting Ltd. Tree Schedule, Arboricultural Method Statement and Tree Protection Plan, for full details of all surveyed trees and how all aspects of the development may be implemented without detriment to retained trees.

Unit 3, Well House Barns, Chester, CH4 0DH
<https://arbtech.co.uk>, 01244 661170

Project: Growing Places at Havant, Civic Centre Road, Havant, Hampshire, PO9 2AX.

Client: Growing Places

Drawing: Arboricultural Impact Assessment

Based on: Fence Layout

Drawing No: Arbtech AIA 01

Date: Aug 2025 Scale: 1:100 @ A1 Drawn: MGM

Key:

Tree Nos.:	1	Tree Canopies:		Trunks:	
RPAs:		Category 'U' trees:		Category 'B' trees:	
Category 'C' trees:		Category 'C' groups:		Existing Site (OS file):	
Trees to be removed:		Incursion - Fences:			

All dimensions should be checked on site. No dimensions are to be scaled from this drawing. Please notify us of any discrepancies found. Arbtech Consulting Ltd. cannot be held responsible for inaccuracies in the base drawing in which this plan is based.
This drawing is designed to reflect the principles of the layout or design only, and relates only to the protection of retained trees.
This drawing is not to be read as a definitive part of the engineering or construction designs or method statement. An architect or structural engineer should be contacted over any matters of construction, detailing or specification and for any standards or regulatory requirements relating to proposed structures, their siting or underground services.
This drawing was produced in colour - a monochrome copy should not be relied upon.

© Arbtech Consulting Ltd. 2021
