


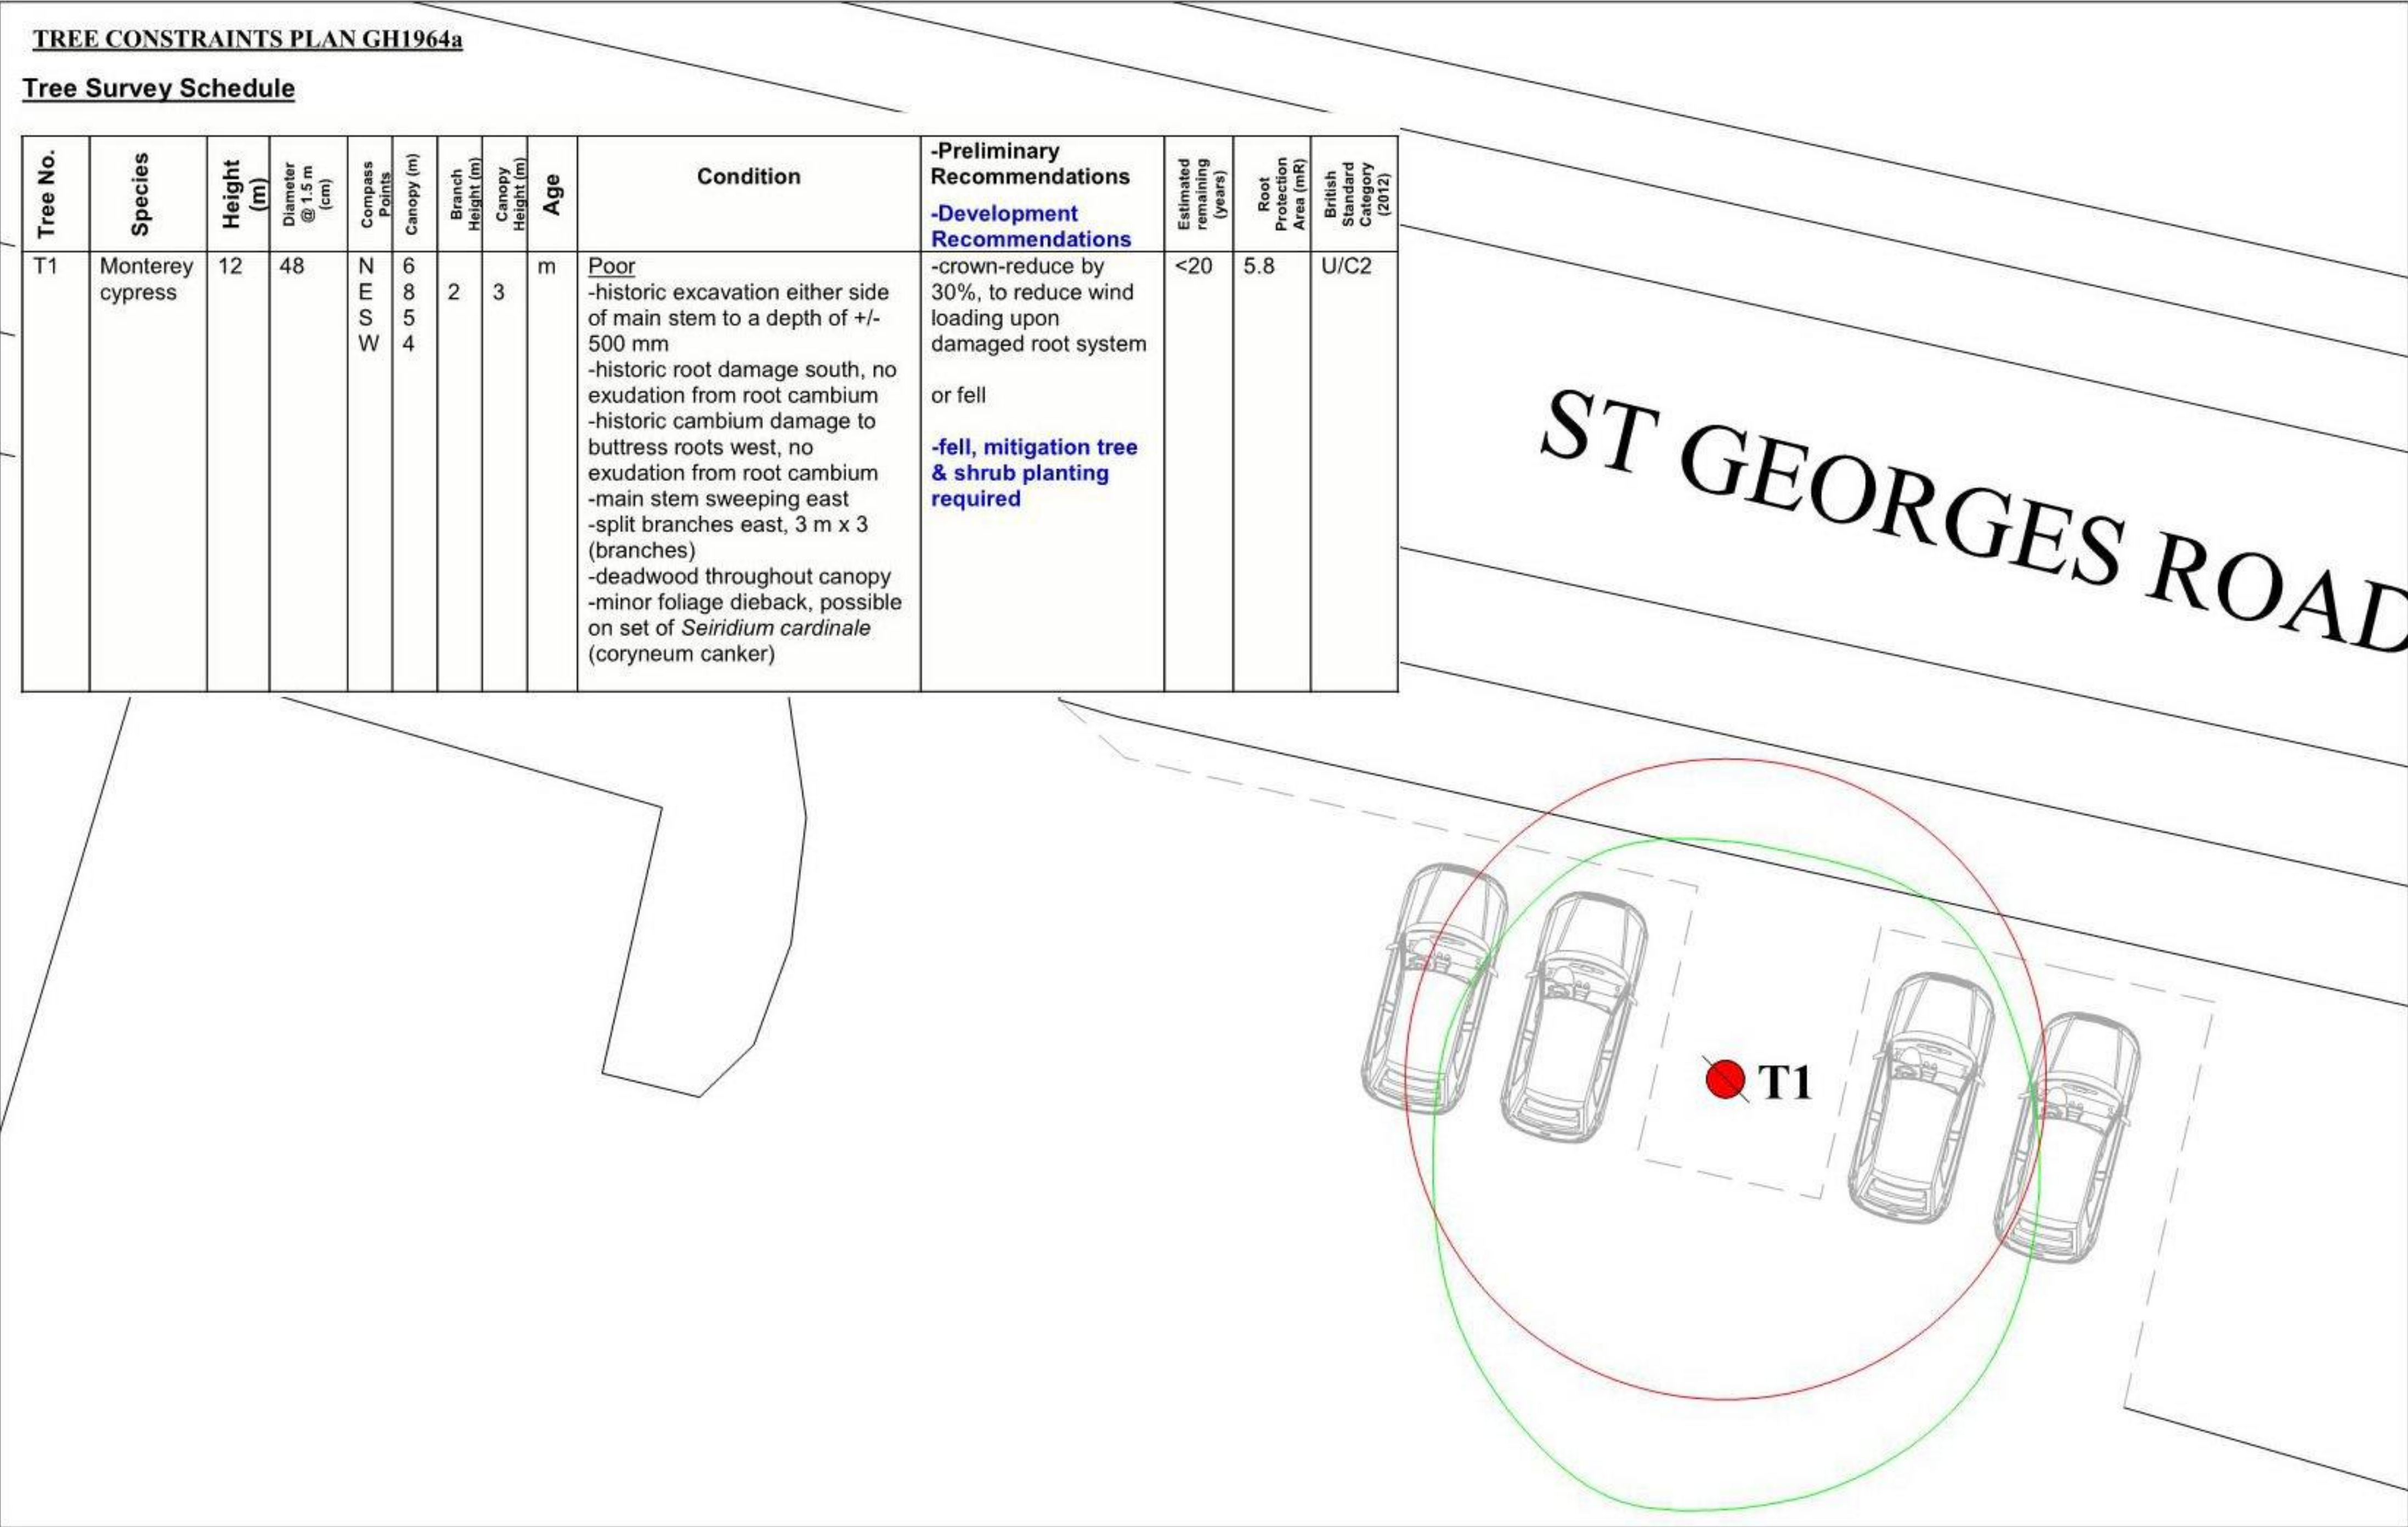

British Standard 5837:2012 Tree Categories Key

BS 5837:2012
Category U Tree
Root Protection Area

LEGEND

Tree Location & Number

Trees not detailed on plans provided

Trees for Removal

Indicative landscape features not detailed on plans provided

Canopy Spread

Root Protection Area

Proposed Structures

Landscape Planting (see Shrub Planting Schedule)

Landscape Planting (see Shrub Planting Schedule)

Timber Sleeper Raised Bed (see Planting / Landscape Notes)

Tree Planting (see section 10.2)

0m 1 2 3 4 5 Scale: 1-100

Site Address:

Gorseway
354 Sea Front
Hayling Island, PO11 0BA

Client:

Agrincare Group

Drawing Title:

Tree Constraints Plan GH1964a
Tree & Shrub Planting Plan GH1964b

Rev. 00 Paper Size and Scale: A1 - 1:100

Date: 16/08/2019 Project Ref: GH1964

Drawing Ref: GH1964a & GH1964b

IMPORTANT NOTICE:
This plan is based on the plans and/or site layout plans provided. All measurements must be checked with these plans and appropriate documents. All dimensions to be checked on site prior to commencement of work. Differences between drawings, specifications or structural engineer's details are to be referred immediately to Gwydion's Tree Consultancy. Work should only be undertaken from local authority approved drawings.

THIS PLAN SHOULD BE VIEWED IN COLOUR

GWYDION'S
TREE
CONSULTANCY

Tel: 01202 748967
office@gwydiontreeconsultancy.co.uk
gwydiontreeconsultancy.co.uk

Copyright 2019

Phased Development in relation to Arboriculture & Landscape

1. Phased Development in relation to Tree Protection – in order of events A to E

A. tree work - see Tree Survey Schedule within plan GH1964a

B. specific construction technique – installation of planting borders, see Planting/Landscaping Notes & plan GH1964b

C. main construction & main construction completion

D. specific construction technique – planting see Planting Schedule, Planting/Landscaping Notes & plan GH1964b

E. specific construction technique - see below Five-Year Maintenance Plan

= Supervision required

The project manager will give the Arboricultural Consultant at least 48 hours' written notice prior to any Arboricultural Supervision activity. If there is a specific request from a representative of the LPA wishing to attend, 7 days' notice shall be required. An Arboricultural Supervision statement will be submitted to the Local Planning Authority, in writing after each supervision event.

Tree and Shrub Planting Schedule:

Trees

Tree No.	Species	HT	GIRTH @ 1 m	CH	Age	Condition	-Recommendations
P1 P2	Field Maple (<i>Acer campestre</i>)	3.5 m	8–10 cm @ 1 m	1.75 - 200 m	Y	Good -container grown 45 l pot or -rootball, size minimum 300 mm in diameter -no stem movement in rootball -no root bulges within the rootball -centrally located stem in rootball -tree in good form with no included branches, secondary crossing branches, defined central leader FURTHER GUIDANCE FROM BS8545-2014	-formative prune, if not undertaken prior to purchase
P2	Scots Pine (<i>Pinus sylvestris</i>)	2 – 2.5 m	N/A	0.0 m	Y	Good -100 l container grown -tree of good form with no included branches, secondary crossing branches, defined central leader FURTHER GUIDANCE FROM BS8545-2014	-as above

FURTHER GUIDANCE FROM BS8545-2014

Shrubs

No.	Species Name	Plan Ref.	Specification	Density
57	<i>Ligustrum vulgare</i>	LV3	3L 30 – 40 cm	3/m ²
48	<i>Cistus ladanifer</i>	CIS3	3L 30 – 40 cm	4/m ²
