
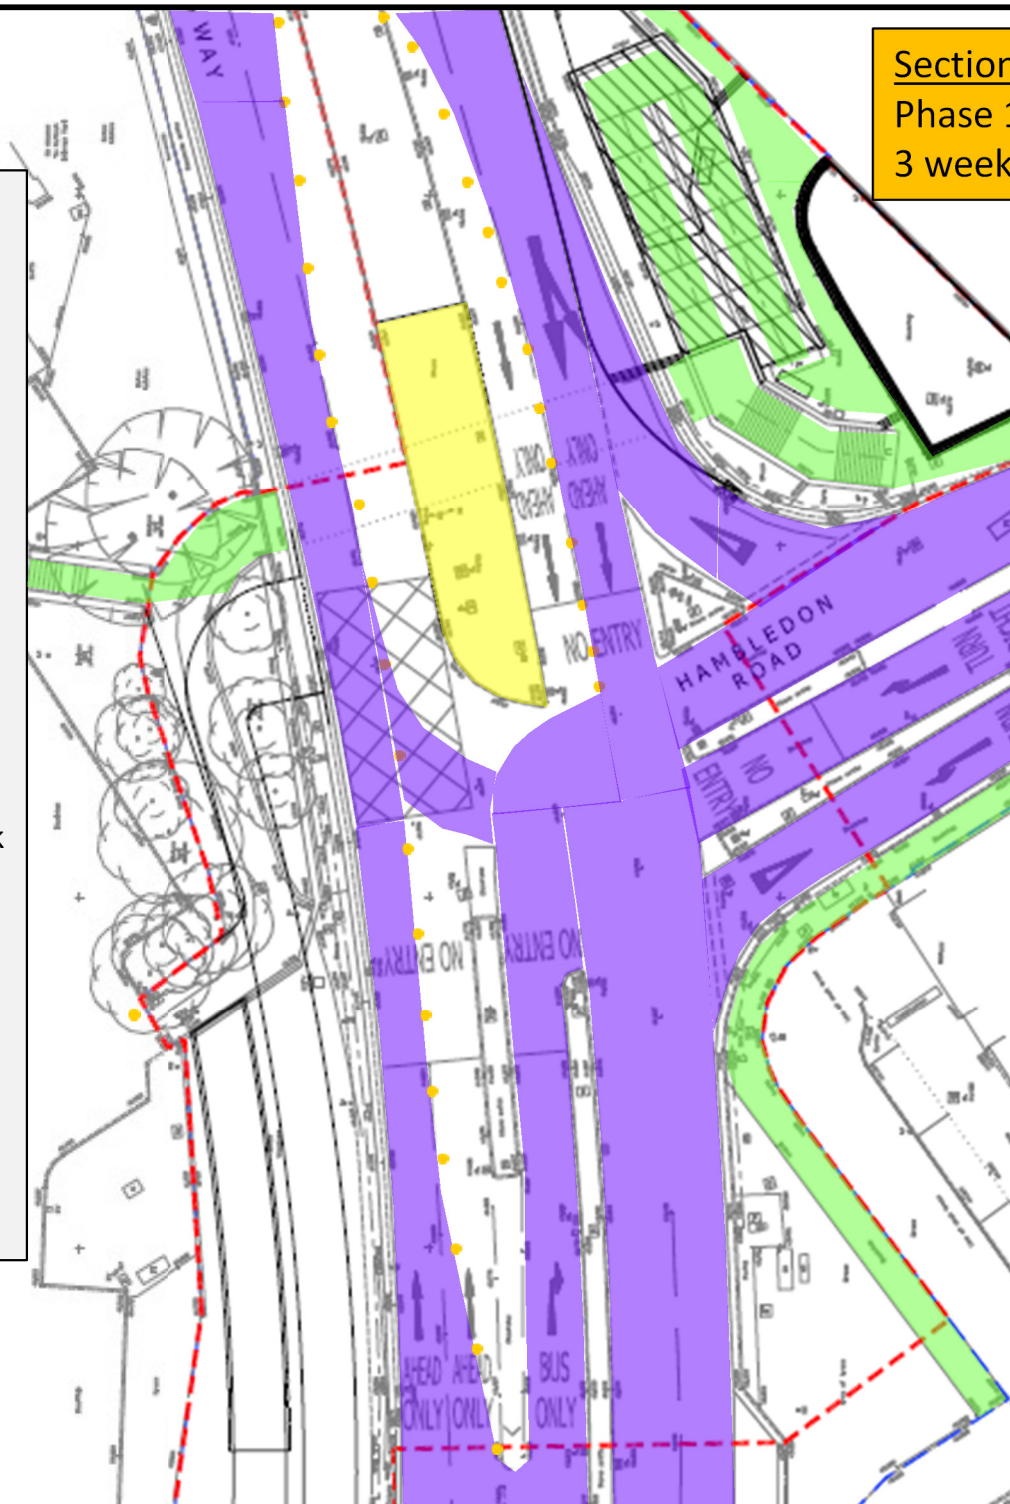


Section 278 Works (Maurepas Way).
Phase 1
3 weeks.

Key points.
Phase 1.

- Pedestrian route through underpass must remain open.
- Existing stepped ramp must remain open.
- Must keep two lanes of traffic open in both directions during peak traffic flows (0700 – 0930 and 1600 – 1900).
- Construct central refuge island with lane closures either side during off-peak hours (= 5.5 effective working hours/day, allowing for 0.5 hrs each for setting up & taking down TM).
- Construction of new pedestrian/cycle ramp is ongoing simultaneously.




Key points.
Phases 2 & 3.

- Pedestrian route through underpass must remain open.
- Existing stepped ramp must remain open.
- Must keep two lanes of traffic open in both directions during peak traffic flows (0700 – 0930 and 1600 – 1900).
- Construct Phases 2 & 3 concurrently with lane closures during off peak hours.
- Construction of new pedestrian/cycle ramp is ongoing and must finish at the same time as these phases.

Section 278 Works (Maurepas Way).
Phase 2 (Town centre side) and
Phase 3 (Retail Park side) to run
concurrently.
5 weeks total.

Key.

-  Pedestrian & Cycle routes.
-  Vehicular routes.
-  Construction areas.
-  Already complete.

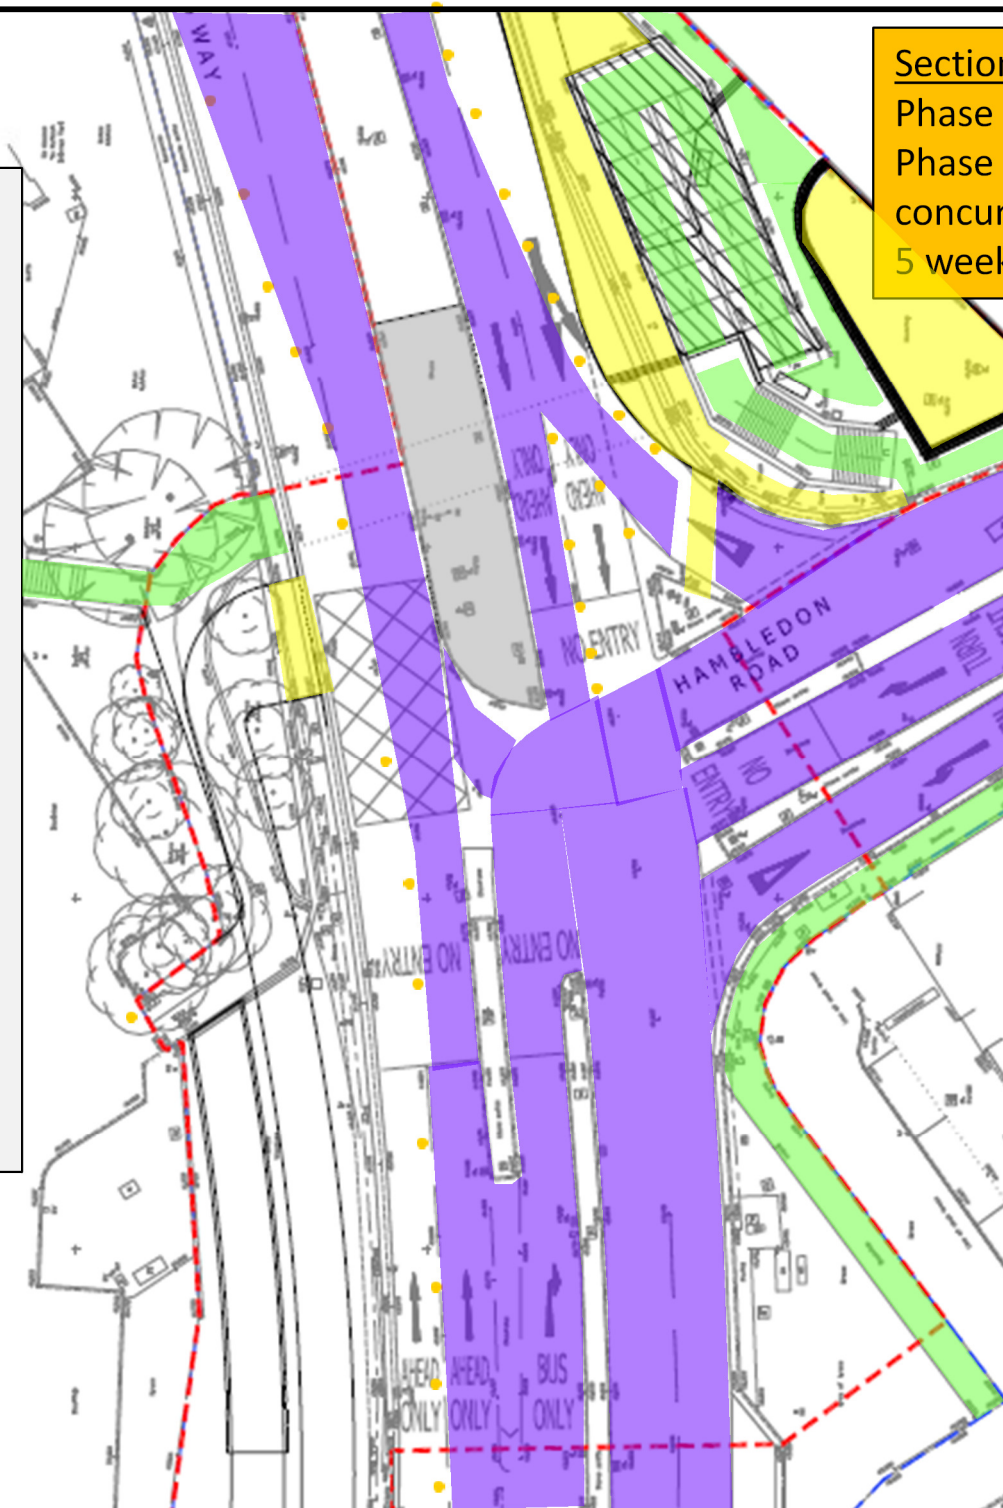

Key points.
Phase 4.

- C/way resurfacing and line marking (Off-peak only. Possible nightworks with closure of west bound c/way).
- Pedestrian route through underpass must remain open.
- Existing stepped ramp must remain open.
- Must keep two lanes of traffic open in both directions during peak flows (0700 – 0930 and 1600 – 1900).
- Construction of new pedestrian/cycle ramp is ongoing.

Section 278 Works (Maurepas Way).
Phase 4.
2 weeks (Concurrent with last 2 weeks of phase 2&3).

Key.


-  Pedestrian & Cycle routes.
-  Vehicular routes
-  Construction areas.
-  Already completed.



Section 278 Works (Maurepas Way).
Phase 5
12 weeks.

Key points.
Phase 5.

- Pedestrian route through underpass must remain open.
- Existing stepped ramp closed for infilling.
- Must keep two lanes of traffic open in both directions during peak flows (0700 – 0930 and 1600 – 1900).
- Construction of new pedestrian/cycle ramp is complete. Pedestrians and cyclists now using new Toucan crossing and new ramp.
- Temporary footway needed on town centre side whilst ramp is infilled and slabs/tarmac laid.

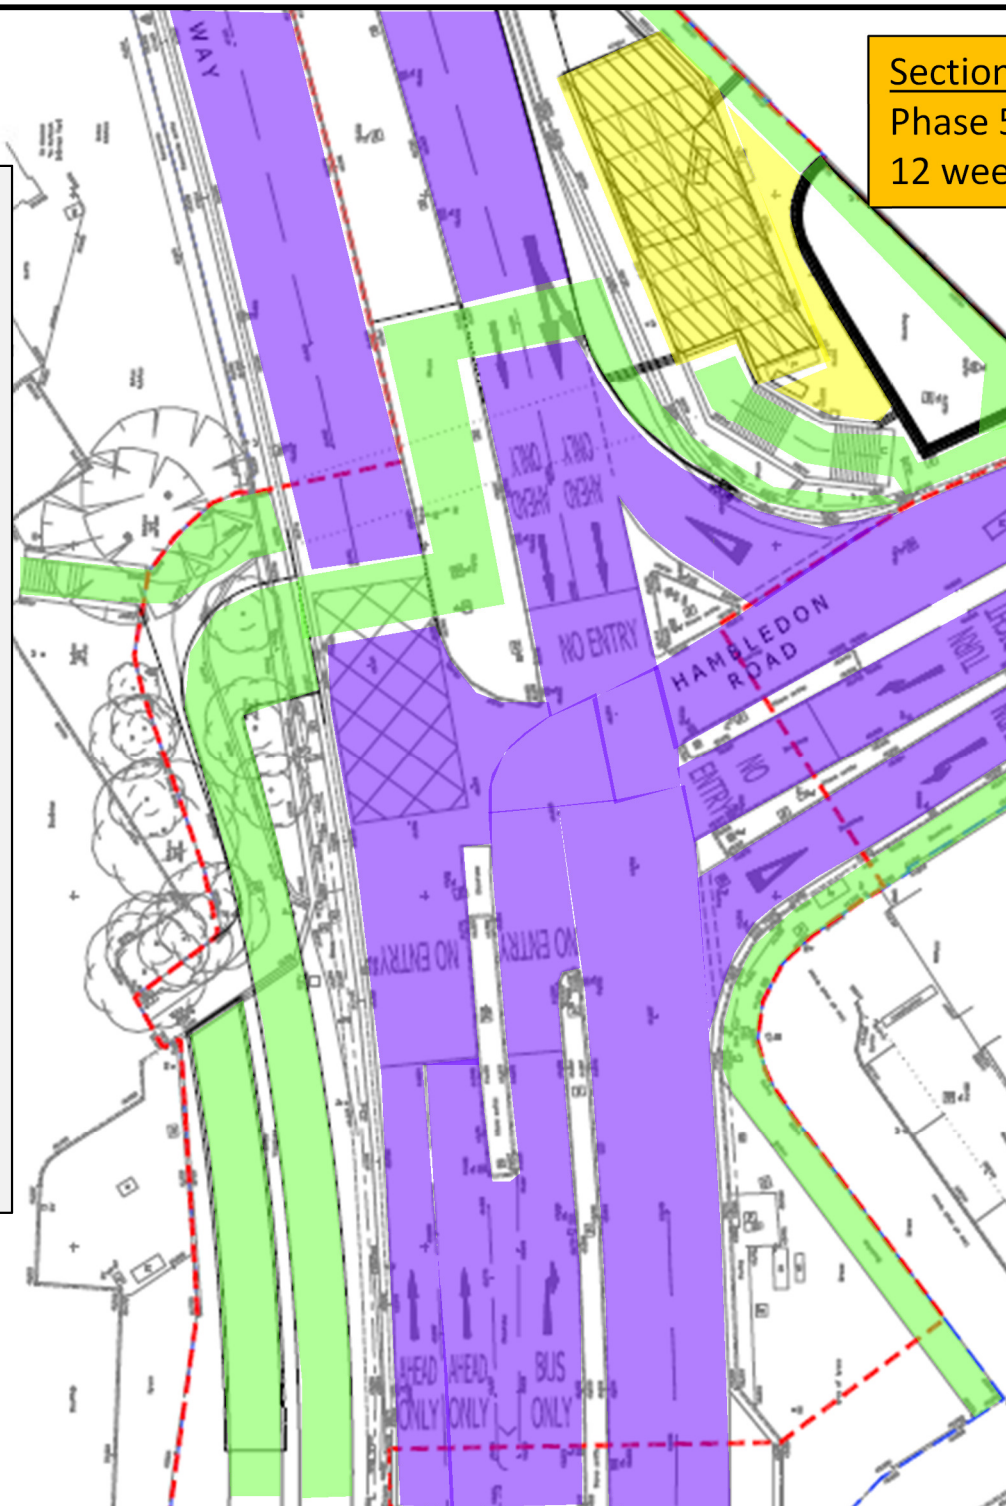

Key.

-  Pedestrian & Cycle routes.
-  Vehicular routes
-  Construction areas.

Section 278 Works (Maurepas Way).
Completion.

Key points.
Completion.

- Completion of all S278 works is a condition of the S278 Agreement.
- LED apply to S278 over-run.

Key.

-  Pedestrian & Cycle routes.
-  Vehicular routes

