

CONSTRUCTION EXCLUSION ZONE

Root protection areas (RPA) of retained trees within which all construction activity is restricted.

All trees that are being retained on site must be protected by barriers and/or ground protection before any materials or machinery are brought onto the site, and before any demolition, development or stripping of soil commences. Where all activity can be excluded from the RPA, vertical barriers must be erected to create a construction exclusion zone. Where, due to site constraints, construction activity cannot be fully or permanently excluded in this manner from all or part of a tree's RPA, appropriate ground protection can be installed.

DEFAULT POSITION FOR THE TREE PROTECTION BARRIERS.

The specification for the fencing can be found in the method statement. Should an alternative design be more viable and appropriate, it must be agreed with the project arboriculturist before its implementation.

TEMPORARY FENCING

The fencing is used to protect areas of special detail. It is to be installed with the main tree protection fence and is only to be removed when the detail is installed as per the method statement & under the supervision of the project arboriculturist. It shall be weld-mesh panels on boots, secured to the ground with road pins (or similar).

NO-DIG SURFACE

Cellular confinement system (CCS) to be used to create this area of hard surface, above the existing ground level. Topsoil to be retained. Depth of CCS to be 50/75mm for pedestrian surfaces and 100/200 for vehicular surfaces. Surface to be porous to approved details and specifications. To be installed under arboricultural supervision. **All specifications subject to engineering design.**

Cells to be filled with 20-40mm clean graded angular stone to manufacturers details and specifications

Peg and board edging

Top soil to BS3882:2007

Original ground level

TreeTex T300 non-woven geotextile or similar approved laid over formation

Depressions and soft spots in formation to be filled with sharp sand to levels required

CCS/Cellular confinement system (Geosynthetics CellWeb or similar approved)

Porous surface to finish

TREE TO BE REMOVED

A CATEGORY TREE

B CATEGORY TREE

C CATEGORY TREE

U CATEGORY TREE

ROOT PROTECTION AREA (RPA) FOR RETAINED TREES

1

2

3

4

5

6

7

8

9

The original of this drawing was produced in colour- a monochrome copy should not be relied upon.

012345

metres

D	12.06.2020	Revised parking by plot 119-112	RA
C	02.07.2019	Revised layout and drainage	TRG
B	03.06.19	Phase 2 tree protection extended	AJB
A	10.05.2019	No dig added T1 - 3	TRG
Rev	Date	Details	Drawn

HEAD OFFICE
Rodbourne Rail Business Centre, Grange Lane,
Malmesbury, SN16 0ES
Tel: 01465 825646

Courtyard House, Mill Lane, Codrington, GU7 1EY
Tel: 01483 425714

Suite 6, Crescent House, Yonge Close, Eastleigh, SO50 9SX
Tel: 02382 026300

9 Brownlow Road, Cambridge, CB4 3NG
Tel: 07625 868654

Copyright of ACD. All rights described in Chapter IV of the Copyright, Designs and Patents Act 1988 have been generally assigned. 2015. Copyright of this plan remains with ACD until all fees have been paid in full.

scheme: Woodcroft Farm, Woodcroft Lane, Waterlooville
client: Linden Homes
drawing: Tree Protection Plan
date: March 2018
scale: 1:250@A1
dwg no: LIN21652-03D Sheet 1 of 9
drawn: RA checked: TRG



CONSTRUCTION EXCLUSION ZONE
Root protection areas (RPA) of retained trees within which all construction activity is restricted.

All trees that are being retained on site must be protected by barriers and/or ground protection before any materials or machinery are brought onto the site, and before any demolition, development or stripping of soil commences. Where all activity can be excluded from the RPA, vertical barriers must be erected to create a construction exclusion zone. Where, due to site constraints, construction activity cannot be fully or permanently excluded in this manner from all or part of a tree's RPA, appropriate ground protection can be installed.

DEFAULT POSITION FOR THE TREE PROTECTION BARRIERS.

The specification for the fencing can be found in the method statement. Should an alternative design be more viable and appropriate, it must be agreed with the project arboriculturist before its implementation.

TEMPORARY FENCING
The fencing is used to protect areas of special detail. It is to be installed with the main tree protection fence and is only to be removed when the detail is installed as per the method statement & under the supervision of the project arboriculturist. It shall be weld-mesh panels on posts, secured to the ground with road pins (or similar).

NO-DIG SURFACE
Cellular confinement system (CCS) to be used to create this area of hard surface, above the existing ground level. Topsoil to be retained. Depth of CCS to be 50/75mm for pedestrian surfaces and 100/200 for vehicular surfaces. Surface to be porous to approved details and specifications. To be installed under arboricultural supervision. **All specifications subject to engineering design.**
Cells to be filled with 20-40mm clean graded angular stone to manufacturers details and specifications
Peg and board edging
Top soil to BS3882:2007
Original ground level
TreeTex T300 non-woven geotextile or similar approved laid over formation
Depressions and soft spots in formation to be filled with sharp sand to levels required
CCS/Cellular confinement system (Geosynthetics CellWeb or similar approved)


TREE TO BE REMOVED
A CATEGORY TREE
B CATEGORY TREE
C CATEGORY TREE
U CATEGORY TREE
ROOT PROTECTION AREA (RPA) FOR RETAINED TREES

The original of this drawing was produced in colour- a monochrome copy should not be relied upon.

D	12.06.2020	Revised parking by plot 119-112	RA
C	02.07.2019	Revised layout and drainage	TRG
B	03.06.19	Phase 2 tree protection extended	AJB
A	10.05.2019	No dig added T1 - 3	TRG
Rev	Date	Details	Drawn

ACD ENVIRONMENTAL
HEAD OFFICE
Rodbourne Rail Business Centre, Grange Lane,
Malmesbury, SN16 0ES
Tel: 01666 825646
Courtyard House, Mill Lane, Codrington, GU7 1EY
Tel: 01483 425774
Suite 6, Crescent House, Yonge Close, Eastleigh, SO50 9SX
Tel: 02382 028300
9 Brownlow Road, Cambridge, CB4 3NG
Tel: 07625 868654
Copyright of ACD. All rights described in Chapter IV of the Copyright, Designs and Patents Act 1988 have been generally assigned. 2015. Copyright of this plan remains with ACD until all fees have been paid in full.

Linden HOMES
scheme: Woodcroft Farm, Woodcroft Lane, Waterlooville
client: Linden Homes
drawing: Tree Protection Plan
date: March 2018
scale: 1:250@A1
dwg no: LIN21652-03D Sheet 2 of 9
drawn: RA checked: TRG

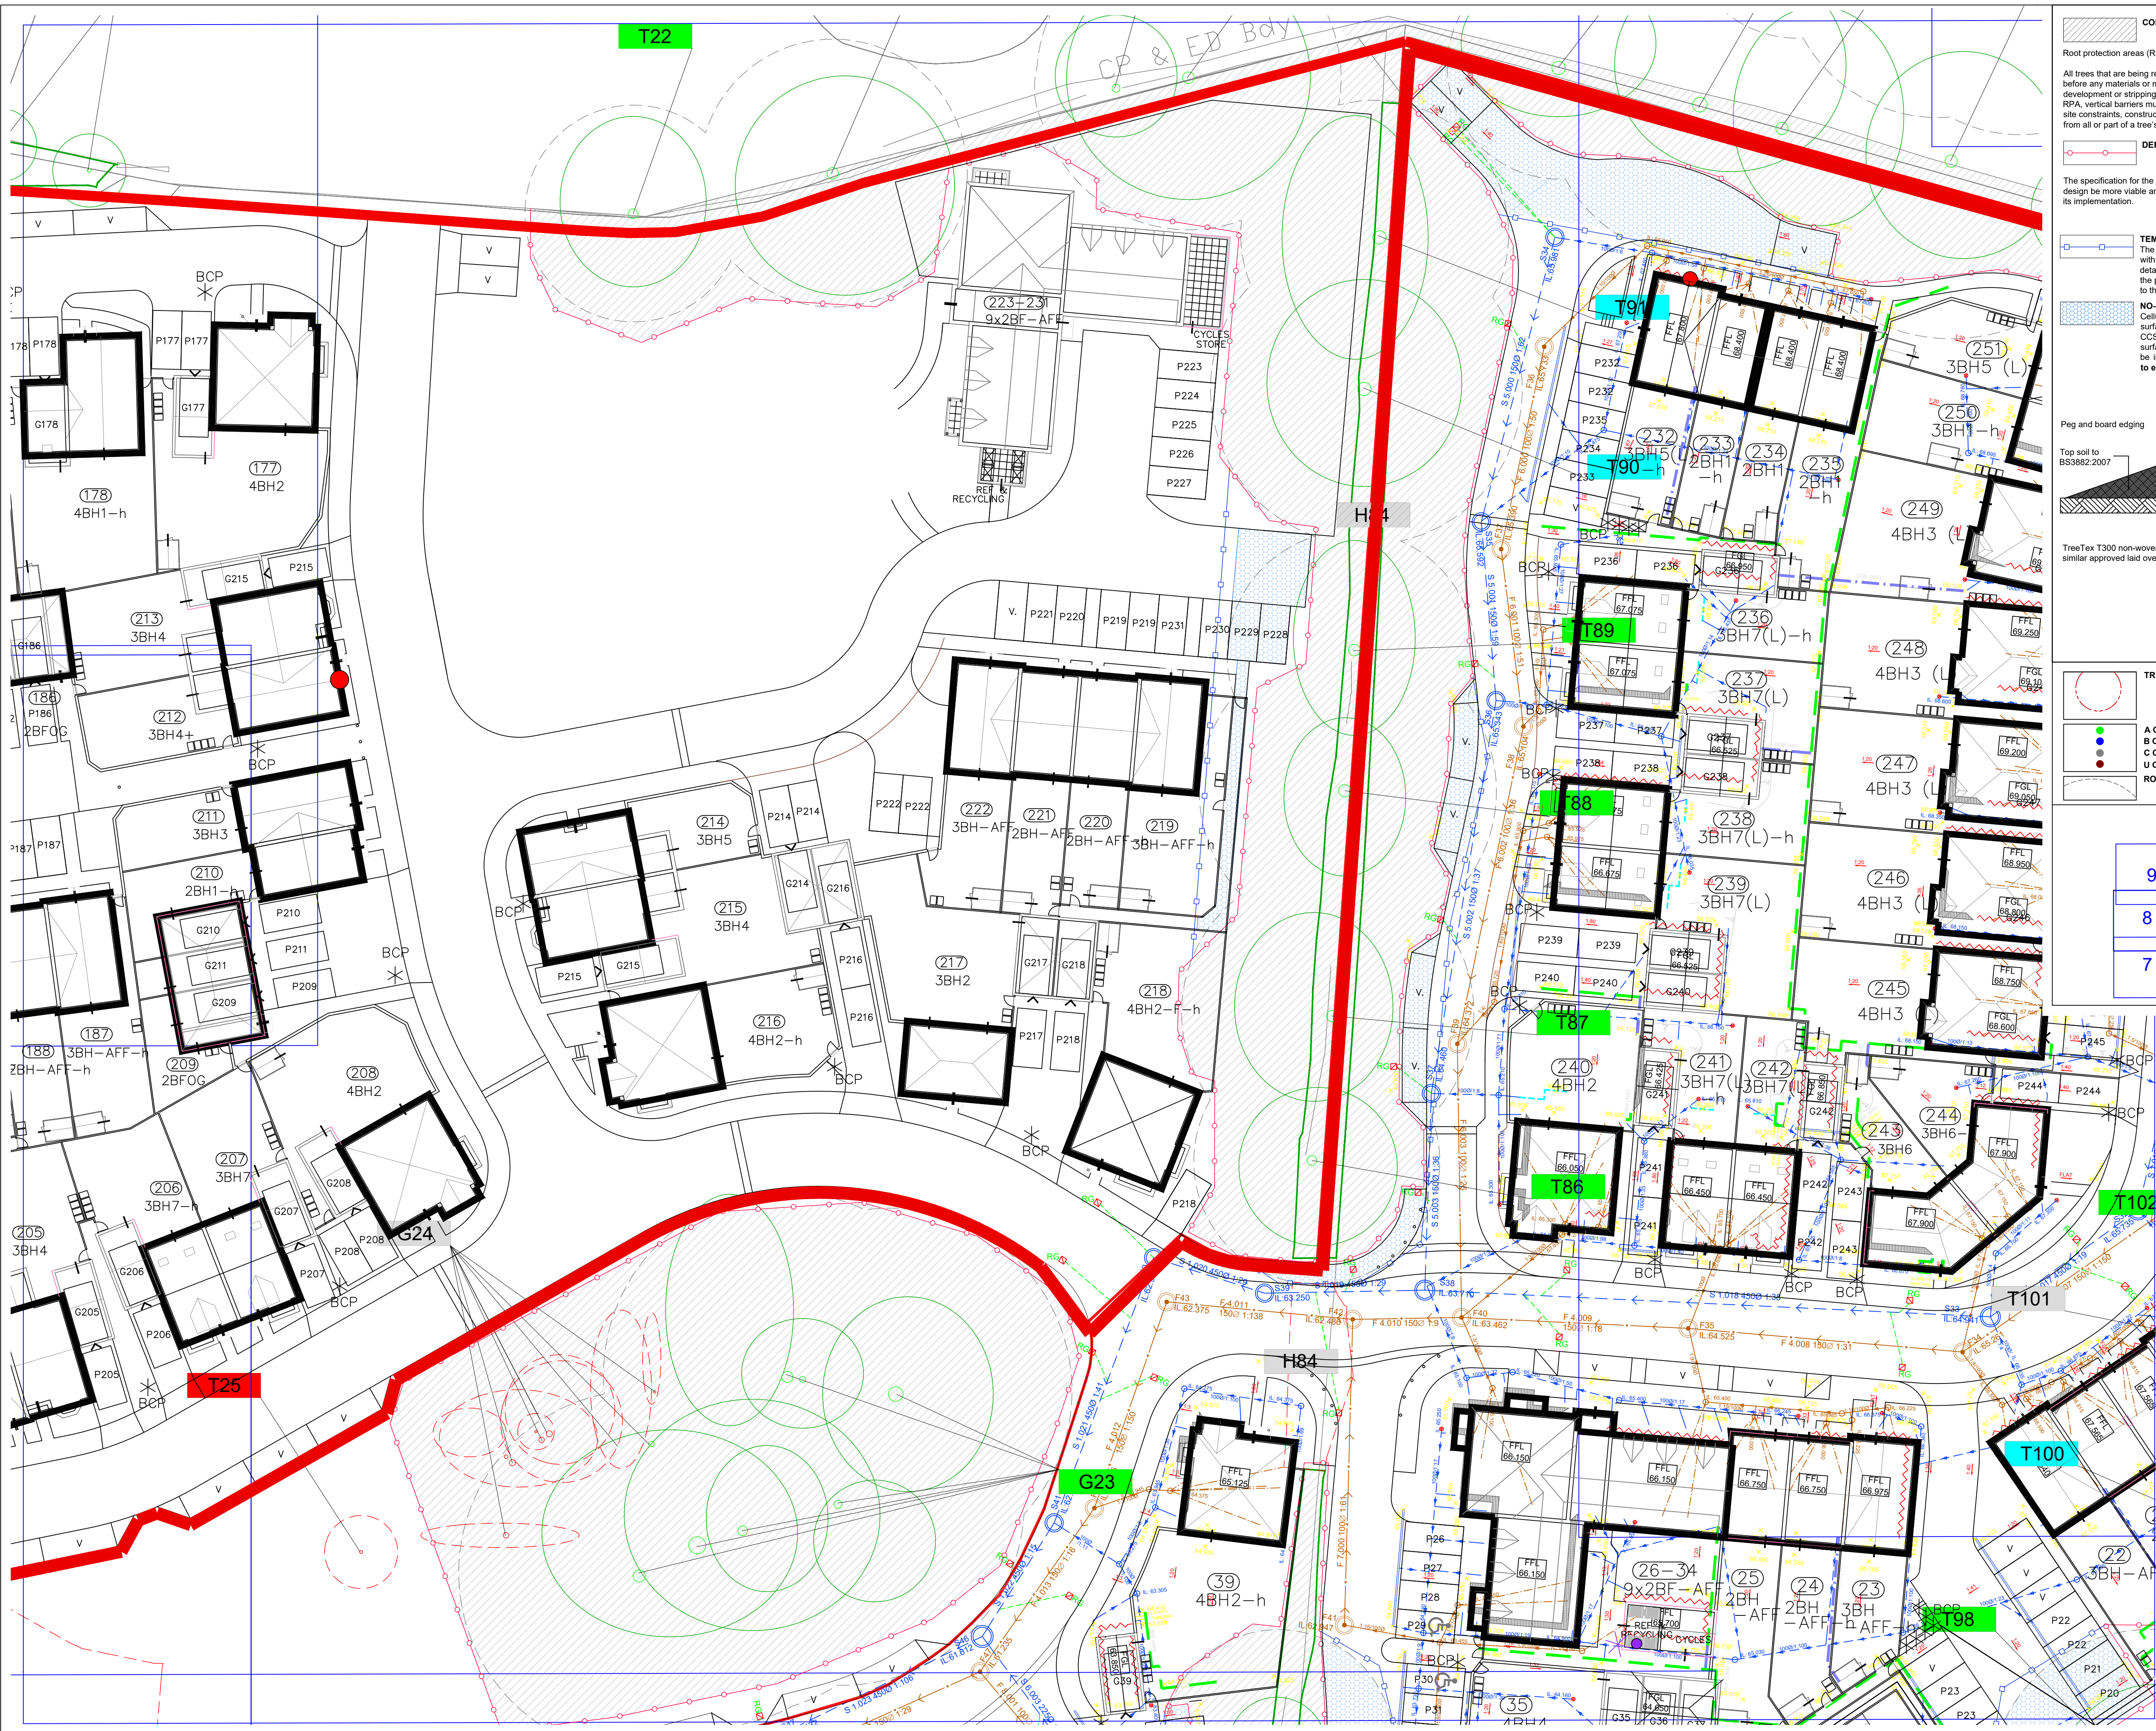

CONSTRUCTION EXCLUSION ZONE

Root protection areas (RPA) of retained trees within which all construction activity is restricted.

All trees that are being retained on site must be protected by barriers and/or ground protection before any materials or machinery are brought onto the site, and before any demolition, development or stripping of soil commences. Where all activity can be excluded from the RPA, vertical barriers must be erected to create a construction exclusion zone. Where, due to site constraints, construction activity cannot be fully or permanently excluded in this manner from all or part of a tree's RPA, appropriate ground protection can be installed.

DEFAULT POSITION FOR THE TREE PROTECTION BARRIERS.

The specification for the fencing can be found in the method statement. Should an alternative design be more viable and appropriate, it must be agreed with the project arboriculturist before its implementation.

TEMPORARY FENCING

The fencing is used to protect areas of special detail. It is to be installed with the main tree protection fence and is only to be removed when the detail is installed as per the method statement & under the supervision of the project arboriculturist. It shall be weld-mesh panels on posts, secured to the ground with road pins (or similar).

NO-DIG SURFACE

Cellular confinement system (CCS) to be used to create this area of hard surface, above the existing ground level. Topsoil to be retained. Depth of CCS to be 50-75mm for pedestrian surfaces and 100-200 for vehicular surfaces. Surface to be porous to approved details and specifications. To be installed under arboricultural supervision. **All specifications subject to engineering design.**

Cells to be filled with 20-40mm clean graded angular stone to manufacturers details and specifications

Peg and board edging

Top soil to BS3882:2007

Original ground level

Depressions and soft spots in formation to be filled with sharp sand to levels required

CCS/Cellular confinement system (Geosynthetics CellWeb or similar approved)

TREE TO BE REMOVED

A CATEGORY TREE
B CATEGORY TREE
C CATEGORY TREE
U CATEGORY TREE

ROOT PROTECTION AREA (RPA) FOR RETAINED TREES

The original of this drawing was produced in colour - a monochrome copy should not be relied upon.

D	12.06.2020	Revised parking by plot 119-112	RA
C	02.07.2019	Revised layout and drainage	TRG
B	03.06.19	Phase 2 tree protection extended	AJB
A	10.05.2019	No dig added T1 - 3	TRG
Rev	Date	Details	Drawn

ACD ENVIRONMENTAL

HEAD OFFICE
Rodbourne Rail Business Centre, Grange Lane,
Malmesbury, SN16 0ES
Tel: 01666 823544

Courtyard House, Mill Lane, Codrington, GU7 1EY
Tel: 01483 425774

Suite 6, Crescent House, Yonge Close, Eastleigh, SO50 9SX
Tel: 02382 026300

9 Brownlow Road, Cambridge, CB4 3NG
Tel: 07625 868654

Copyright of ACD. All rights described in Chapter IV of the Copyright, Designs and Patents Act 1988 have been generally assumed. 2015. Copyright of this plan remains with ACD until all fees have been paid in full.

Linden HOMES

scheme: Woodcroft Farm, Woodcroft Lane, Waterlooville
client: Linden Homes
drawing: Tree Protection Plan
date: March 2018
scale: 1:250@A1
dwg no: LIN21652-03D Sheet 3 of 9
drawn: RA checked: TRG

CONSTRUCTION EXCLUSION ZONE

Root protection areas (RPA) of retained trees within which all construction activity is restricted.

All trees that are being retained on site must be protected by barriers and/or ground protection before any materials or machinery are brought onto the site, and before any demolition, development or stripping of soil commences. Where all activity can be excluded from the RPA, vertical barriers must be erected to create a construction exclusion zone. Where, due to site constraints, construction activity cannot be fully or permanently excluded in this manner from all or part of a tree's RPA, appropriate ground protection can be installed.

DEFAULT POSITION FOR THE TREE PROTECTION BARRIERS.

The specification for the fencing can be found in the method statement. Should an alternative design be more viable and appropriate, it must be agreed with the project arboriculturist before its implementation.

TEMPORARY FENCING

The fencing is used to protect areas of special detail. It is to be installed with the main tree protection fence and is only to be removed when the detail is installed as per the method statement & under the supervision of the project arboriculturist. It shall be weld-mesh panels on posts, secured to the ground with road pins (or similar).

NO-DIG SURFACE

Cellular confinement system (CCS) to be used to create this area of hard surface, above the existing ground level. Topsoil to be retained. Depth of CCS to be 50/75mm for pedestrian surfaces and 100/200 for vehicular surfaces. Surface to be porous to approved details and specifications. To be installed under arboricultural supervision. **All specifications subject to engineering design.**

Cells to be filled with 20-40mm clean graded angular stone to manufacturers details and specifications

Peg and board edging

TreeTex T300 geotextile or similar laid over CellWeb

Porous surface to finish

Top soil to BS3882:2007

Original ground level


TreeTex T300 non-woven geotextile or similar approved laid over formation

Depressions and soft spots in formation to be filled with sharp sand to levels required

TREE TO BE REMOVED

A CATEGORY TREE
B CATEGORY TREE
C CATEGORY TREE
U CATEGORY TREE

ROOT PROTECTION AREA (RPA) FOR RETAINED TREES



The original of this drawing was produced in colour - a monochrome copy should not be relied upon.



D	12.06.2020	Revised parking by plot 119-112	RA
C	02.07.2019	Revised layout and drainage	TRG
B	03.06.19	Phase 2 tree protection extended	AJB
A	10.05.2019	No dig added T1 - 3	TRG
Rev	Date	Details	Drawn



HEAD OFFICE
Rodbourne Rail Business Centre, Grange Lane,
Malmesbury, SN16 0ES
Tel: 01666 825646

Courtyard House, Mill Lane, Codrington, GU7 1EY
Tel: 01483 425774

Suite 6, Crescent House, Yonge Close, Eastleigh, SO50 9SX
Tel: 02382 026300

9 Brownlow Road, Cambridge, CB4 3NG
Tel: 07625 868654

Copyright of ACD. All rights described in Chapter IV of the Copyright, Designs and Patents Act 1988 have been generally assigned. 2015. Copyright of this plan remains with ACD until all fees have been paid in full.



scheme: Woodcroft Farm, Woodcroft Lane, Waterlooville
client: Linden Homes
drawing: Tree Protection Plan
date: March 2018
scale: 1:250@A1
dwg no: LIN21652-03D Sheet 4 of 9
drawn: RA checked: TRG

CONSTRUCTION EXCLUSION ZONE

Root protection areas (RPA) of retained trees within which all construction activity is restricted.

All trees that are being retained on site must be protected by barriers and/or ground protection before any materials or machinery are brought onto the site, and before any demolition, development or stripping of soil commences. Where all activity can be excluded from the RPA, vertical barriers must be erected to create a construction exclusion zone. Where, due to site constraints, construction activity cannot be fully or permanently excluded in this manner from all or part of a tree's RPA, appropriate ground protection can be installed.

DEFAULT POSITION FOR THE TREE PROTECTION BARRIERS.

The specification for the fencing can be found in the method statement. Should an alternative design be more viable and appropriate, it must be agreed with the project arboriculturist before its implementation.

TEMPORARY FENCING

The fencing is used to protect areas of special detail. It is to be installed with the main tree protection fence and is only to be removed when the detail is installed as per the method statement & under the supervision of the project arboriculturist. It shall be weld-mesh panels on posts, secured to the ground with road pins (or similar).

NO-DIG SURFACE

Cellular confinement system (CCS) to be used to create this area of hard surface, above the existing ground level. Topsoil to be retained. Depth of CCS to be 50-75mm for pedestrian surfaces and 100-200 for vehicular surfaces. Surface to be porous to approved details and specifications. To be installed under arboricultural supervision. All specifications subject to engineering design.

Cells to be filled with 20-40mm clean graded angular stone to manufacturers details and specifications

TreeTex T300 geotextile or similar laid over CellWeb

Porous surface to finish

Peg and board edging

Top soil to BS3882:2007

Original ground level


Depressions and soft spots in formation to be filled with sharp sand to levels required

CCS/Cellular confinement system (Geosynthetics CellWeb or similar approved)

TREE TO BE REMOVED

A CATEGORY TREE
B CATEGORY TREE
C CATEGORY TREE
U CATEGORY TREE

ROOT PROTECTION AREA (RPA) FOR RETAINED TREES



The original of this drawing was produced in colour - a monochrome copy should not be relied upon.



D	12.06.2020	Revised parking by plot 119-112	RA
C	02.07.2019	Revised layout and drainage	TRG
B	03.06.19	Phase 2 tree protection extended	AJB
A	10.05.2019	No dig added T1 - 3	TRG
Rev	Date	Details	Drawn



HEAD OFFICE
Rodbourne Rail Business Centre, Grange Lane,
Malmesbury, SN16 0ES
Tel: 01666 823546

Courtyard House, Mill Lane, Codrington, GU7 1EY
Tel: 01483 425774

Suite 6, Crescent House, Yonge Close, Eastleigh, SO50 9SX
Tel: 02382 026300

9 Brownlow Road, Cambridge, CB4 3NG
Tel: 07625 868554

Copyright of ACD. All rights described in Chapter IV of the Copyright, Designs and Patents Act 1988 have been generally assumed. 2015. Copyright of this plan remains with ACD until all fees have been paid in full.



scheme: Woodcroft Farm, Woodcroft Lane, Waterlooville

client: Linden Homes


drawing: Tree Protection Plan

date: March 2018

scale: 1:250@A1

dwg no: LIN21652-03D Sheet 5 of 9

drawn: RA checked: TRG

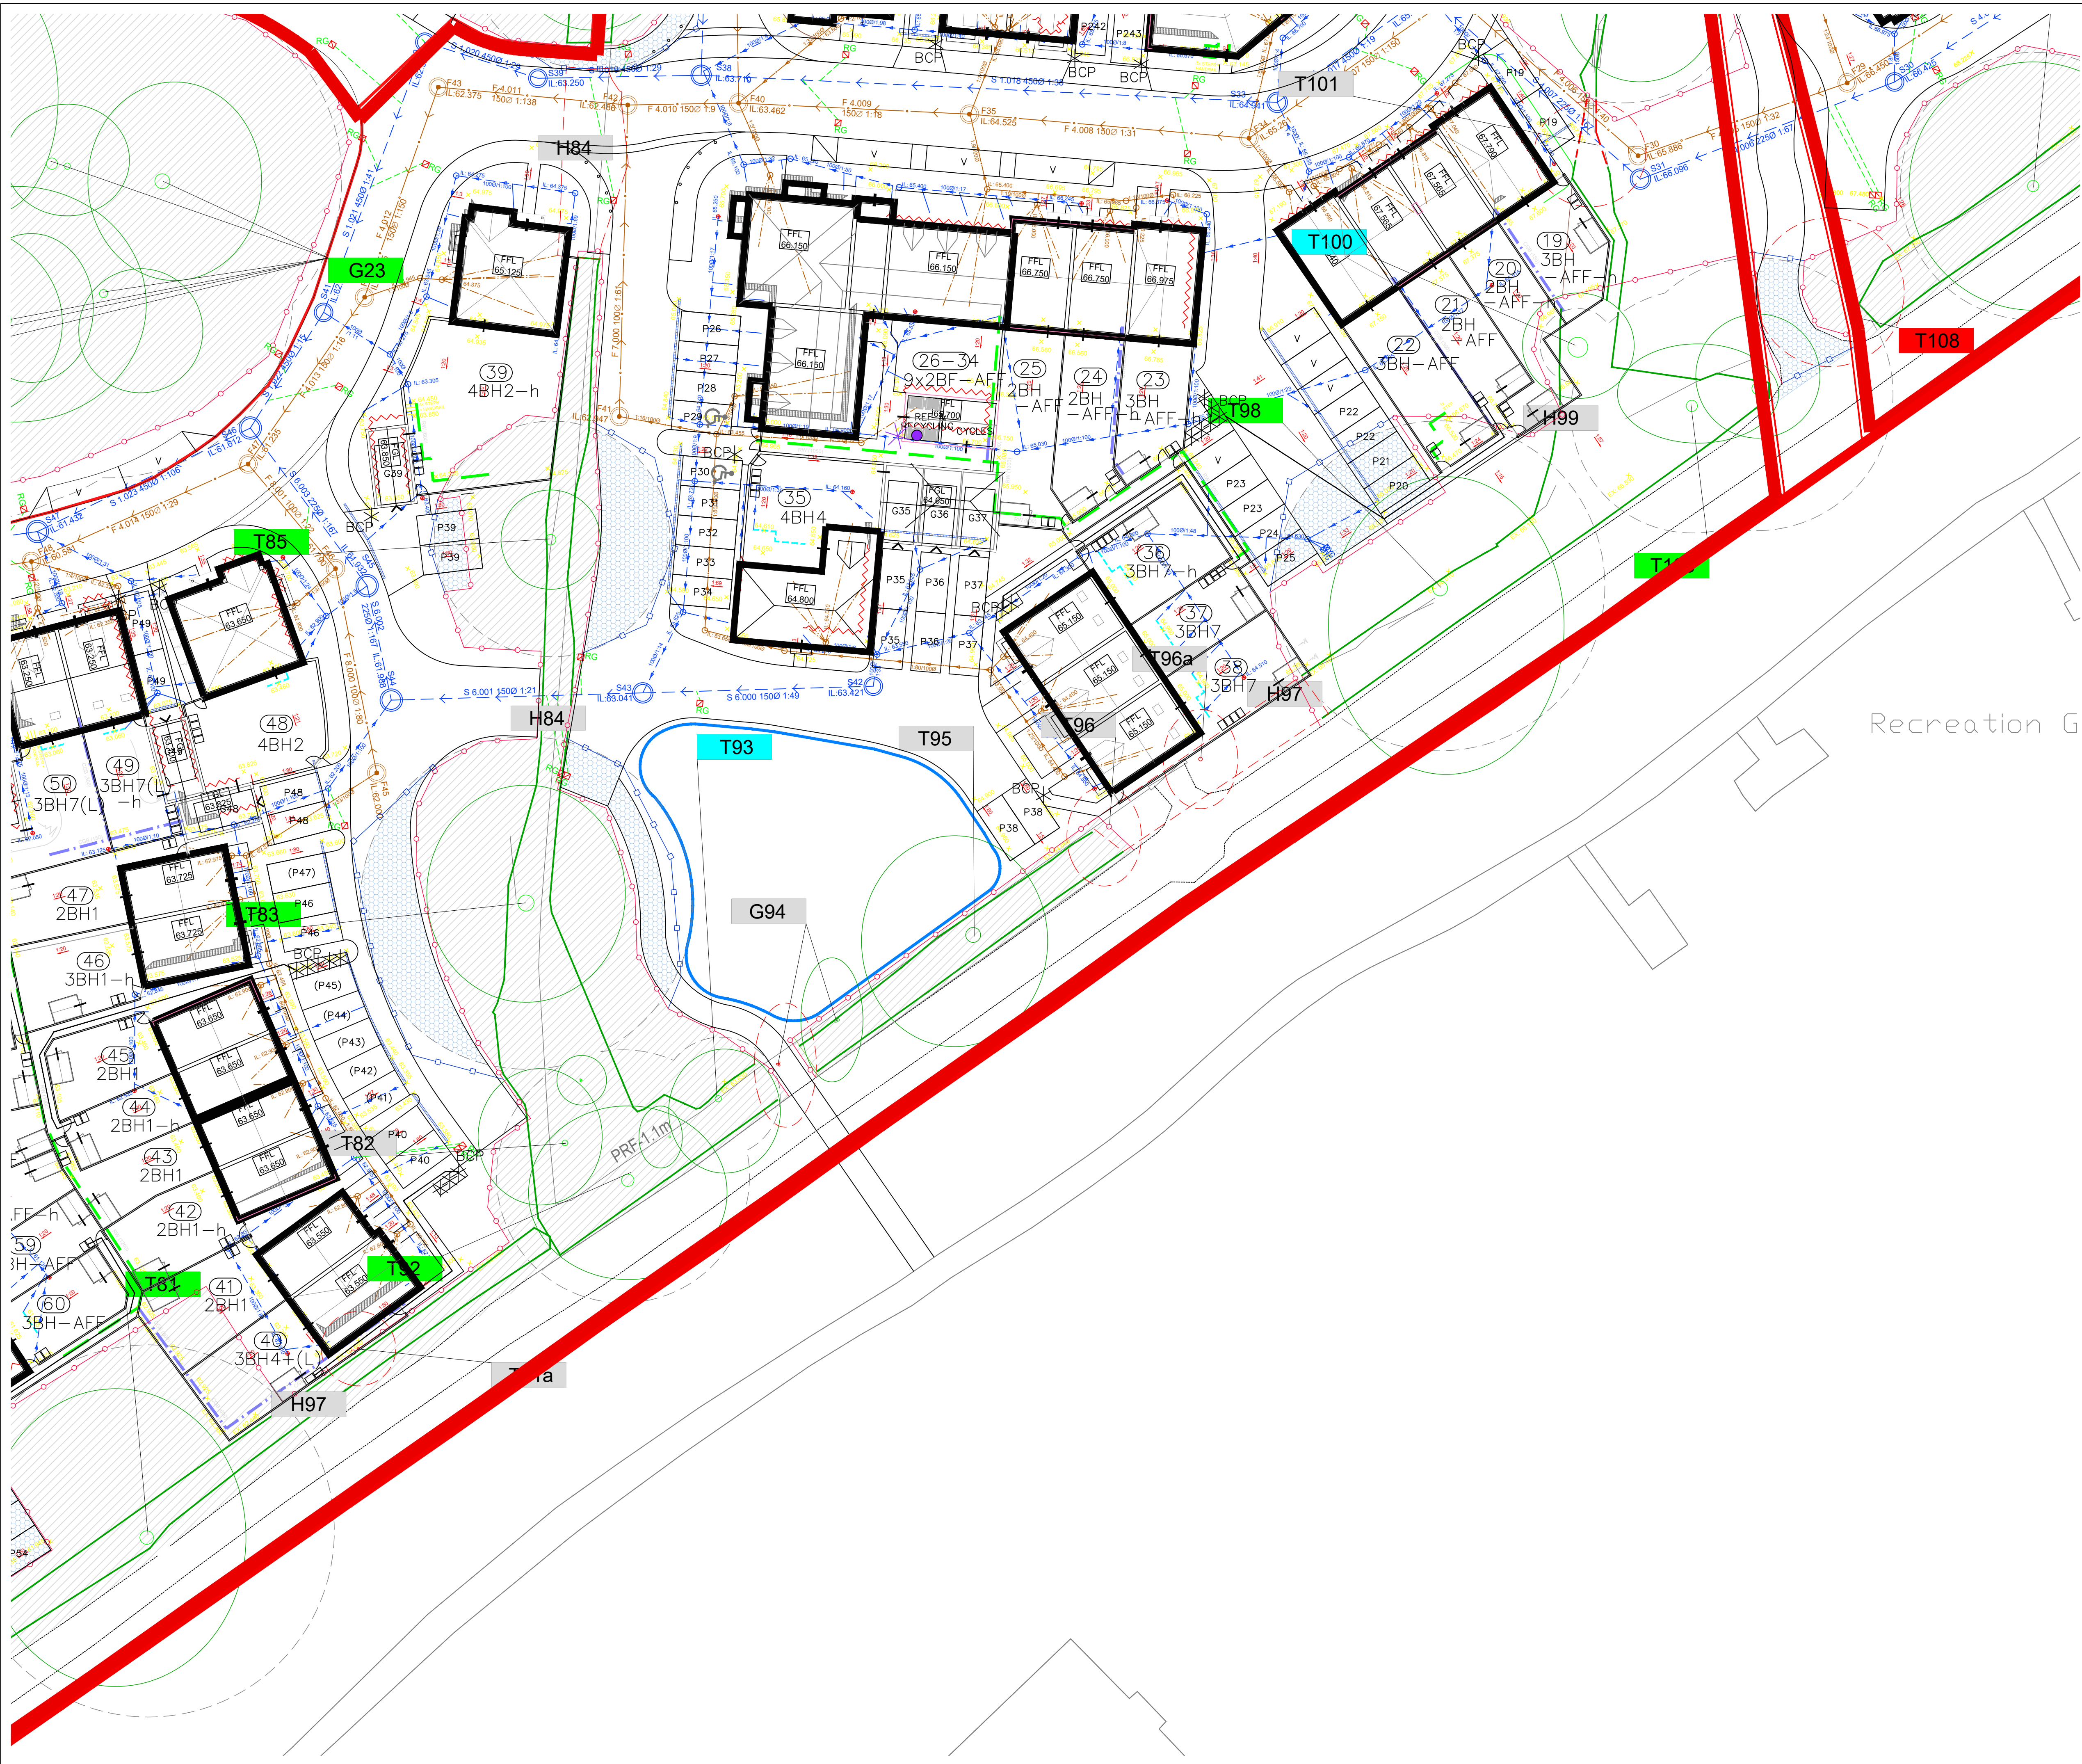

CONSTRUCTION EXCLUSION ZONE

Root protection areas (RPA) of retained trees within which all construction activity is restricted.

All trees that are being retained on site must be protected by barriers and/or ground protection before any materials or machinery are brought onto the site, and before any demolition, development or stripping of soil commences. Where all activity can be excluded from the RPA, vertical barriers must be erected to create a construction exclusion zone. Where, due to site constraints, construction activity cannot be fully or permanently excluded in this manner from all or part of a tree's RPA, appropriate ground protection can be installed.

DEFAULT POSITION FOR THE TREE PROTECTION BARRIERS.

The specification for the fencing can be found in the method statement. Should an alternative design be more viable and appropriate, it must be agreed with the project arboriculturist before its implementation.

TEMPORARY FENCING

The fencing is used to protect areas of special detail. It is to be installed with the main tree protection fence and is only to be removed when the detail is installed as per the method statement & under the supervision of the project arboriculturist. It shall be weld-mesh panels on posts, secured to the ground with road pins (or similar).

NO-DIG SURFACE

Cellular confinement system (CCS) to be used to create this area of hard surface, above the existing ground level. Topsoil to be retained. Depth of CCS to be 50-75mm for pedestrian surfaces and 100-200 for vehicular surfaces. Surface to be porous to approved details and specifications. To be installed under arboricultural supervision. **All specifications subject to engineering design.**

Cells to be filled with 20-40mm clean graded angular stone to manufacturers details and specifications

TREE TO BE REMOVED

A CATEGORY TREE

B CATEGORY TREE

C CATEGORY TREE

U CATEGORY TREE

ROOT PROTECTION AREA (RPA) FOR RETAINED TREES

The original of this drawing was produced in colour- a monochrome copy should not be relied upon.



D	12.06.2020	Revised parking by plot 119-112	RA
C	02.07.2019	Revised layout and drainage	TRG
B	03.06.19	Phase 2 tree protection extended	AJB
A	10.05.2019	No dig added T1 - 3	TRG
Rev	Date	Details	Drawn

ACD ENVIRONMENTAL

HEAD OFFICE
Rodbourne Rail Business Centre, Grange Lane,
Malmesbury, SN16 0ES
Tel: 01666 823546

Courtyard House, Mill Lane, Codrington, GU7 1EY
Tel: 01483 425774


Suite 6, Crescent House, Yonge Close, Eastleigh, SO50 9SX
Tel: 02382 026300

9 Brownlow Road, Cambridge, CB4 3NG
Tel: 07625 868554

Copyright of ACD. All rights described in Chapter IV of the Copyright, Designs and Patents Act 1988 have been generally asserted. 2015. Copyright of this plan remains with ACD until all fees have been paid in full.

Linden HOMES

scheme: Woodcroft Farm, Woodcroft Lane, Waterloooville
client: Linden Homes
drawing: Tree Protection Plan
date: March 2018
scale: 1:250@A1
dwg no: LIN21652-03D Sheet 6 of 9
drawn: RA checked: TRG

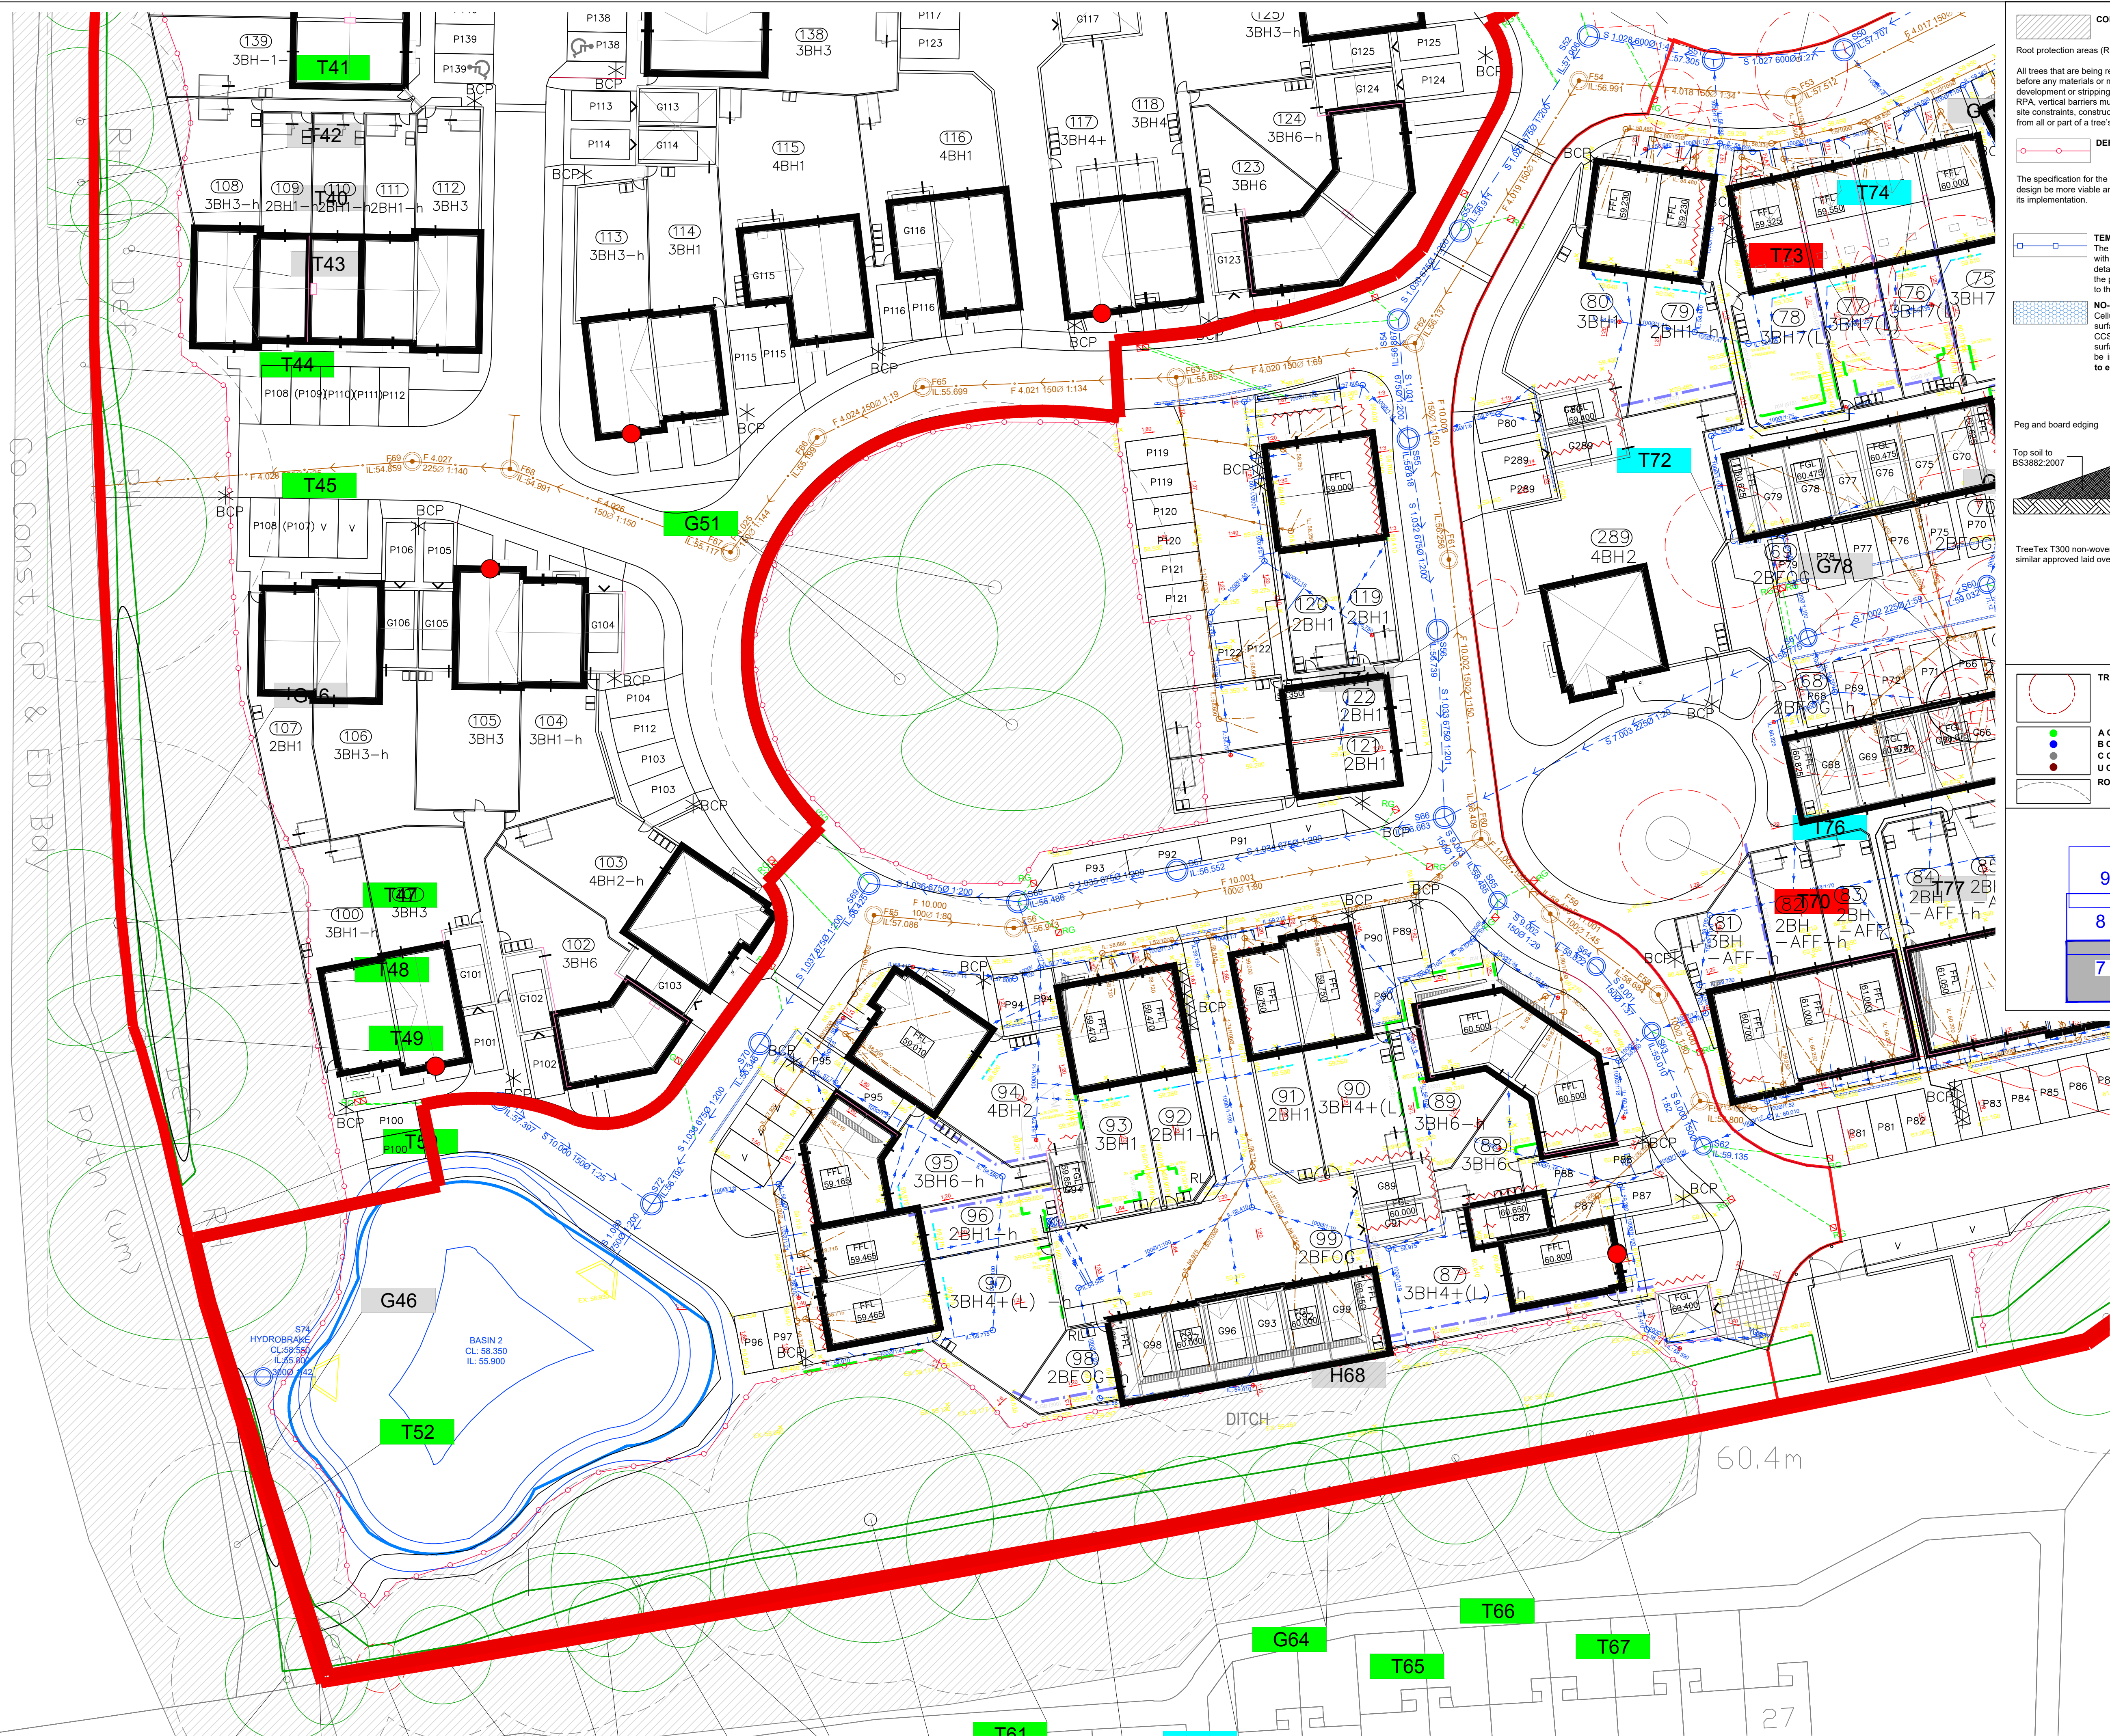

CONSTRUCTION EXCLUSION ZONE

Root protection areas (RPA) of retained trees within which all construction activity is restricted.

All trees that are being retained on site must be protected by barriers and/or ground protection before any materials or machinery are brought onto the site, and before any demolition, development or stripping of soil commences. Where all activity can be excluded from the RPA, vertical barriers must be erected to create a construction exclusion zone. Where, due to site constraints, construction activity cannot be fully or permanently excluded in this manner from all or part of a tree's RPA, appropriate ground protection can be installed.

DEFAULT POSITION FOR THE TREE PROTECTION BARRIERS.

The specification for the fencing can be found in the method statement. Should an alternative design be more viable and appropriate, it must be agreed with the project arboriculturist before its implementation.

TEMPORARY FENCING

The fencing is used to protect areas of special detail. It is to be installed with the main tree protection fence and is only to be removed when the detail is installed as per the method statement & under the supervision of the project arboriculturist. It shall be weld-mesh panels on posts, secured to the ground with road pins (or similar).

NO-DIG SURFACE

Cellular confinement system (CCS) to be used to create this area of hard surface, above the existing ground level. Topsoil to be retained. Depth of CCS to be 50-75mm for pedestrian surfaces and 100-200 for vehicular surfaces. Surface to be porous to approved details and specifications. To be installed under arboricultural supervision. All specifications subject to engineering design.

Cells to be filled with 20-40mm clean graded angular stone to manufacturers details and specifications

Peg and board edging

TreeTex T300 geotextile or similar laid over CellWeb

Porous surface to finish

Top soil to BS3882:2007

Original ground level

Depressions and soft spots in formation to be filled with sharp sand to levels required

CCS/Cellular confinement system (Geosynthetics CellWeb or similar approved)


TREE TO BE REMOVED

A CATEGORY TREE
B CATEGORY TREE
C CATEGORY TREE
U CATEGORY TREE

ROOT PROTECTION AREA (RPA) FOR RETAINED TREES

1 2
9 3 4
8 5 6
7

The original of this drawing was produced in colour - a monochrome copy should not be relied upon.



D	12.06.2020	Revised parking by plot 119-112	RA
C	02.07.2019	Revised layout and drainage	TRG
B	03.06.19	Phase 2 tree protection extended	AJB
A	10.05.2019	No dig added T1 - 3	TRG
Rev	Date	Details	Drawn



HEAD OFFICE
Rodbourne Rail Business Centre, Grange Lane,
Malmesbury, SN16 0ES
Tel: 01666 823540

Courtyard House, Mill Lane, Codrington, GU7 1EY
Tel: 01483 425774


Suite 6, Crescent House, Yonge Close, Eastleigh, SO50 9SX
Tel: 02382 028300

9 Brownlow Road, Cambridge, CB4 3NG
Tel: 07625 868554

Copyright of ACD. All rights described in Chapter IV of the Copyright, Designs and Patents Act 1988 have been generally assigned. 2015. Copyright of this plan remains with ACD until all fees have been paid in full.



scheme: Woodcroft Farm, Woodcroft Lane, Waterlooville
client: Linden Homes
drawing: Tree Protection Plan
date: March 2018
scale: 1:250@A1
dwg no: LIN21652-03D Sheet 7 of 9
drawn: RA checked: TRG



D	12.06.2020	Revised parking by plot 119-112	RA
C	02.07.2019	Revised layout and drainage	TRG
B	03.06.19	Phase 2 tree protection extended	AJB
A	10.05.2019	No dig added T1 - 3	TRG
Rev	Date	Details	Drawn



HEAD OFFICE
Rodbourne Rail Business Centre, Grange Lane,
Malmesbury, SN16 0ES
Tel: 01666 825646

Courtyard House, Mill Lane, Godalming, GU7 1EY
Tel: 01483 425714

Suite 6, Crescent House, Yonge Close, Eastleigh, SO50 9SX
Tel: 02382 026300

9 Brownlow Road, Cambridge, CB4 3NC
Tel: 07825 868654

Copyright of ACD. All rights described in Chapter IV of the Copyright, Designs and Patents Act 1988 have been generally asserted: 2015. Copyright of this plan remains with ACD until all fees have been paid in full.



scheme: Woodcroft Farm, Woodcroft
Lane, Waterloooville
client: Linden Homes
drawing: Tree Protection Plan
date: March 2018
scale: 1:250@A1
dwg no: LIN21652-03D Sheet 8 of 9
drawn: RA checked: TRG

CONSTRUCTION EXCLUSION ZONE

Root protection areas (RPA) of retained trees within which all construction activity is restricted.

All trees that are being retained on site must be protected by barriers and/or ground protection before any materials or machinery are brought onto the site, and before any demolition, development or stripping of soil commences. Where all activity can be excluded from the RPA, vertical barriers must be erected to create a construction exclusion zone. Where, due to site constraints, construction activity cannot be fully or permanently excluded in this manner from all or part of a tree's RPA, appropriate ground protection can be installed.

DEFAULT POSITION FOR THE TREE PROTECTION BARRIERS.

The specification for the fencing can be found in the method statement. Should an alternative design be more viable and appropriate, it must be agreed with the project arboriculturist before its implementation.

TEMPORARY FENCING

The fencing is used to protect areas of special detail. It is to be installed with the main tree protection fence and is only to be removed when the detail is installed as per the method statement & under the supervision of the project arboriculturist. It shall be weld-mesh panels on posts, secured to the ground with road pins (or similar).

NO-DIG SURFACE

Cellular confinement system (CCS) to be used to create this area of hard surface, above the existing ground level. Topsoil to be retained. Depth of CCS to be 50-75mm for pedestrian surfaces and 100-200 for vehicular surfaces. Surface to be porous to approved details and specifications. To be installed under arboricultural supervision. All specifications subject to engineering design.

Cells to be filled with 20-40mm clean graded angular stone to manufacturers details and specifications

Peg and board edging

TreeTex T300 geotextile or similar laid over CellWeb

Porous surface to finish

Top soil to BS3882:2007

Original ground level

Depressions and soft spots in formation to be filled with sharp sand to levels required

TreeTex T300 non-woven geotextile or similar approved laid over formation

CCS/Cellular confinement system (Geosynthetics CellWeb or similar approved)

TREE TO BE REMOVED

A CATEGORY TREE

B CATEGORY TREE

C CATEGORY TREE

U CATEGORY TREE

ROOT PROTECTION AREA (RPA) FOR RETAINED TREES

0 1 2 3 4 5 6m

The original of this drawing was produced in colour- a monochrome copy should not be relied upon.

D	12.06.2020	Revised parking by plot 119-112	RA
C	02.07.2019	Revised layout and drainage	TRG
B	03.06.19	Phase 2 tree protection extended	AJB
A	10.05.2019	No dig added T1 - 3	TRG
Rev	Date	Details	Drawn

HEAD OFFICE
Rodbourne Rail Business Centre, Grange Lane,
Malmesbury, SN16 0ES
Tel: 01666 823544

Courtyard House, Mill Lane, Codrington, GU7 1EY
Tel: 01483 425774

Suite 6, Crescent House, Yonge Close, Eastleigh, SO50 9SX
Tel: 02382 026300

9 Brownlow Road, Cambridge, CB4 3NG
Tel: 07625 868554

Copyright of ACD. All rights described in Chapter IV of the Copyright, Designs and Patents Act 1988 have been generally asserted. 2015. Copyright of this plan remains with ACD until all fees have been paid in full.

scheme: Woodcroft Farm, Woodcroft Lane, Waterlooville
client: Linden Homes
drawing: Tree Protection Plan
date: March 2018
scale: 1:250@A1
dwg no: LIN21652-03D Sheet 9 of 9
drawn: RA checked: TRG
