

Tree schedule				
Tree No	Species	Category	RPA Radius	Tree Works
All retained trees & hedges				
Carry out safety check and lift over site to 3-4m as necessary.				
T1	Hawthorn	C	4.8	Fell - Phase 1
G2	Pine, hazel, birch, ash, maple	C	3.6	-
G3	Oak	B	5.4	-
G4	Oak, ash	C	3.6	-
T5	Ash	B	9.6	-
G6	Hazel, cherry, goat willow	C	3.6	-
T7	Oak	U	5.4	Advisory - Fell for management
T8	Ash	U	15.0	Advisory - Fell for management
T9	Ash	U	6.6	Advisory - Fell for management
T10	Oak	A	9.6	-
T11	Oak	B	10.8	-
G12	Hawthorn	C	3.6	-
T13	Ash	A	9.0	-
T14	Ash	C	4.8	-
T15	Ash	B	12.0	-
T16	Ash	U	7.2	-
G17	Hawthorn, ash, oak	C	4.8	-
G18	Bramble, ash, hawthorn	C	2.4	-
G19	Oak, ash, hawthorn, goat willow	C	3.6	-
G20	Goat willow	C	3.6	-
T21	Lombardy poplar	B	9.0	-
T22	Lombardy poplar	B	7.2	-
T23	Oak	B	10.8	-
T24	Sycamore	C	3.6	-
T25	Scots pine	B	7.2	-
T26	Oak	A	9.3	-
T27	Oak	A	12.9	-
G28	Oak	A	11.4	-
T29	Ash	A	9.6	-
G30	Goat willow	C	6.0	-
T31	Oak	A	8.4	-
T32	Oak	A	8.4	-
T33	Oak	A	9.6	-
T34	Oak	A	10.8	-
T35	Ash	B	7.8	-
G36	Oak	B	7.2	-
H37	Hawthorn, blackthorn	C	3.0	-
T38	Oak	U	9.6	Advisory - Fell for management
G39	Goat willow	C	4.8	-
T40	Oak	A	10.2	-
T41	Oak	A	5.4	-
H42	Hawthorn, field maple, hazel	C	3.6	-
T43	Field maple	B	5.4	-
T44	Oak	B	5.4	-
T45	Oak	A	13.2	-
H46	Hazel, blackthorn, hawthorn, ash	C	2.4	-
T47	Oak	B	7.2	-
T48	Ash	C	9.6	-
T49	Oak	B	7.8	-
T50	Oak	A	11.4	-
T51	Oak	B	9.0	-
T52	Field maple	A	7.8	-
T53	Oak	A	9.0	-
T54	Oak	A	12.0	-
G55	Oak	A	10.5	-
T56	Oak	A	9.6	-
G57	Ash, hazel, goat willow	C	3.6	Fell part - Future phase
T58	Ash	U	10.8	Advisory - Fell for management
T59	Ash	B	9.6	-
T60	Oak	A	7.2	-
T61	Field maple	B	8.4	-
T62	Oak	B	8.4	-
G63	Ash, aspen, oak	B	7.2	-
T64	Oak	A	7.2	-
T65	Oak	B	5.4	-
T66	Oak	A	10.8	-
G67	Oak	B	4.8	-
G68	Cypress, elder, scrub	C	3.6	-
G69	White poplar	B	5.4	-
G70	Oak, ash	C	3.6	-
T71	Goat willow	C	9.3	-
T72	Poplar	C	9.6	-
G73	Ash, cypress	C	4.8	-
T74	White poplar	B	8.4	-
T75	Turkey oak	B	3.0	-
H76	Hawthorn, blackthorn, white poplar	C	2.4	-
T77	Cypress	C	3.6	-
G78	Hawthorn, hazel	C	3.6	Fell - Future phase
G79	White poplar	C	3.0	-
G80	Alder	C	3.6	Fell - Future phase
H81	Field maple, hawthorn, blackthorn	C	2.4	Fell - Future phase

- BS category A

Trees of high quality
- BS category B

Trees of moderate quality
- BS category C


Trees of low quality
- BS category U

Trees unsuitable for retention
- Trees to be removed
- Proposed layout - Phase 1
- Proposed layout - Outline
- Estimated tree positions not included on original land survey and/or adjusted crown spreads
- Protective barrier/fencing
- Construction exclusion zone (CEZ)
- Root protection area (RPA) boundaries for category A and B trees
- Root protection area (RPA) boundaries for category C trees

Tree protection plan
Location of trees, categorisation & protection/management proposals for land at College Road, Campdown, Purbrook, Portsmouth

Barrell Plan Ref: 18072-BT2

Provided Plan Refs: 340CD01.dwg, 340CD01.dwg, 536 A-02-007-LU & 536 A-02-003-AM

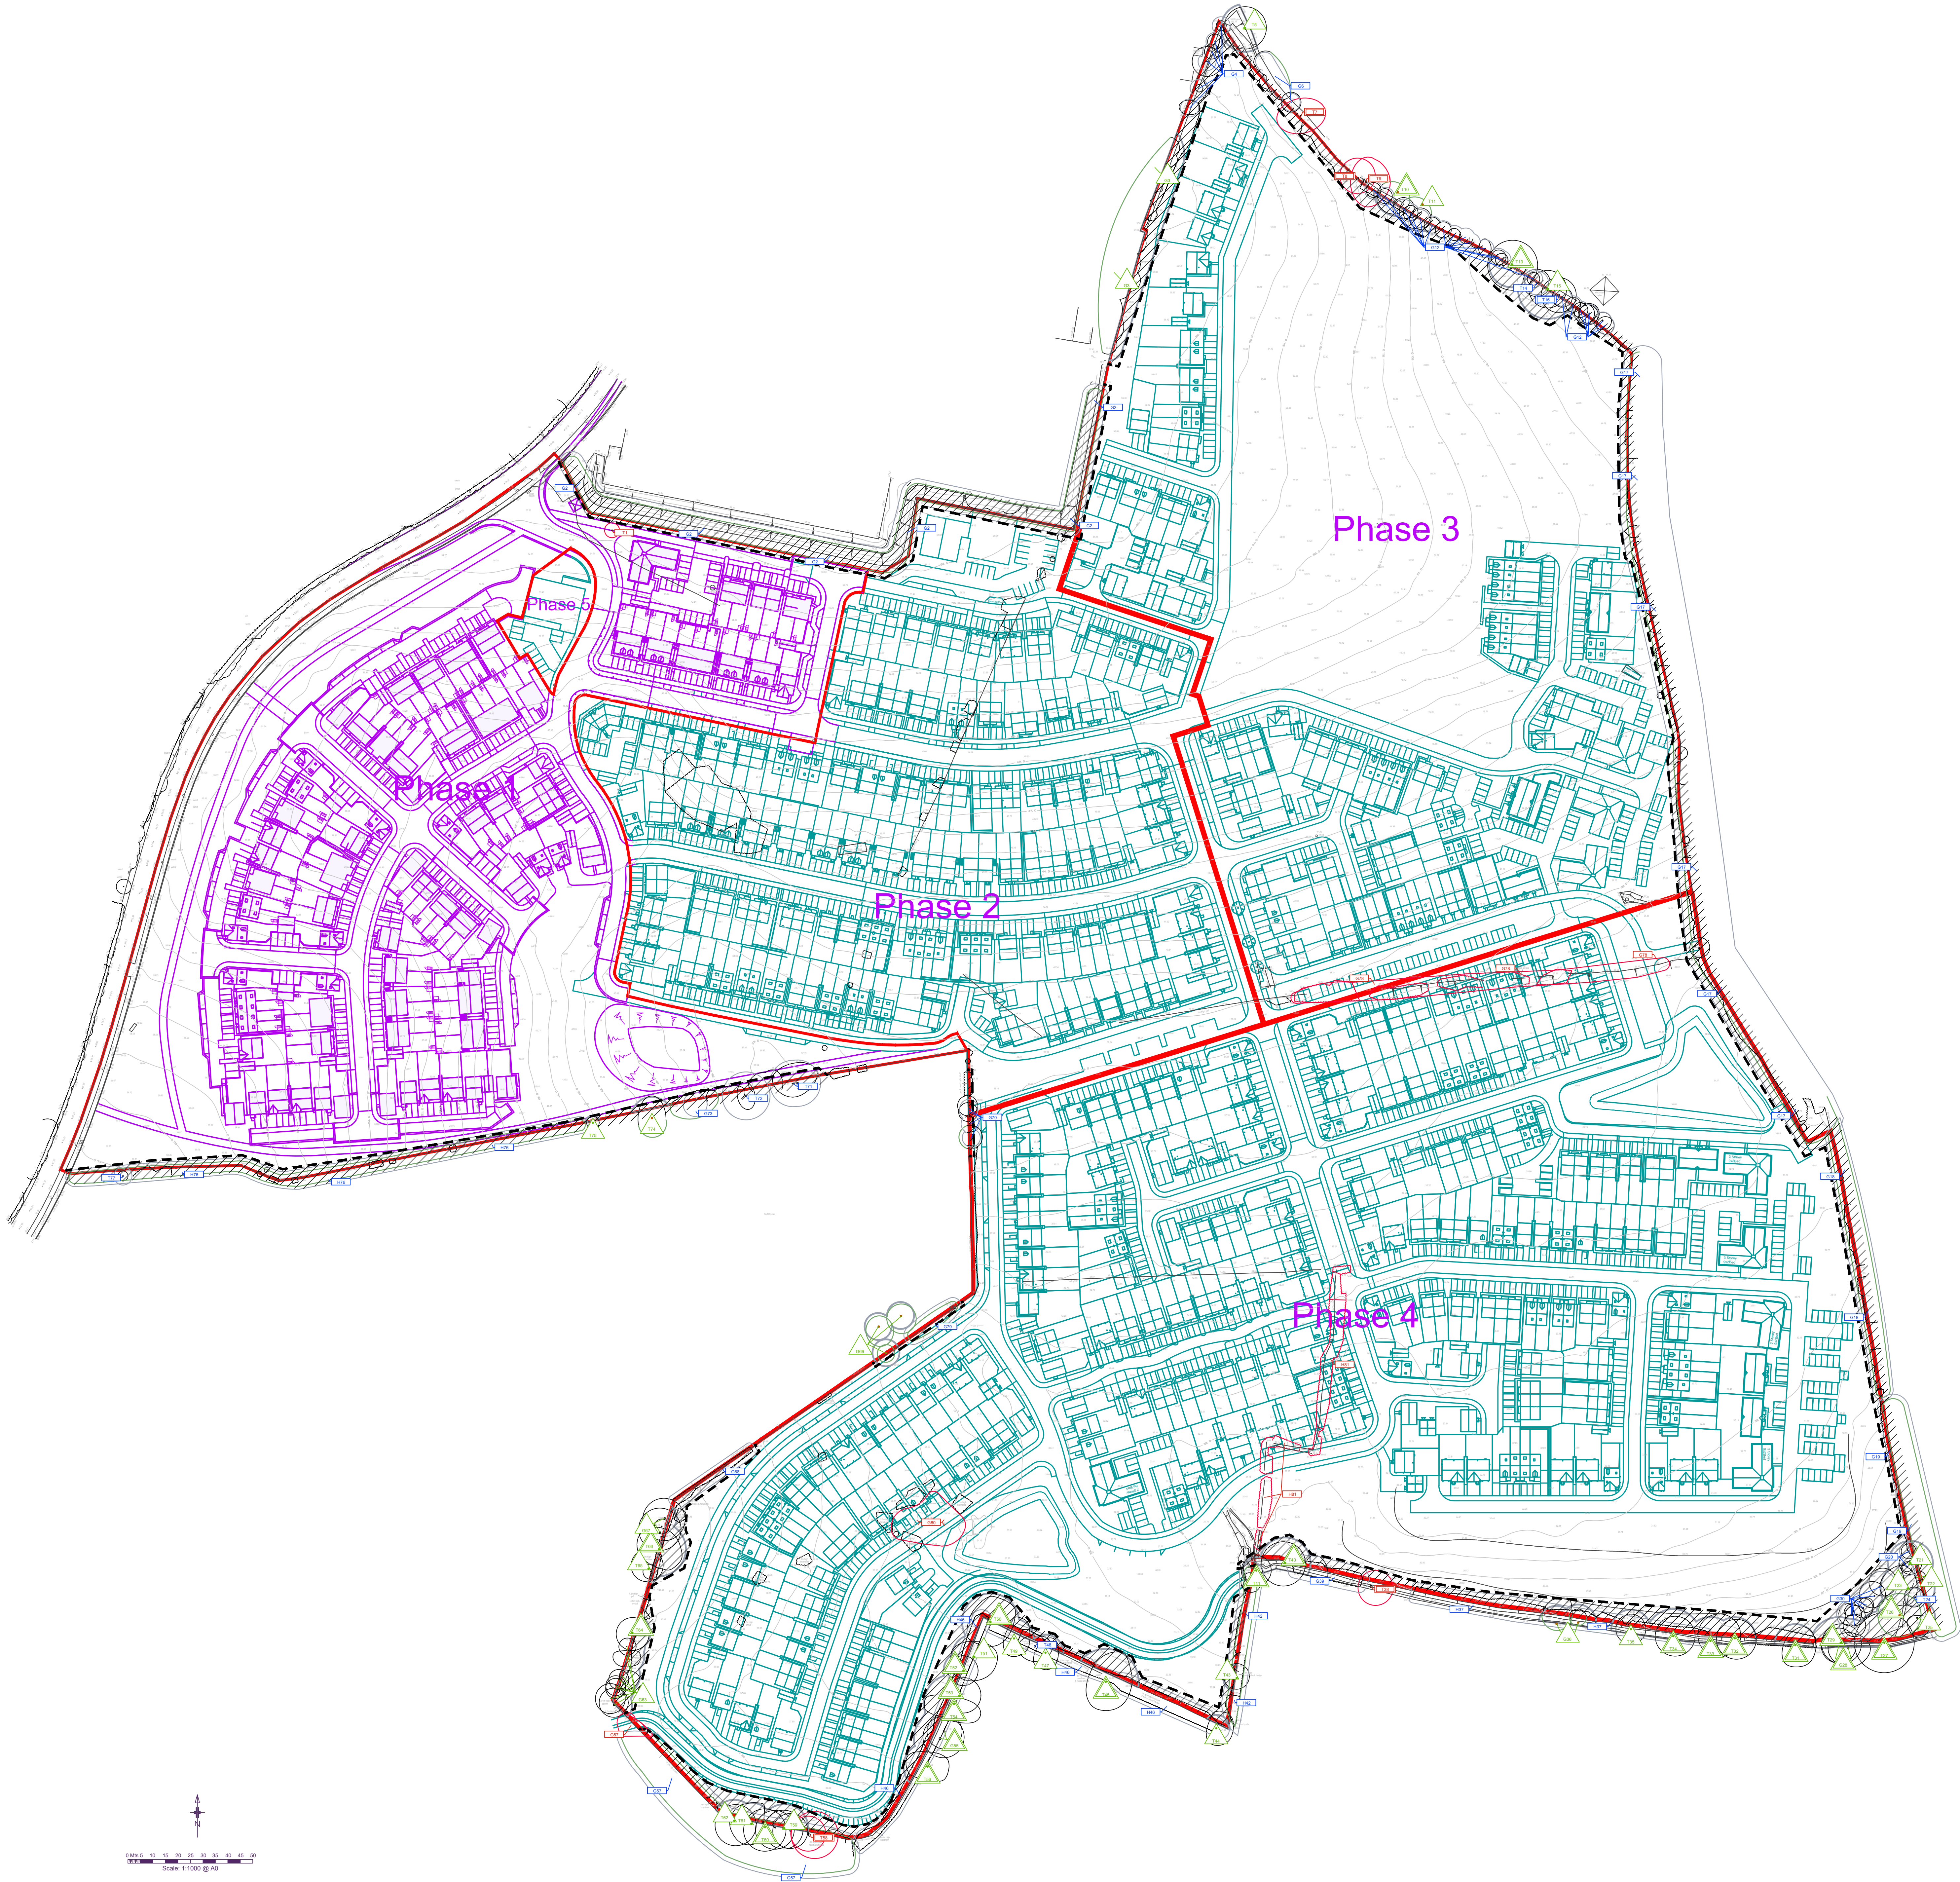

SGN 1 Monitoring tree protection



- Always:**
- have a pre-commencement meeting with the tree consultant before development starts
 - use the tree consultant to regularly check that protection remains fit for purpose
 - use the tree consultant to supervise work in RPAs
 - keep a written record of supervision



SGN 2 Fencing protected trees



- Always:**
- install protection before development starts
 - make sure protection is fit for purpose, i.e. it prevents damage to trees and soil
 - keep protection in place until there is no risk to trees
 - get written permission to move or remove any protection



SGN 4 Pollution control



- Always:**
- keep toxic products away from RPAs



SGN 5 Site cranes & piling rigs



- Always:**
- use the tree consultant to supervise work with cranes and piling rigs in RPAs



SGN 9 Installing/upgrading surfacing in RPAs




- Always:**
- use the tree consultant to supervise work in RPAs
 - minimise damage to roots and disturbance to soil in RPAs
 - minimise excavation when installing or upgrading surfacing in RPAs



SGN 11 Installing services in RPAs



- Always:**
- use the tree consultant to supervise work in RPAs
 - select the least damaging option when installing services, so prioritise trenchless, over broken trench over continuous trench
 - hand-dig trenches if trenchless is not feasible

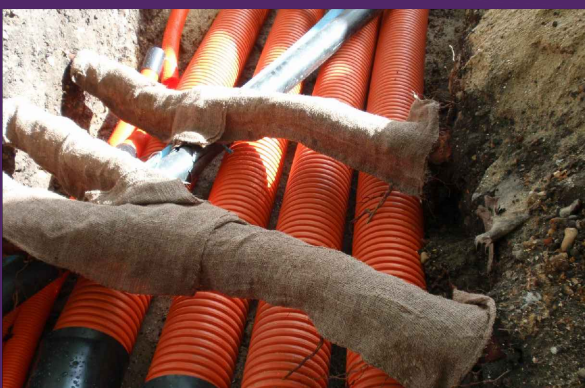

SGN 12 Landscaping in RPAs



- Always:**
- use the tree consultant to supervise work in RPAs
 - avoid raising ground levels within 1m of the trunks of retained trees



How to use plan

More detailed guidance on each Site Guidance Note (SGN) can be found in a printed hard copy compilation of all the SGNs, issued to the Site Manager at the pre-commencement site meeting. **(Note:** This should be retained on site throughout the duration of works). Additionally, an electronic pdf compilation of all the SGNs, was submitted with this drawing to the local planning authority and the client. Alternatively, a pdf of each SGN can be downloaded by:

- clicking the image links in the electronic pdf version of this plan;
- holding a mobile phone QR (Quick Response) code reader over the QR code in the paper version of this plan; or,
- visiting our website at <https://www.barrelltreecare.co.uk/resources/technical-guidance>
