




Contract: Harts Farm Way, Havant		Client: Upton McGougan		Trial Pit: TP22	
Contract Ref: 727927	Start: 18.06.13 End: 18.06.13	Ground Level ---	Co-ordinates: ---	Sheet: 1 of 1	

Samples and In-situ Tests				Water	Backfill	Description of Strata	Depth (Thick ness)	Material Graphic Legend
Depth	No	Type	Results					
0.00-0.50	1	B				MADE GROUND: Dark brown and white clayey very sandy subangular to subrounded fine to coarse GRAVEL of tarmac, chalk, brick and concrete. Wood fragments noted. Occasional rootlets.		
0.40 0.50	2	PID ES	0.0ppm				(0.80)	
0.80-1.30 0.80 0.90 1.00	4 3	B PID ES PID	0.0ppm 0.0ppm 0.0ppm				0.80 (0.50)	
1.30-1.80	6	B					1.30	
1.50 1.50	5	ES PID	0.0ppm			Light grey very silty sandy angular to subangular fine to coarse GRAVEL of flint and chert. Sand is fine to coarse. Low cobble content of flint. (HEAD GRAVEL)	(1.50)	
2.00		PID	0.0ppm					
2.80-3.30 2.80	7	B PID	0.0ppm			Orangish yellow silty sandy angular to subangular fine to coarse GRAVEL of flint and chert. Medium cobble content of flint. (HEAD GRAVEL)	2.80	
3.00	8	W					(1.00)	
						Trial pit terminated at 3.80m depth.	3.80	

Plan (Not to Scale)	General Remarks
---------------------	-----------------

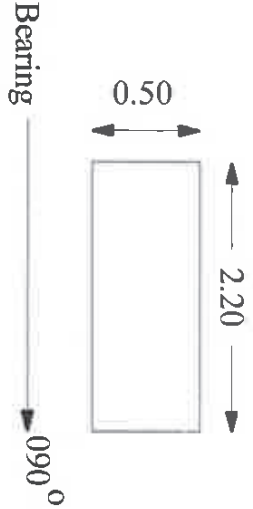

1. Pit collapse at 1.80m depth whilst being terminated at 3.20m depth.
2. Groundwater strike at 3.10m depth.
3. Backfilled with arisings on completion.

Method Used: Machine dug	Plant Used: JCB-3CX	Logged By: APope	Checked By: VS	Scale: 1:25	
---------------------------------	----------------------------	-------------------------	-----------------------	--------------------	--
