
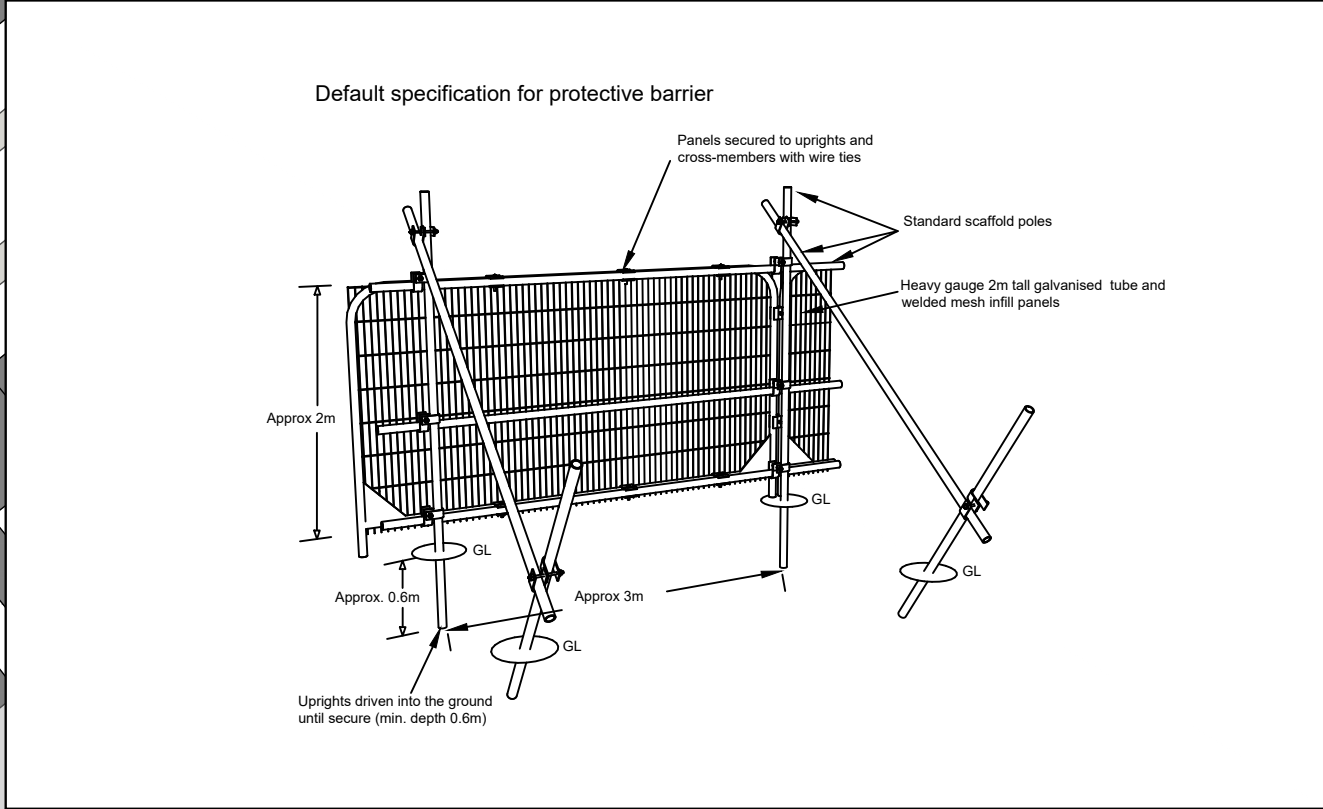


TREE PROTECTION PLAN

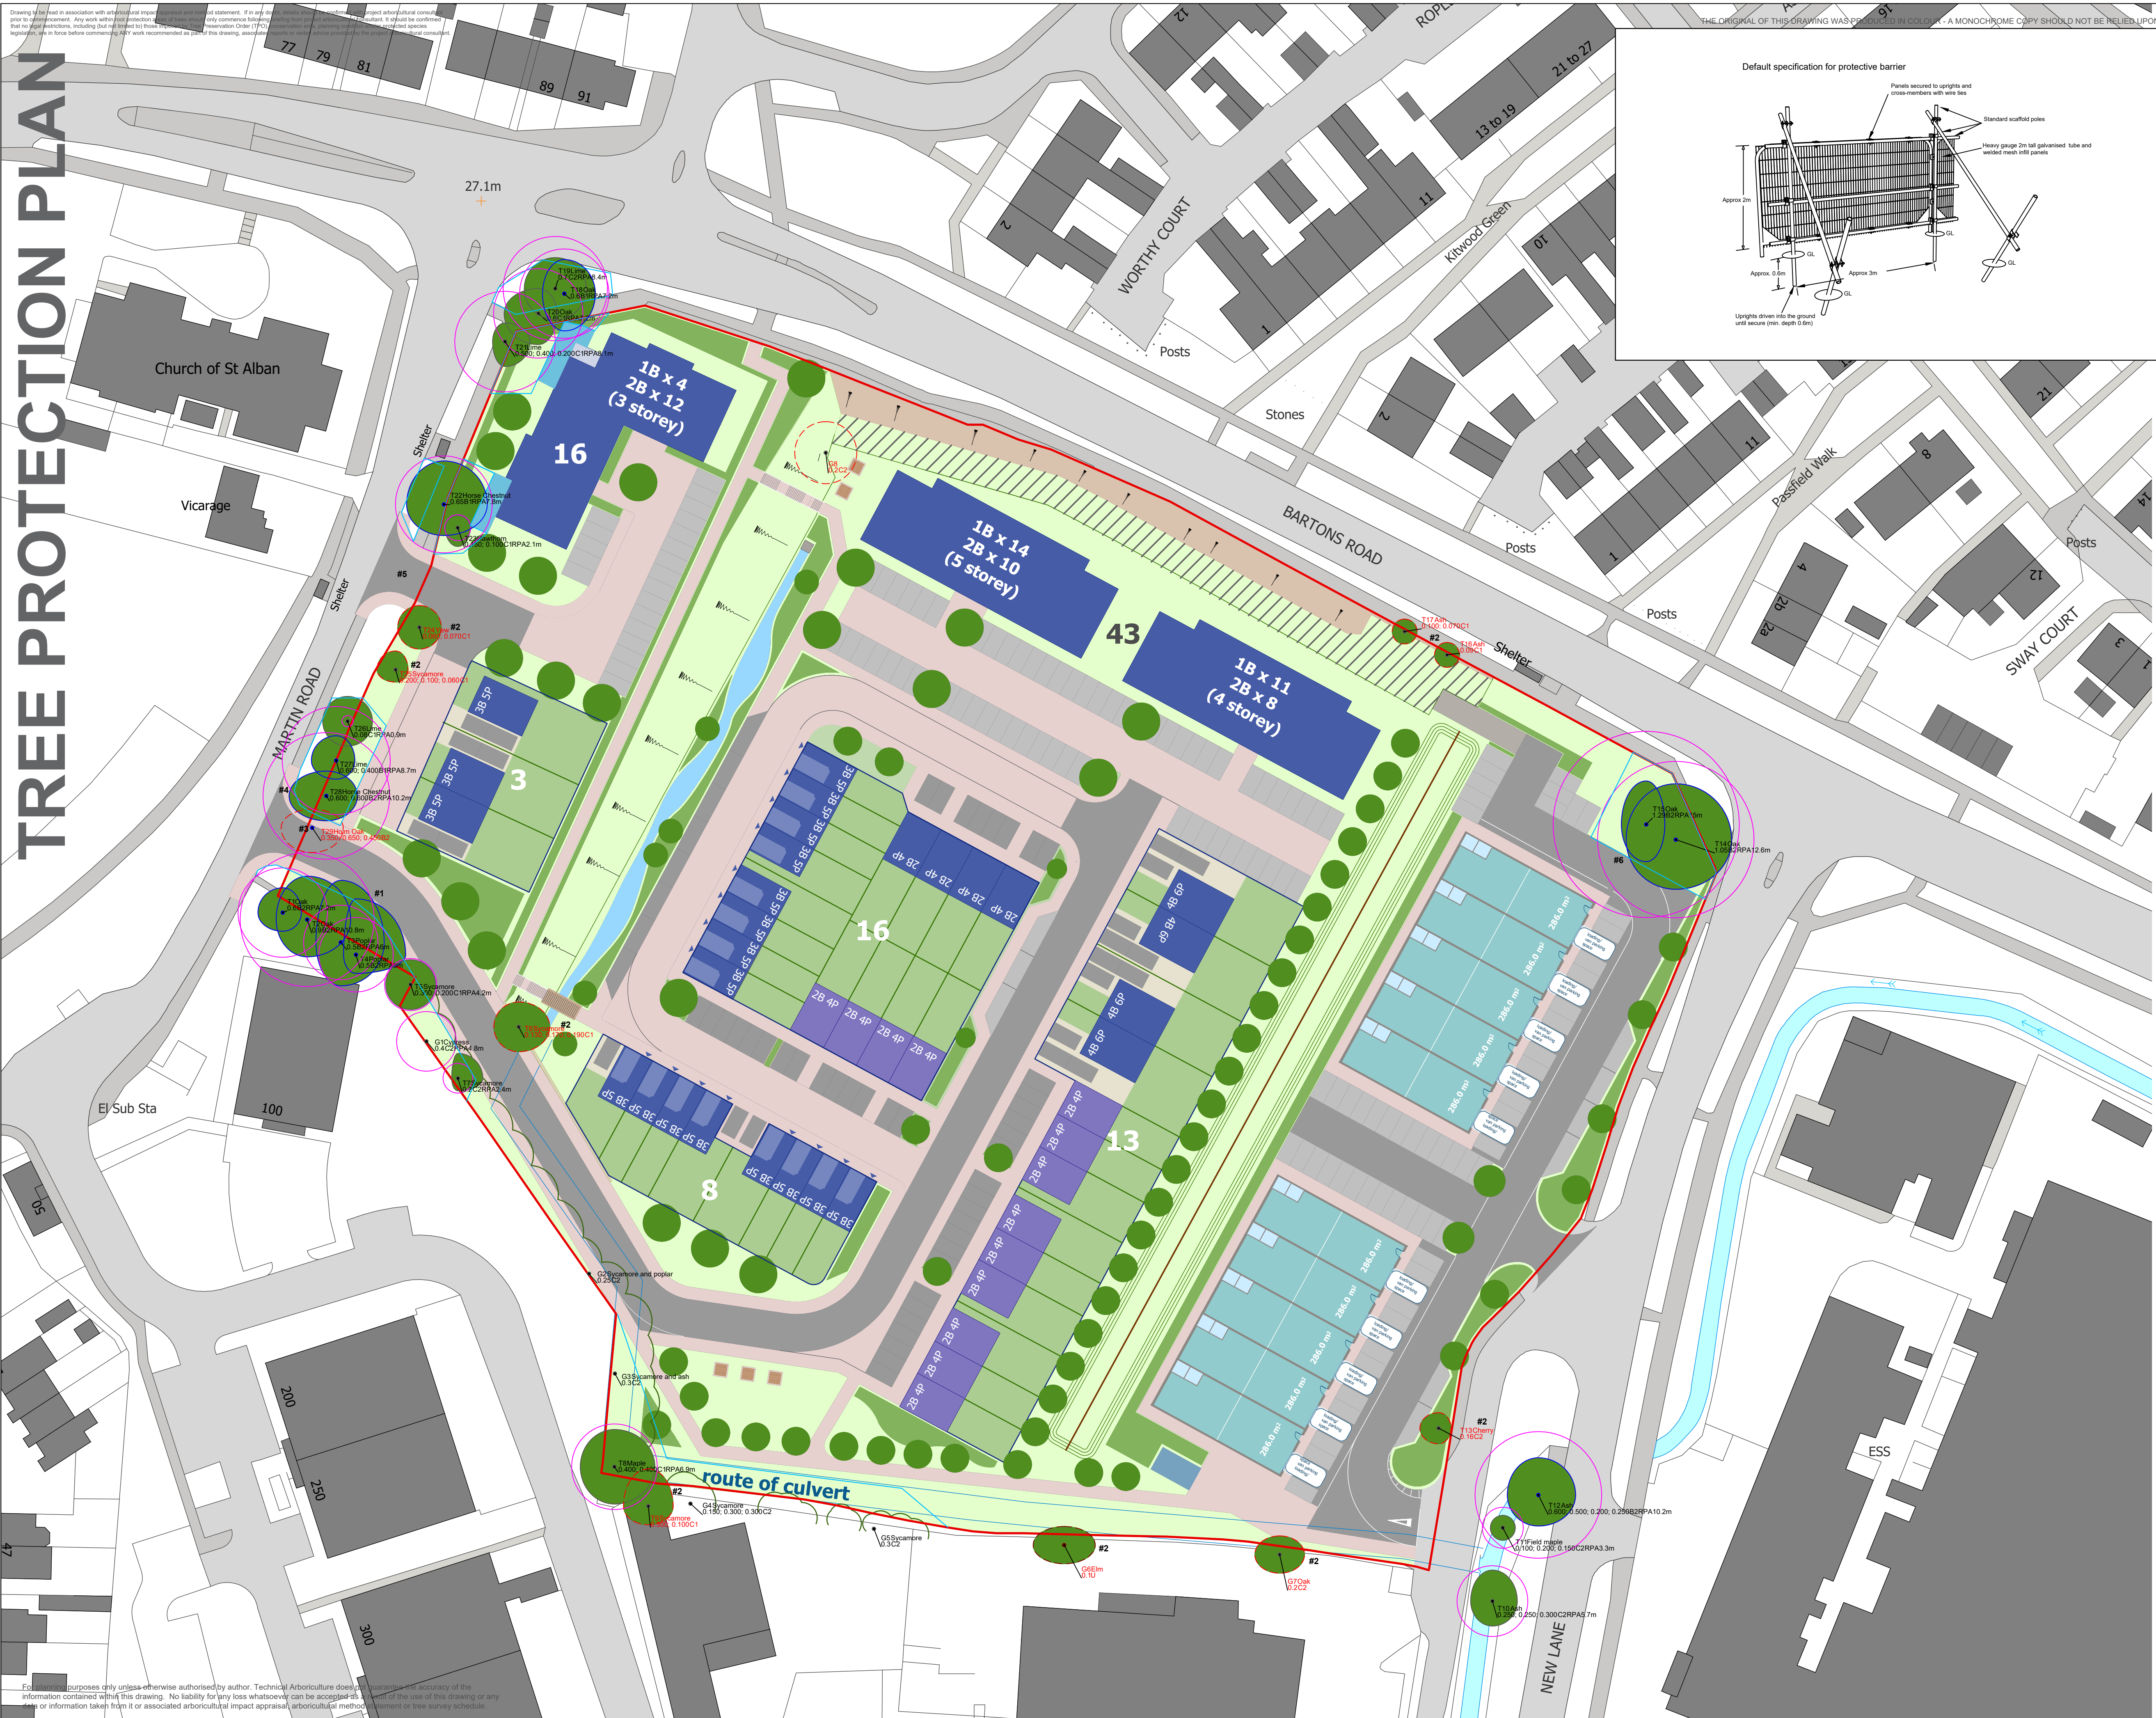

**TREE PROTECTION AREA
KEEP OUT!**

TREES ENCLOSED BY THIS FENCE ARE PROTECTED
BY PLANNING CONDITIONS AND/OR ARE THE
SUBJECT OF ATREE PRESERVATION ORDER.
CONTRAVENTION OF A TREE PRESERVATION ORDER
MAY LEAD TO CRIMINAL PROSECUTION
THIS FENCING MUST NOT BE REMOVED WITHOUT
PERMISSION FROM THE TREE AND LANDSCAPE
OFFICER

ATTENTION!


TREE PROTECTION

Tree protection comprises two elements;

1. Fencing AND;
2. ground protection

Do not assume that because you are outside the fence you are outside the RPA.

Legend

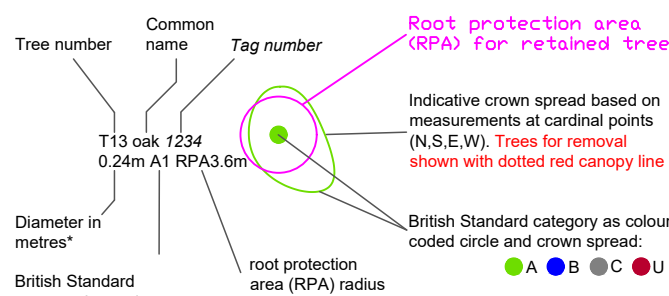

*where the tree is multi stemmed, the figure stated is the calculated combined stem diameter, as recommended by BS5837:2012 (unless otherwise stated in the drawing).

 Protective fencing to BS5837:2012. Refer to BS5837 figure 2 and figure 3 as appropriate.

Space restrictions will require ground protection capable of supporting the level of construction traffic entering the area (refer to guidance in text box within drawing). Refer to relevant sections of arboricultural impact appraisal and methodology statement.

Indicative location and suggested species of new semi mature tree. Crown spread shown as estimated after 25 years (data from Hillier's design guide)

Ground protection specification for different levels of construction traffic (after BS587:2012):

- Pedestrian movements - scaffold boards placed either on top of a driven scaffold frame to form a suspended walkway; or on top of a compression resistant layer of 100 mm depth of woodchip, laid onto a geotextile membrane;
- Plant (pedestrian operated up to 2 t gross weight) - proprietary, inter linked, round protection boards placed onto a compression resistant layer of 150 mm depth of woodchip, laid onto a geotextile membrane;
- Construction traffic (wheeled or tracked exceeding 2 t gross weight) - an alternative system (e.g. proprietary systems or pre cast reinforced concrete slabs) to a design engineering specification designed in conjunction with the project architectural consultant, to accommodate the expected loading.

Drawing notes

#1 - refer to paragraph 30 of arboricultural impact appraisal
#2 - refer to paragraph 39 of arboricultural impact appraisal
#3 - refer to paragraph 40 of arboricultural impact appraisal
#4 - refer to paragraph 31 of arboricultural impact appraisal
#5 - refer to paragraph 32 of arboricultural impact appraisal
#6 - refer to paragraph 33 of arboricultural impact appraisal

**Technical
Arboriculture**
www.techarb.co.uk

Technical Arboriculture Limited
1 Chase Farm Close
Waltham Chase
Hampshire
SO32 2UB
09 896 655 info@techarb.co.uk

PROJECT	Former Colt International site, New Lane, Havant
DATE	March 2018
JOB REF	A/A/AMS-KC/HCA/COLTS/001 TSP-KC/HCA/
DRAWING NO	COLTS/001 KC
DRAWN	1:500 at A1
SCALE	FINAL
STATUS	0
REVISION	

REVISION NOTES



TREE PROTECTION PLAN
