

#### GENERAL CONSIDERATIONS WITHIN AND OUTSIDE OF THE CONSTRUCTION EXCLUSION ZONE

1.1 The protective fencing is to be erected in accordance with the location set out on plan and will be erected prior to any site works or compound clearance works.

1.2 Once the fencing is in place it must remain in situ throughout the following list:

- Contractor occupancy
- Plant and materials delivery
- Demolition and clearance works
- Construction works
- Installation of impermeable surfacing
- Utility installation
- Completion of development

1.3 The area within the Construction Exclusion Zone (CEZ) is to be regarded as sacrosanct, and the tree protective fencing should not be taken down or relocated at any time, without the written approval of the Local Planning Authority (LPA).

1.4 In order to inform site personnel of the purpose of the fencing, information notices shall be fixed to the fencing at 5 metre intervals. These notices shall be of all-weather construction and shall be replaced as and when necessary.

## 2.0 PROHIBITIONS ADJACENT TO TREES:

2.1 Inside the Construction Exclusion Zone (CEZ) of the protective fencing the following prohibitions shall apply:

- No mechanical digging or scraping
- No hand digging
- No storage of plant, equipment or materials
- No vehicular or plant access
- No fire lighting
- No washing down of vehicles or machinery
- No handling, discharge or spillage of any chemical substance, including cement washings
- No action likely to cause localised water-logging
- No change in ground levels
- No construction of a hard surface
- No outworks.

2.2 In addition to the above, further precautions are necessary adjacent to trees outside CEZ:


Materials which will contaminate the soil, e.g. concrete mixing, diesel oil and vehicle washings should not be discharged within 10m of the tree stem. This should take into consideration the topography of the site and slopes, to avoid materials such as concrete washings running towards trees.

Fires should not be lit in a position where their flames can extend to within 5 metres of foliage, branches or trunk. This will depend on the size of the fire and the wind directions.


Stove boards, telephone cables or other services should not be attached to any part of the tree.

FIGURE 1: TREE PROTECTION FENCE


1. Standard scaffold poles
2. Uprights to be driven into the ground by 600mm
3. Panels secured to uprights with wire ties and where necessary standard scaffold clamps
4. Weldmesh wired to the uprights and horizontals
5. Standard clamps
6. Wire twisted and secured on inside face of fencing to avoid easy dismantling
7. Ground level

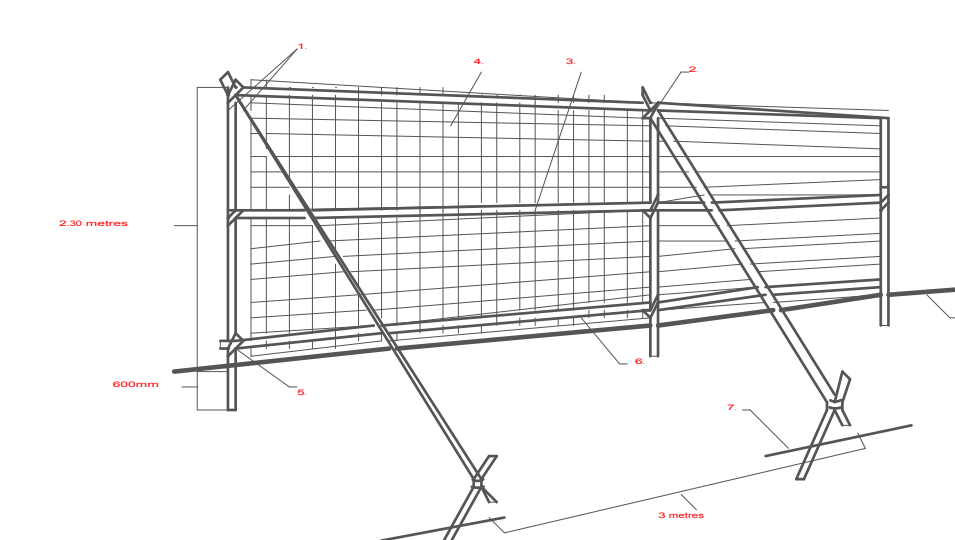

= Tree protection fence (as per figure 1 above)  
To surround the Construction Exclusion Zone (CEZ).



<sup>a</sup> Construction Exclusion Zone (CEZ)



|                                                                                                                                                                                                                                                                                                       |                              |             |          |
|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------|-------------|----------|
| <h1 style="text-align: center;">TAYLOR TRIPP LTD</h1> <h2 style="text-align: center;">LANDSCAPE DESIGN</h2> <p style="text-align: center;">5 City Road<br/>Winchester<br/>Hampshire<br/>SO23 8SD</p> <p style="text-align: center;">Telephone: 01962 793500<br/>www.taylortripp.co.uk</p>             |                              |             |          |
| CLIENT:                                                                                                                                                                                                                                                                                               | Mr & Mrs D Holland           |             |          |
| PROJECT:                                                                                                                                                                                                                                                                                              | Tideclids                    |             |          |
| TITLE:                                                                                                                                                                                                                                                                                                | Tree Protection Plan         |             |          |
| PLAN CODE:                                                                                                                                                                                                                                                                                            | 14.HOL_501                   | CHECKED BY: | NT       |
| SCALE:                                                                                                                                                                                                                                                                                                | 1:200 Printed at A0 portrait |             |          |
| COPYRIGHT:                                                                                                                                                                                                                                                                                            | Taylor Tripp Ltd             |             |          |
| <p><small>This is a non-replicable property. It is not recommended that you scale from this drawing. Being sent to digital and hard copy as separate files. All drawings are to be checked on site before contract. All discrepancies to be reported immediately to the client on design.</small></p> |                              |             |          |
| DRAWN BY:                                                                                                                                                                                                                                                                                             | G Green                      | DATE:       | 20.03.14 |
