

BREEAM NC 2018 Assessment Tracker


Waterloo Park, Waterlooville

27/06/2025

This report tracks the development's progress toward achieving a BREEAM V6 New Construction rating of **Very Good**.

This requires an overall score of **55%** to be achieved in addition to the mandatory criteria.

The development is being assessed under **Retail- Shell Only**

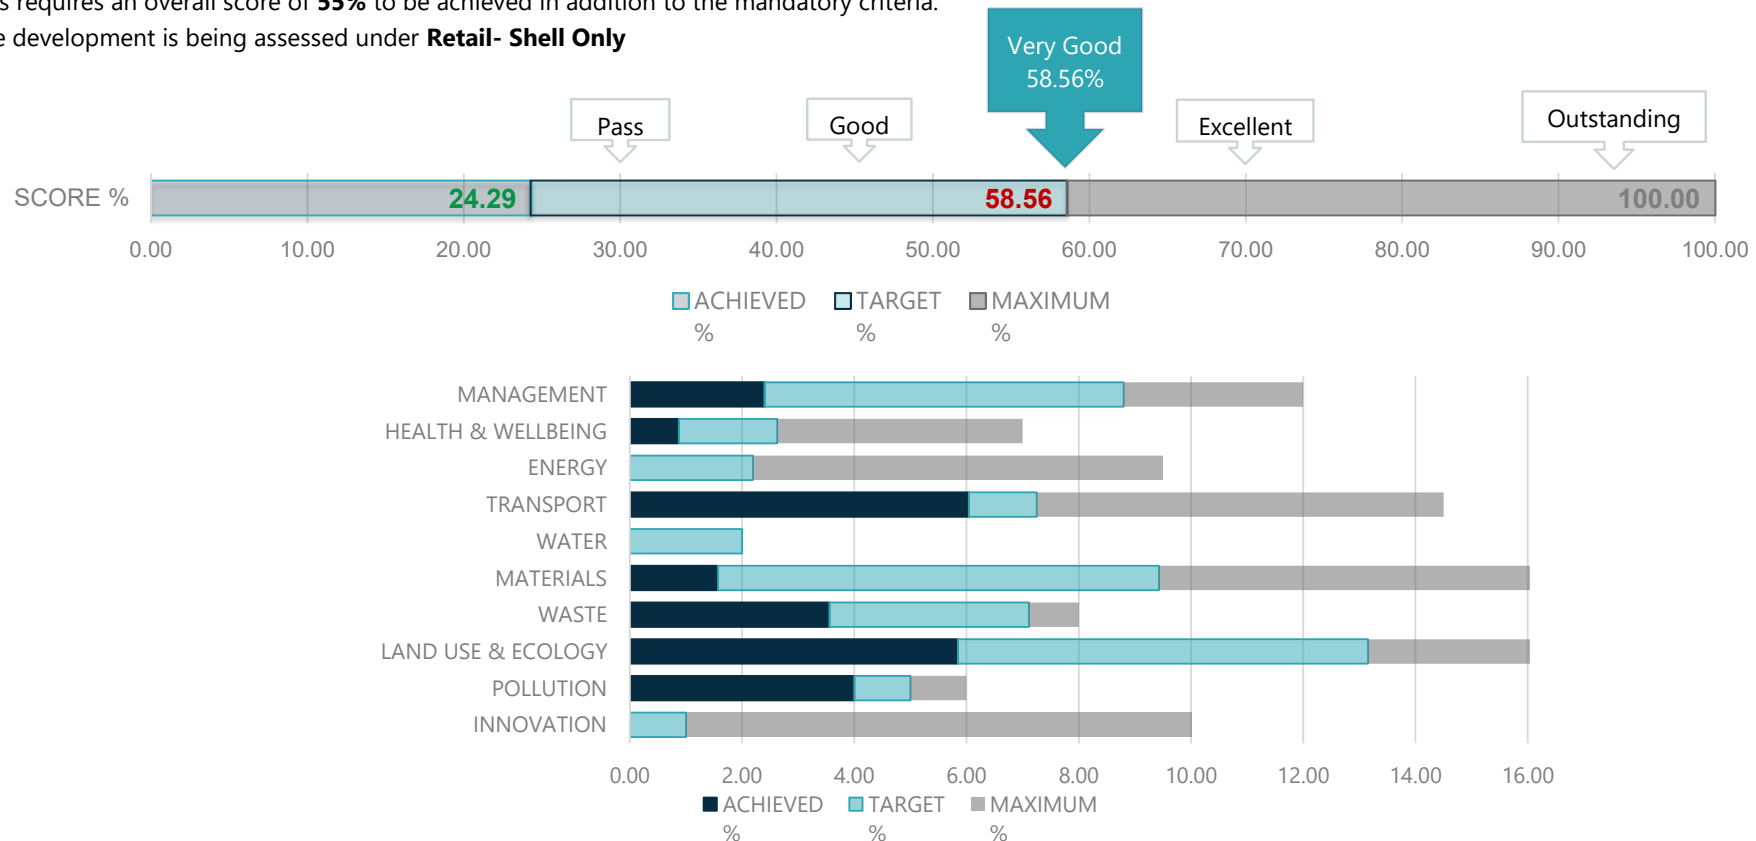

BREEAM NC V6 Assessment Tracker

Waterloo Park, Waterlooville

Management		Available	Target	Achieved
Man 01	Project Brief & Design	4	3	3
Man 02	Life Cycle Cost & Service Life Planning	4	2	0
Man 03	Responsible Construction Practices	6	6	0
Man 04	Commissioning & Handover	1	0	0
Section Total		15	11	3
Section Score %		12.00	8.80	2.40
Single Credit Value %		0.80		

Health & Wellbeing		Available	Target	Achieved
Hea 01	Visual Comfort	4	1	0
Hea 02	Indoor Air Quality	0	0	0
Hea 05	Acoustic Performance	1	1	0
Hea 06	Security	1	0	0
Hea 07	Safe & Healthy Surroundings	2	1	1
Section Total		8	3	1
Section Score %		7.00	2.63	0.88
Single Credit Value %		0.88		

Energy		Available	Target	Achieved
Ene 01	Reduction of Energy Use & Carbon Emissions	9	2	0
Ene 03	External Lighting	1	1	0
Ene 04	Low Carbon Design	3	0	0
Section Total		13	3	0
Section Score %		9.50	2.19	0.00
Single Credit Value %		0.73		

Transport		Available	Target	Achieved
Tra 01	Transport Assessment & Travel Plan	2	2	2
Tra 02	Sustainable Transport Measures	10	4	3
Section Total		12	6	5
Section Score %		14.50	7.25	6.04
Single Credit Value %		1.21		

Water		Available	Target	Achieved
Wat 02	Water Monitoring	1	1	0
Wat 03	Water Leak Detection & Prevention	1	1	0
Section Total		2	2	0
Section Score %		2.00	2.00	0.00
Single Credit Value %		1.00		

27/06/2025

Materials		Available	Target	Achieved
Mat 01	Building Life Cycle Assessment	7	1	0
Mat 02	Environmental Product Declarations	1	0	0
Mat 03	Responsible Sourcing of Construction Products	4	3	1
Mat 05	Designing for Durability & Resilience	1	1	0
Mat 06	Material Efficiency	1	1	0
Section Total		14	6	1
Section Score %		22.00	9.43	1.57
Single Credit Value %		1.57		

Waste		AVAILABLE	TARGET	ACHIEVED
Wst 01	Construction Waste Management	4	4	0
Wst 02	Use of Recycled & Sustainably Sourced Aggregates	1	0	0
Wst 03	Operational Waste	1	1	1
Wst 05	Adaptation to Climate Change	1	1	1
Wst 06	Functional Adaptability	2	2	2
Section Total		9	8	4
Section Score %		8.00	7.11	3.56
Single Credit Value %		0.89		

Land Use & Ecology		Available	Target	Achieved
Le 01	Site Selection	2	1	1
Le 02	Identifying & Understanding the Risks& Opportunities for the Project	2	2	2
Le 03	Managing Negative Impacts on Ecology	3	2	0
Le 04	Change & Enhancement of Ecological Value	4	2	1
Le 05	Long Term Ecology Management & Maintenance	2	2	0
Section Total		13	9	4
Section Score %		19.00	13.15	5.85
Single Credit Value %		1.46		

Pollution		Available	Target	Achieved
Pol 03	Flood & Surface Water Management	5	4	4
Pol 04	Reduction of Night Time Light Pollution	1	1	0
Section Total		6	5	4
Section Score %		6.00	5.00	4.00
Single Credit Value %		1.00		

Innovation		Available	Target	Achieved
Exemplary Performance		10	1	0
Section Total		10	1	0
Section Score %		10.00	1.00	0.00
Single Credit Value %		1.00		


Target Score %	58.56
Target Rating	VERY GOOD

Achieved Score %	24.29
Achieved Rating	UNCLASSIFIED

BREEAM NC V6 Assessment Tracker

Waterloo Park, Waterlooville

27/06/2025



Management				⌚	Responsibility	Available	Target	Achieved	Comments
Man 01	Project Brief & Design	Project Delivery Planning Define key roles, responsibilities & contributions for each key phase of the project.			Design Team	1	1	1	Project Execution Plan received Planning Trackers received Directory received
		Stakeholder Consultation (Interested Parties) Consult all interested parties & demonstrate their contributions including how their feedback has influenced the design.			Design Team	1	0	0	
		Formally Agree Strategic Performance Targets			Design Team	P	P	P	BREEAM Very Good target stated in formal documents
		BREEAM Advisory Professional (Concept Design) Appoint a BREEAM AP to work with the design team to establish targets, monitor progress & identify project risks.			Design Team	1	1	1	ESC appointed and have undertaken advisory role throughout Concept Design Stage
		BREEAM Advisory Professional (Developed Design) The BREEAM AP should review progress and assist in maximising the project's overall performance.			Design Team	1	1	1	ESC appointed and have undertaken advisory role throughout Developed Design Stage
Man 02	Life Cycle Cost & Service Life Planning	Elemental Life Cycle Cost Undertake an entire asset LCC plan.			Specialist	2	0	0	
		Component Level LCC Options Appraisal Undertake a component level LCC options appraisal.			Specialist	1	1	0	
		Capital Cost Reporting Report the project cost in £ per square meter of gross internal area.			Main Contractor	1	1	0	
Man 03	Responsible Construction Practices	Legally Harvested & Traded Timber All site timber & timber-based products are legally harvested & traded timber.			Main Contractor	P	P	0	
		Environmental Management All parties who manage the construction site operate an Environmental Management System.			Main Contractor	1	1	0	
		Formally Agree Strategic Performance Targets			Main Contractor	P	P	0	
		BREEAM Advisory Professional (Site) Appoint a BREEAM AP to work with the project team to establish targets, monitor progress & identify project risks.			Main Contractor	1	1	0	
		Responsible Construction Management The principal contractor evaluates the risks (on site & off site), plans & implements actions to minimise the identified risks.			Main Contractor	2	2	0	

BREEAM NC V6 Assessment Tracker

Waterloo Park, Waterloooville

27/06/2025

		Utility Consumption Set targets for site energy & water consumption, monitor & record data.		Main Contractor	1	1	0	
		Transportation of Construction Materials & Waste Set targets for transportation of materials to site & waste from site, monitor & record data.		Main Contractor	1	1	0	
Man 04	Commissioning & Handover	Testing & Inspection Building Fabric Undertake an air tightness test & thermographic survey & rectify any defects.		Main Contractor	1	0	0	
Section Total					15	11	3	
Section Score %					12.00	8.80	2.40	
Single Credit Value %					0.80			

BREEAM NC V6 Assessment Tracker

Waterloo Park, Waterlooville

27/06/2025

Health & Wellbeing			🕒	Responsibility	Available	Target	Achieved	Comments
Hea 01	Visual Comfort	Daylighting Undertake daylighting calculations.		Architect	2	0	0	
		View Out Maximise view out through layout and window design.		Architect	1	0	0	
		External Lighting Levels, Zoning & Controls Specify efficient lighting & design for occupant wellbeing using zones and controls.		Electrical Contractor	1	1	0	
Hea 05	Acoustic Performance	Indoor Ambient Noise Level The building meets the appropriate acoustic performance standards & testing requirements.		Acoustician	1	1	0	
Hea 06	Security	Security of Site & Building Appoint a specialist to undertake a Security Needs Assessment & implement the recommended security measures.		Specialist	1	0	0	
Hea 07	Safe & Healthy Surroundings	Safe Access Design the site to allow safe access for all building users.		Architect	1	1	1	Site layout received showing access strategy to each building
		Outdoor Space Provide a suitable outdoor space for building users.		Architect	1	0	0	
Section Total					8	3	1	
Section Score %					7.00	2.63	0.88	
Single Credit Value %					0.88			

BREEAM NC V6 Assessment Tracker

Waterloo Park, Waterloooville

27/06/2025

Energy			🕒	Responsibility	Available	Target	Achieved	Comments
Ene 01	Reduction of Energy Use & Carbon Emissions	Energy Performance Calculate an Energy Performance Ratio for New Construction (EPR NC).		Mechanical Contractor	9	2	0	
Ene 03	External Lighting	External Lighting Install energy efficient external light fittings & controls.		Electrical Contractor	1	1	0	
Ene 04	Low Carbon Design	Passive Design Analysis Undertake an analysis of passive design measures to reduce energy use.		Mechanical Consultant	1	0	0	
		Free Cooling Undertake a free cooling analysis & implement a free cooling solution.		Mechanical Consultant	1	0	0	
		Low & Zero Carbon Technologies Undertake a review of all available LZC technologies & achieve a significant reduction in carbon emissions.		Mechanical Consultant	1	0	0	
Section Total					13	3	0	
Section Score %					9.50	2.19	0.00	
Single Credit Value %					0.73			

BREEAM NC V6 Assessment Tracker

Waterloo Park, Waterloooville

27/06/2025

Transport			⌚	Responsibility	Available	Target	Achieved	Comments
Tra 01	Transport Assessment & Travel Plan	Travel Plan Undertake a site-specific travel assessment & travel plan.		Transport Consultant	2	2	2	Updated documents received
Tra 02	Sustainable Transport Measures	Transport Options Implementation Implement sustainable transport measures. - Car share 5% - EV charging 10% - Cycle storage - Cycle facilities		Design Team	10	4	3	Drawing received demonstrating the incorporation of transport measures
Section Total					12	6	5	
Section Score %					14.50	7.25	6.04	
Single Credit Value %					1.21			

BREEAM NC V6 Assessment Tracker

Waterloo Park, Waterloooville

27/06/2025

Water			🕒	Responsibility	Available	Target	Achieved	Comments
Wat 02	Water Monitoring	Water Monitoring Specify a pulsed output water meter on the mains water supply to each building.		Mechanical Contractor	1	1	0	
Wat 03	Water Leak Detection & Prevention	Leak Detection System Install a leak detection system capable of detecting a major water leak within the building & between the building & utilities meter.		Mechanical Contractor	1	1	0	
Section Total					2	2	0	
Section Score %					2.00	2.00	0.00	
Single Credit Value %					1.00			

BREEAM NC V6 Assessment Tracker

Waterloo Park, Waterloooville

27/06/2025

Materials			⌚	Responsibility	Available	Target	Achieved	Comments
Mat 01	Building Life Cycle Assessment	Superstructure Carry out an LCA on the building's superstructure & an options appraisal.		ESC	6	1	0	
		Substructure & Hard Landscaping Options Appraisal Carry out a LCA options appraisal for the substructure & hard landscaping.		Design Team	1	0	0	
Mat 02	Environmental Product Declarations	Specification of products with a recognised environmental product declaration (EPD)		Main Contractor	1	0	0	
Mat 03	Responsible Sourcing of Construction Products	Legally Harvested & Traded Timber All construction timber & timber-based products are legally harvested & traded timber.		Main Contractor	P	P	0	
		Enabling Sustainable Procurement A sustainable procurement plan must be used by the design team to guide specification towards sustainable construction products.		Design Team	1	1	1	Sustainable Procurement Plan received
		Measuring Responsible Sourcing Use materials with a certified supply chain process.		Main Contractor	3	2	0	
Mat 05	Designing for Durability & Resilience	Protect Vulnerable & Exposed Elements from Damage & Degradation Incorporate protection measures to reduce damage to the building's fabric or materials & design building elements to limit long and short term degradation due to environmental factors.		Architect	1	1	0	Durability and Resilience Assessment received
Mat 06	Material Efficiency	Minimise Environmental Impact of Materials Set targets and report on opportunities and methods to optimise the use of materials.		Design Team	1	1	0	Concept Design Stage report received
Section Total					14	6	1	
Section Score %					22.00	9.43	1.57	
Single Credit Value %					1.57			

BREEAM NC V6 Assessment Tracker

Waterloo Park, Waterlooville

27/06/2025

Waste			🕒	Responsibility	Available	Target	Achieved	Comments
Wst 01	Construction Waste Management	Pre-Demolition Audit Produce a pre-demoliton audit of any existing buildings, structures or hard surfaces being considered for demolition		Demoliton Contractor	1	1	0	Required prior to start on site
		Construction Resource Efficiency Produce a compliant Resource Management Plan & meet the waste benchmarks.		Main Contractor	3	3	0	
		Diversion of Resources from Landfill Meet the diversion from landfill benchmarks & sort waste into key waste groups.		Main Contractor	1	1	0	
Wst 02	Use of Recycled & Sustainably Sourced Aggregates	Project Sustainable Aggregate Points Identify all aggregate uses & types on the project & use sustainable aggregate.		Main Contractor	1	0	0	Potential credit to target - to be agreed with Contractor
Wst 03	Operational Waste	Operational Waste Provide a dedicated space for the segregation and storage of operational recyclable waste generated.		Architect	1	1	1	Letter received Drawings of operational waste storage received. Sizes of stores confirmed.
Wst 05	Adaptation to Climate Change	Resilience of Structure, Fabric, Building Services & Renewables Installation Conduct a climate change adaptation strategy appraisal.		Design Team	1	1	1	Concept Stage report received Information of flooding and drainage received. ESC to provide all implementation evidence for submission
Wst 06	Functional Adaptability	Design for Disassembly & Functional Adaptability - Recommendations Conduct a study to explore the ease of disassembly & the functional adaptation potential of different design scenarios.		Design Team	1	1	1	Concept stage report received
		Design for Disassembly & Functional Adaptability - Implementation Implement solutions where practical & justify any omissions.		Design Team	1	1	1	Revised update received from HNW to confirm implementation of measures
Section Total					10	9	4	
Section Score %					8.00	7.20	3.20	
Single Credit Value %					0.80			

BREEAM NC V6 Assessment Tracker

Waterloo Park, Waterlooville

27/06/2025

Land Use & Ecology			🕒	Responsibility	Available	Target	Achieved	Comments
Le 01	Site Selection	Previously Occupied Land At least 75% of the proposed development's footprint is on an area of land which has previously been occupied.		Architect	1	1	1	Drawing received showing the existing and proposed site. Circa 100% of the land is considered previously occupied.
		Contaminated Land Where contaminated, land is remediated.		Specialist	1	0	0	
Le 02	Identifying & Understanding the Risks & Opportunities for the Project	Assessment Route Selection Appoint an Ecologist where required & comply with all relevant UK & EU legislation.		Design Team	P	P	P	
		Survey & Evaluation An SQE undertakes a survey & evaluation to determine the ecological baseline.		Ecologist	1	1	1	Preliminary Ecology Appraisal received
		Determining the Ecological Outcomes for the Site The optimal ecological outcome for the site is selected using the hierarchy of action.		Ecologist	1	1	1	GN40 Ecologist Report received
Le 03	Managing Negative Impacts on Ecology	Le 02 - Identification & Understanding the Risks & Opportunities of the Site		Design Team	P	P	P	
		Planning, Liaison, Implementation & Data The potential impact of site preparation & construction works on ecology are identified.		Design Team	1	1	0	
		Managing Negative Impacts of the Project Negative impacts are managed to reduce loss of ecological value.		Ecologist	2	1	0	
Le 04	Change & Enhancement of Ecological Value	Le 03 - Managing Negative Impacts on Ecology		Design Team	P	P	P	
		Liaison, Implementation & Data Collection Implement ecological enhancement measures either on or off site.		Design Team	1	1	0	
		Enhancement of Ecology Calculation of the site's final ecological value.		Ecologist	3	1	1	BNG assessment received - confirms -24% net gain
Le 05	Long Term Ecology Management & Maintenance	Roles & Responsibilities, Implementation, Statutory Obligations Le 03 is achieved & at least one Le 04 Enhancement of Ecology credit is achieved.		Design Team	P	P	P	
		Planning, Liaison, Data, Monitoring & Review Management & Maintenance Develop & review management & maintenance solutions, actions or measures.		Design Team	1	1	0	
		Landscape & Ecology Management Plan Development Produce a landscape & ecology management plan.		Ecologist	1	1	0	
Section Total					13	9	4	
Section Score %					19.00	13.15	5.85	
Single Credit Value %					1.46			

BREEAM NC V6 Assessment Tracker

Waterloo Park, Waterlooville

27/06/2025

Pollution			⌚	Responsibility	Available	Target	Achieved	Comments
Pol 03	Flood & Surface Water Management	Appropriate Consultant		Civil Engineer	P	P	P	
		Flood Resilience Produce a flood risk assessment that considers all sources of flooding.		Civil Engineer	2	2	2	Flood Risk Assessment received from BPC which confirms the site has low risk
		Bespoke Surface Water Run-Off Design Solutions		Civil Engineer	P	P	P	Drainage Layout received
		Surface Water Run-Off - Rate Reduce the peak rate of run-off from the site.		Civil Engineer	1	0	0	
		Surface Water Run-Off - Volume Reduce the volume of run-off from the site.		Civil Engineer	1	1	1	Completed GN38 form received
		Minimise Watercourse Pollution Prevent discharge leaving the site & minimise pollution risk using SuDS.		Civil Engineer	1	1	1	Completed GN38 form received
Pol 04	Reduction of Night Time Light Pollution	Reduction of Night Time Light Pollution Control external lighting and light spill.		Electrical Contractor	1	1	0	
Section Total					6	5	4	
Section Score %					6.00	5.00	4.00	
Single Credit Value %					1.00			

BREEAM NC V6 Assessment Tracker

Waterloo Park, Waterloooville

27/06/2025

Innovation			⌚	Responsibility	Available	Target	Achieved	Comments
Exemplary Performance	Man 03	Responsible Construction Practices - All Criteria		Main Con.	1	1	0	
	Hea 01	Visual Comfort - Daylighting		Mech. Con.	1	0	0	
	Hea 06	Security - SABRE		Architect	1	0	0	
	Ene 01	Reduction of Energy Use & Carbon Emissions		Mech. Con.	5	0	0	
	Wat 01	Water Consumption		Mech. Con.	1	0	0	
	Mat 01	Building Life Cycle Assessment		Design Team	3	0	0	
	Mat 03	Responsible Sourcing of Construction Products		Main Con.	1	0	0	
	Wst 01	Construction Waste Management		Main Con.	1	0	0	
	Wst 02	Use of Recycled & Sustainably Sourced Aggregate		Main Con.	1	0	0	
	Wst 05	Adaptation to Climate Change		Design Team	1	0	0	
	Le 02	Identifying & Understanding the Risks & Opportunities for the Project		Design Team	1	0	0	
	Le 04	Change & Enhancement of Ecological Value		Design Team	1	0	0	
	Inn	BRE Approved Innovations		Design Team	1	0	0	
	Section Total				10	1	0	
	Section Score %				10.00	1.00	0.00	
	Single Credit Value %				1.00			
