

Your ref LIV-SN-23-006703


Our ref 09542GLOB

360Globalnet Ltd
Bramley House,
Bramley Road,
Long Eaton,
NG10 3SX

Geo-Serv Limited
17 Hoveden Road
London NW2 3X

te **020 8208 034**
ema. **mon@geo-serv.co**

**Subsidence
Monitoring
Service**



GEO-SERV

Issue date: 27/03/2025

Monitoring visit **8** of **8**

Monitoring Plus Report

Owners name	Mrs. Hayley Psaila	Suspected cause	to be advised	Monitoring type	levels & cracks	
Address	28 Damask Gardens Waterlooville Waterlooville PO7 8QZ	Principal area of damage	to be advised	Installed	03/08/2023	
		Damage category	to be advised	Frequency (weeks)	8.7	
		Surface geology	to be advised	Completion date		
				Status	completed	
Comment	Feedback from last visit					
Max movement 8.1 mm	no feedback for this visit					
Focal area Pts 8,						
27/03/2025- Instructed visits completed		Sketch showing location of monitoring points				

Crack monitoring results

Survey: By: Date:		1 VV 03/08/2023		2 VV 25/10/2023		3 VV 15/02/2024		4 Vanya 16/05/2024		5 Vanya 25/07/2024		
Crack ID	initial width mm	sprtn mm	chngs mm	sprtn mm	chngs mm	sprtn mm	chngs mm	sprtn mm	chngs mm	levels mm	chngs mm	
A (horiz)	0.47	46.78	0.0	46.88	0.1	46.86	0.1	46.94	0.2	46.86	0.1	
A (diag)		66.92	0.0	66.92	0.0	66.88	0.0	66.77	-0.2	66.98	0.1	
A (check)		46.23	0.0	46.18	0.0	46.13	-0.1	46.19	0.0	46.20	0.0	
B (horiz)		11.39	68.43	0.0	68.24	-0.2	68.06	-0.4	68.01	-0.4	68.06	-0.4
B (diag)			93.24	0.0	93.24	0.0	92.97	-0.3	92.78	-0.5	92.98	-0.3
B (check)			50.87	0.0	50.92	0.1	50.86	0.0	50.79	-0.1	50.90	0.0

all measurements made with internal jaws unless marked with asterisk, ^ = angle bracket, \$ = measurement with butt end of calipers


crack descriptions

A (horiz) Demec triplet, internal, above of extension door
 B (horiz) Demec triplet, nternal, rhs corner of extension

Survey: By: Date:		6 Vanya 17/10/2024		7 Simon 23/01/2025		8 Vanya 27/03/2025		9 #N/A		10 #N/A	
Crack ID	initial width mm	sprtn mm	chngs mm	sprtn mm	chngs mm	sprtn mm	chngs mm	sprtn mm	chngs mm	levels mm	chngs mm
A (horiz)	0.5	46.92	0.1	46.94	0.2	46.99	0.2		#N/A		#N/A
A (diag)		66.91	0.0	66.97	0.0	67.05	0.1		#N/A		#N/A
A (check)		46.16	-0.1	46.16	-0.1	46.19	0.0		#N/A		#N/A
B (horiz)		68.01	-0.4	67.95	-0.5	68.06	-0.4		#N/A		#N/A
B (diag)		92.77	-0.5	92.84	-0.4	92.84	-0.4		#N/A		#N/A
B (check)		50.84	0.0	50.82	0.0	50.92	0.1		#N/A		#N/A

all measurements made with internal jaws unless marked with asterisk, ^ = angle bracket, \$ = measurement with butt end of calipers

Crack monitoring

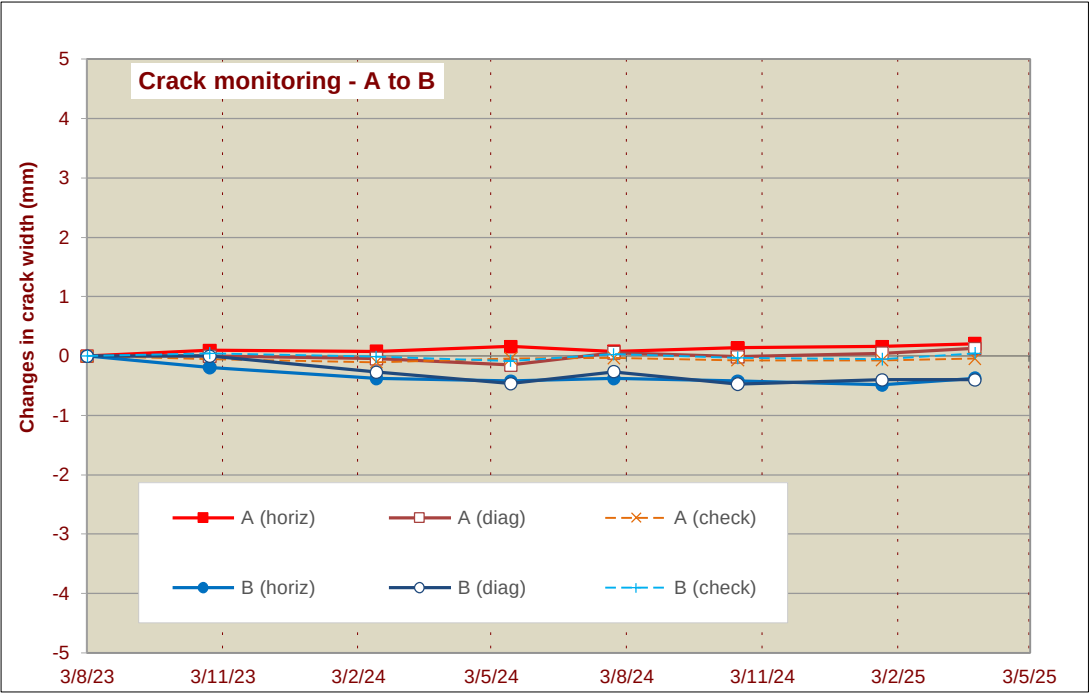

Level Monitoring Results


Survey:	1 VV		2 VV		3 VV		4 Vanya		5 Vanya	
By:	VV		VV		VV		Vanya		Vanya	
Date:	03/08/2023		25/10/2023		15/02/2024		16/05/2024		25/07/2024	
Point ID	levels mm	chngs mm	levels mm	chngs mm	levels mm	chngs mm	levels mm	chngs mm	levels mm	chngs mm
1	1000.00	0.0	1000.00	0.0	1000.00	0.0	1000.00	0.0	1000.00	0.0
2	996.10	0.0	998.18	2.1	997.80	1.7	998.34	2.2	998.09	2.0
3	1228.59	0.0	1230.20	1.6	1228.52	-0.1	1229.04	0.5	1228.86	0.3
4	1220.43	0.0	1222.04	1.6	1222.20	1.8	1222.62	2.2	1222.47	2.0
5	1218.84	0.0	1220.08	1.2	1218.80	0.0	1219.13	0.3	1219.13	0.3
6	1203.65	0.0	1205.32	1.7	1205.47	1.8	1205.78	2.1	1205.92	2.3
7	780.37	0.0	781.35	1.0	780.94	0.6	781.98	1.6	782.14	1.8
8	689.69	0.0	691.82	2.1	696.71	7.0	697.78	8.1	697.35	7.7

closing error (mm) 0.05 0.00 0.00 0.00 0.00

Survey:	6 Vanya		7 Simon		8 Vanya		9		10	
By:	Vanya		Simon		Vanya		#N/A		#N/A	
Date:	17/10/2024		23/01/2025		27/03/2025		#N/A		#N/A	
Point ID	levels mm	chngs mm	levels mm	chngs mm	levels mm	chngs mm	levels mm	chngs mm	levels mm	chngs mm
1	1000.00	0.0	1000.00	0.0	1000.00	0.0		#N/A		#N/A
2	997.90	1.8	997.90	1.8	997.64	1.5		#N/A		#N/A
3	1228.83	0.2	1228.48	-0.1	1228.68	0.1		#N/A		#N/A
4	1222.55	2.1	1222.13	1.7	1222.37	1.9		#N/A		#N/A
5	1219.15	0.3	1218.55	-0.3	1218.95	0.1		#N/A		#N/A
6	1206.08	2.4	1205.08	1.4	1205.68	2.0		#N/A		#N/A
7	781.74	1.4	781.33	1.0	781.77	1.4		#N/A		#N/A
8	696.67	7.0	696.89	7.2	697.43	7.7		#N/A		#N/A

closing error (mm) 0.20 0.20 0.00 #REF #REF

Precise level monitoring related to Point 1

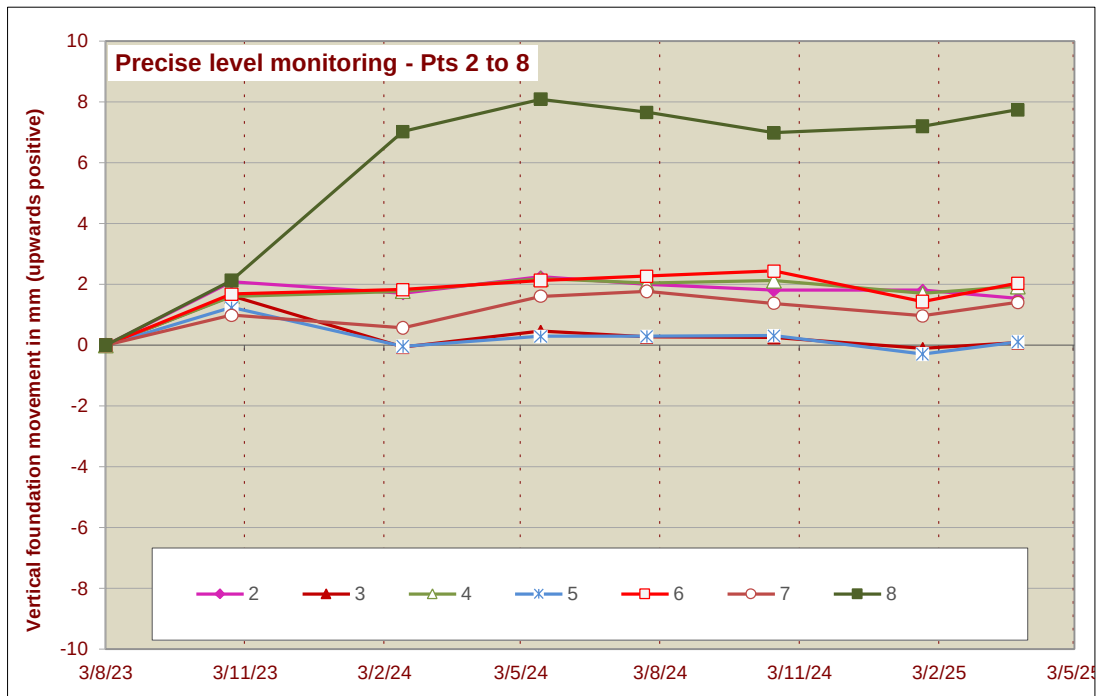

Photos from visit on 27/03/2025

