HTR - Proposed Main Embankment Planting Schedule

Condition 28 Programme

ID	Ref	Task Name	Duration	Start	Finish
1		**HTR - Wetlands Planting**	**1095 days**	**Mon 02/03/26**	**Mon 29/07/30**
2		**Key Dates & Activities**	**1087 days**	**Mon 02/03/26**	**Wed 17/07/30**
3		Earthworks Season 3 - Embankmen Above Ground:	150 days	Mon 02/03/26	Fri 02/10/26
4		Earthworks Season 4 - Embankment Above Ground:	150 days	Mon 01/03/27	Fri 01/10/27
5		Earthworks Season 5 - Embankment Above Ground:	131 days	Wed 01/03/28	Tue 05/09/28
6		Avenue Staircase and Viewing Platform	253 days	Thu 14/09/28	Tue 18/09/29
7		Tracks & Footpaths (after 4 months settlement period)	244 days	Mon 15/01/29	Mon 07/01/30
8		Soft Landscaping (inc wetlands planting)	133 days	Tue 08/01/30	Wed 17/07/30
9		**Planting Key Dates**	**225 days**	**Mon 03/09/29**	**Mon 29/07/30**
10		Planting Start	0 days	Tue 08/01/30	Tue 08/01/30
11		SOWING TIME	81 days	Mon 04/03/30	Fri 28/06/30
12		ROOTBALLED TREES - NOVEMBER TO APRIL.	120 days	Thu 01/11/29	Tue 30/04/30
13		CONIFERS/ EVERGREENS/ CONTAINERISED PLANTING - SEPTEMBER/ OCTOBER	43 days	Mon 03/09/29	Wed 31/10/29
14		CONIFERS/ EVERGREENS/ CONTAINERISED PLANTING - APRIL/ MAY	41 days	Mon 01/04/30	Fri 31/05/30
15		DECIDUOUS SHRUBS - OCTOBER TO APRIL.	127 days	Fri 19/10/29	Fri 26/04/30
16		EVERGREEN SHRUBS - SEPTEMBER / OCTOBER	43 days	Mon 03/09/29	Wed 31/10/29
17		EVERGREEN SHRUBS TO BE PLANTEDOR MARCH / MAY	62 days	Fri 01/03/30	Fri 31/05/30
18		Planting Complete	0 days	Mon 29/07/30	Mon 29/07/30
19		**Tree Planting**	**3 days**	**Thu 01/11/29**	**Mon 05/11/29**
20		Common Hornbeam - 1	1 day	Thu 01/11/29	Thu 01/11/29
21		Common Oak - 2	1 day	Fri 02/11/29	Fri 02/11/29
22		Common Lime - 1	1 day	Mon 05/11/29	Mon 05/11/29
23		**Native Hedgerow**	**9 days**	**Fri 01/03/30**	**Wed 13/03/30**
24		Common Beech - 990	9 days	Fri 01/03/30	Wed 13/03/30
25		**Planting Bed Mix**	**27 days**	**Fri 21/06/30**	**Mon 29/07/30**
26		Milfoil 'Paprikav - 601	2 days	Fri 21/06/30	Mon 24/06/30
27		Feather Reed Grass 'Karl Foerster - 901	5 days	Tue 25/06/30	Mon 01/07/30
28		Silver Dogwood - 901	5 days	Tue 02/07/30	Mon 08/07/30
29		Oregon Grape 'Apollo' - 451	2 days	Tue 09/07/30	Wed 10/07/30
30		Purple Moor Grass 'Poul Petersen - 901	5 days	Thu 11/07/30	Wed 17/07/30
31		Elder Black Lace - 226	2 days	Thu 18/07/30	Fri 19/07/30
32		Cotton Lavender - 601	3 days	Mon 22/07/30	Wed 24/07/30
33		Mexican Feather Grass - 601	3 days	Thu 25/07/30	Mon 29/07/30
34		**Native Rush & Sedge Plugs**	**249 days**	**Wed 06/09/28**	**Tue 04/09/29**
35		Lesser Pond Sedge - 55	2 days	Mon 03/09/29	Tue 04/09/29
36		Compact Rush - 109	2 days	Wed 06/09/28	Thu 07/09/28
37		Soft Rush - 82	2 days	Fri 08/09/28	Mon 11/09/28
38		Common Reed - 28	1 day	Tue 12/09/28	Tue 12/09/28
39		**Embankment Seeding**	**40 days**	**Mon 04/03/30**	**Tue 30/04/30**
40		Wildflower Seed Mix	40 days	Mon 04/03/30	Tue 30/04/30
41		Control House: Grassland creation.	1 day	Mon 04/03/30	Mon 04/03/30
42		Gipsies Plan: Grassland creation.	2 days	Tue 05/03/30	Wed 06/03/30
43		**Avenue Staircase Planting**	**10 days**	**Mon 08/10/29**	**Fri 19/10/29**
44		Avenue Staircase: Grassland creation.	1 day	Mon 08/10/29	Mon 08/10/29
45		Avenue Staircase: Tiered grass banks.	3 days	Tue 09/10/29	Thu 11/10/29
46		Avenue Staircase: Beech hedge planting.	3 days	Fri 12/10/29	Tue 16/10/29
47		Viewing Platform planting.	3 days	Wed 17/10/29	Fri 19/10/29
48		**Avenue Staircase Planting**	**13 days**	**Thu 01/11/29**	**Mon 19/11/29**
49		Viewing platform: Tree planting.	1 day	Thu 01/11/29	Thu 01/11/29
50		Viewing platform: Raised planters.	1 day	Fri 02/11/29	Fri 02/11/29
51		Viewing platform: Grassland creation.	1 day	Mon 12/11/29	Mon 12/11/29
52		Viewing platform: Planting beds.	3 days	Tue 13/11/29	Thu 15/11/29
53		Viewing platform: Reed bed planting.	2 days	Fri 16/11/29	Mon 19/11/29
54		**Embankment Slope Protection**	**534 days**	**Fri 10/07/26**	**Wed 06/09/28**
55		Place Rip-Rap Stone - 0-900	10 days	Fri 18/09/26	Thu 01/10/26
56		Place Enkamat - 0-900	60 days	Fri 10/07/26	Fri 02/10/26
57		Place Rip-Rap - Season - 29.75m	10 days	Fri 18/09/26	Thu 01/10/26
58		Place Enkamat - Season - 29.75m	52 days	Thu 14/01/27	Tue 30/03/27
59		Place Rip-Rap - Season - 36.05m	10 days	Mon 13/09/27	Fri 24/09/27
60		Place Enkamat - Season 3 - 36.05m	85 days	Fri 04/06/27	Fri 01/10/27
61		Place Rip-Rap - Season - 40.5m	10 days	Thu 03/08/28	Wed 16/08/28
62		Place Enkamat - Season - 40.5m	54 days	Fri 23/06/28	Wed 06/09/28

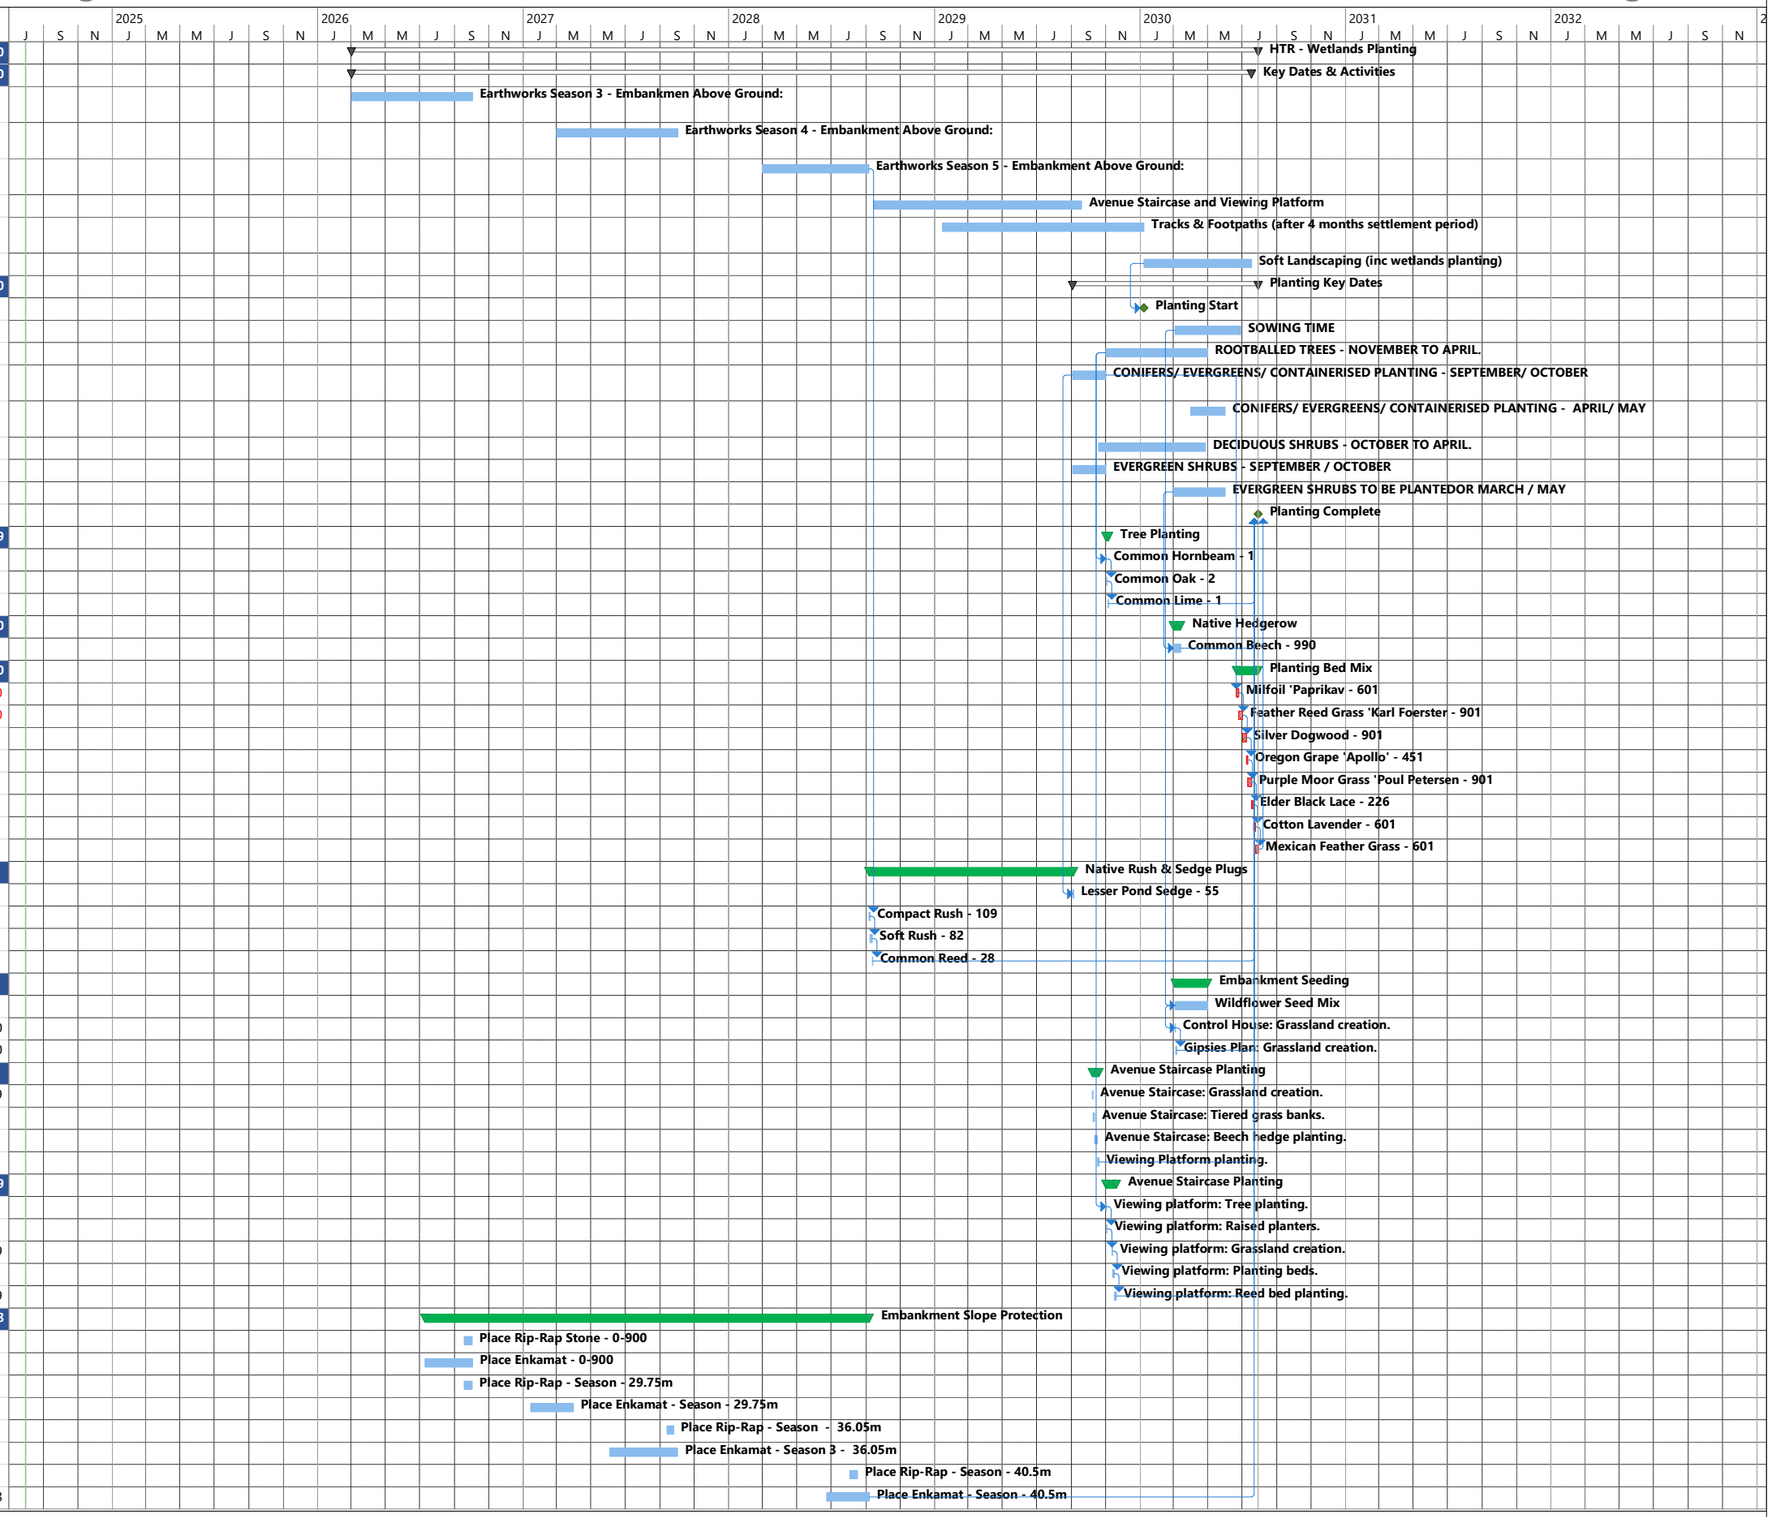

Future Water MJJV Ltd

Portsmouth Water
